

## + CURRENT CONSTRUCTION ACTIVITIES

### LAST WEEK

---

- Completed Sewer Tie-in at Spalding Dr
- Completed Paving and Temporary Striping at Spalding Dr
- Completed Plumbing Underslab Rough-in
- Continued Electrical Underground Rough-in
- Completed Foundation Wall Below Grad Waterproofing

### THIS WEEK

---

- Continuing Slab on Grade Preparation
- Complete MEP Underslab Rough-in
- Pour Partial Slab on Grade
- Install Foundation Wall Drain
- Begin Backfill Foundation Wall

## + JOBSITE PHOTOS



Foundation Wall Waterproofing




Sewer Tie-in and Paving Complete



MEP Underslab Rough-in


## WEATHER

Weather delays last week: 0

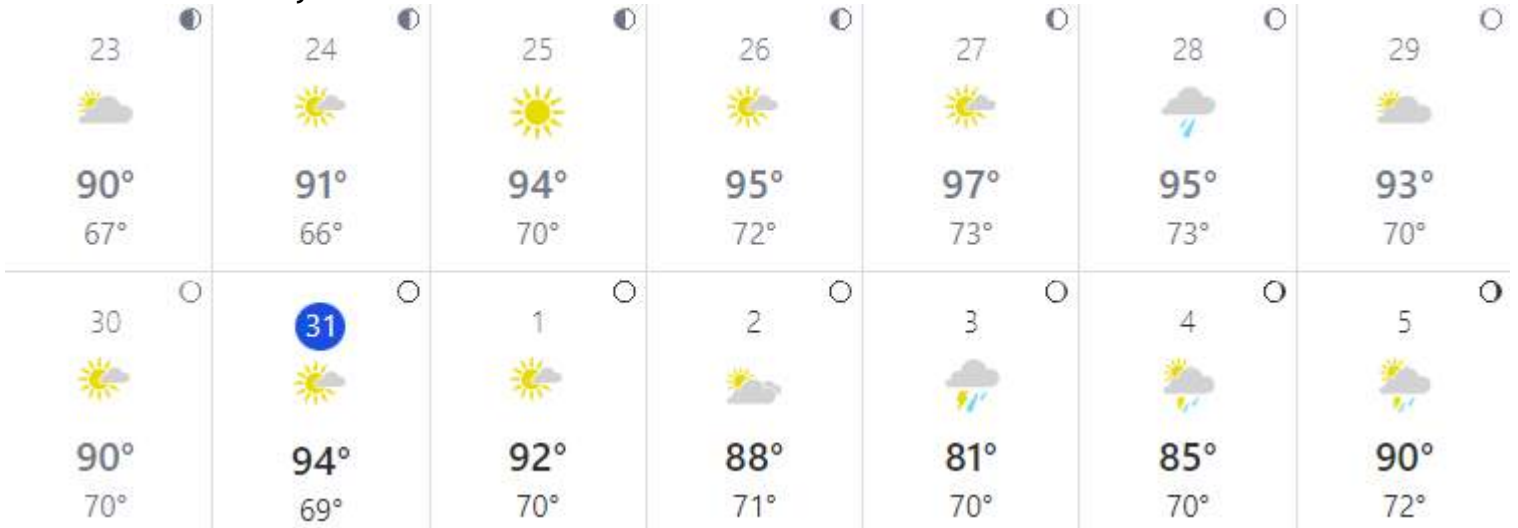

## MANPOWER

MANPOWER GRAPH

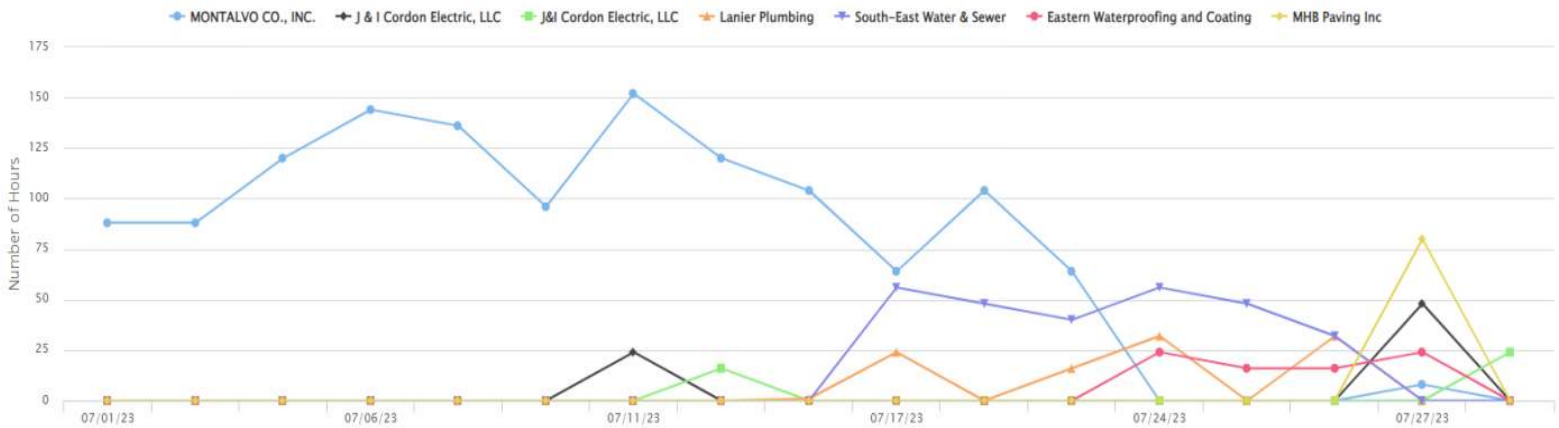

## SAFETY REPORT

- Days without an accident: 75
- Days without lost time: 75

## MILESTONE TRACKING

- Construction Start: April 10, 2023
- Current Contract Completion Date: June 10, 2023
