

CURRENT CONSTRUCTION ACTIVITIES

LAST WEEK

- Prepped and Poured Elevated Slab on Deck at the Second Floor
- Continued Interior and Exterior CMU Walls
- Continued MEP Interior Wall Rough-in
- Began Overhead Rough-in at the First Floor

THIS WEEK

- Continue Setting Structural Steel/Decking at the Apparatus Bay
- Continue MEP in-wall Rough-in
- Continue Overhead Rough-in at the First Floor
- Continue Interior and Exterior CMU Walls

+ JOBSITE PHOTOS



Elevated Slab on Deck Poured at the Second Floor



Continuing Installation of Interior CMU at the Stairwell



Continuing Overhead Rough-in


WEATHER

Weather delays last week: 1



MANPOWER

MANPOWER GRAPH

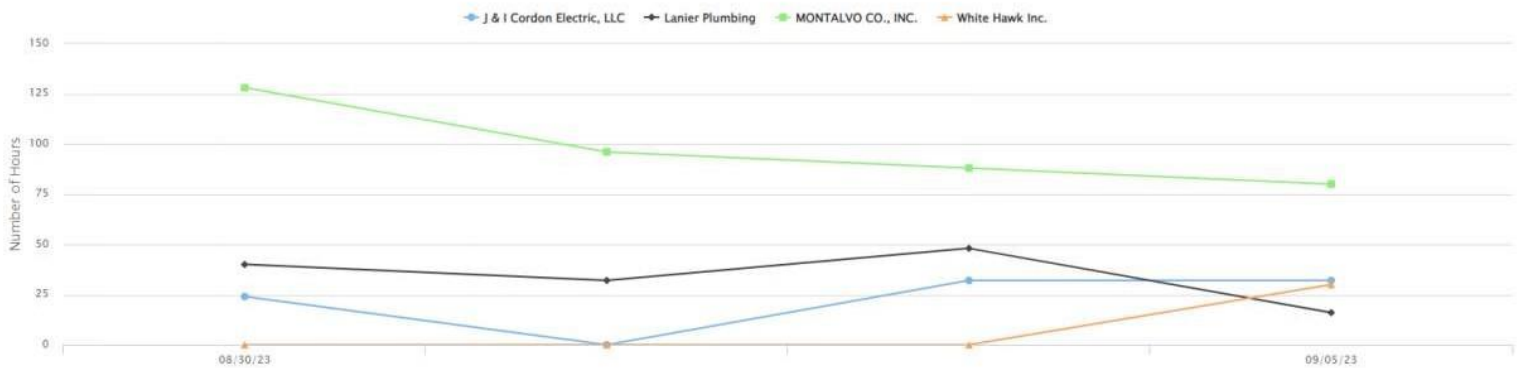

SAFETY REPORT

- Days without an accident: 102
- Days without lost time: 102

MILESTONE TRACKING

- Construction Start: April 10, 2023
- Current Contract Completion Date: June 10, 2024
