

## CURRENT CONSTRUCTION ACTIVITIES

### LAST WEEK

---

- Continued MEP In-Wall Rough-in
- Continued Exterior CMU Walls at the Apparatus Bay
- Continued MEP Interior Wall Rough-in
- Continued MEP Overhead Rough-in at the First Floor

### THIS WEEK

---

- Continue MEP in-wall Rough-in
- Continue MEP Overhead Rough-in at the First Floor
- Set Metal Pan Stairs
- Continue Decking at Apparatus Bay
- Begin Installation of Cold-Formed Trusses

 JOBSITE PHOTOS



Continued Exterior CMU at the Apparatus Bay Doors





Continued MEP Overhead and In-wall Rough-in




Installation of Metal Pan Stairs



## WEATHER

Weather delays last week: 2

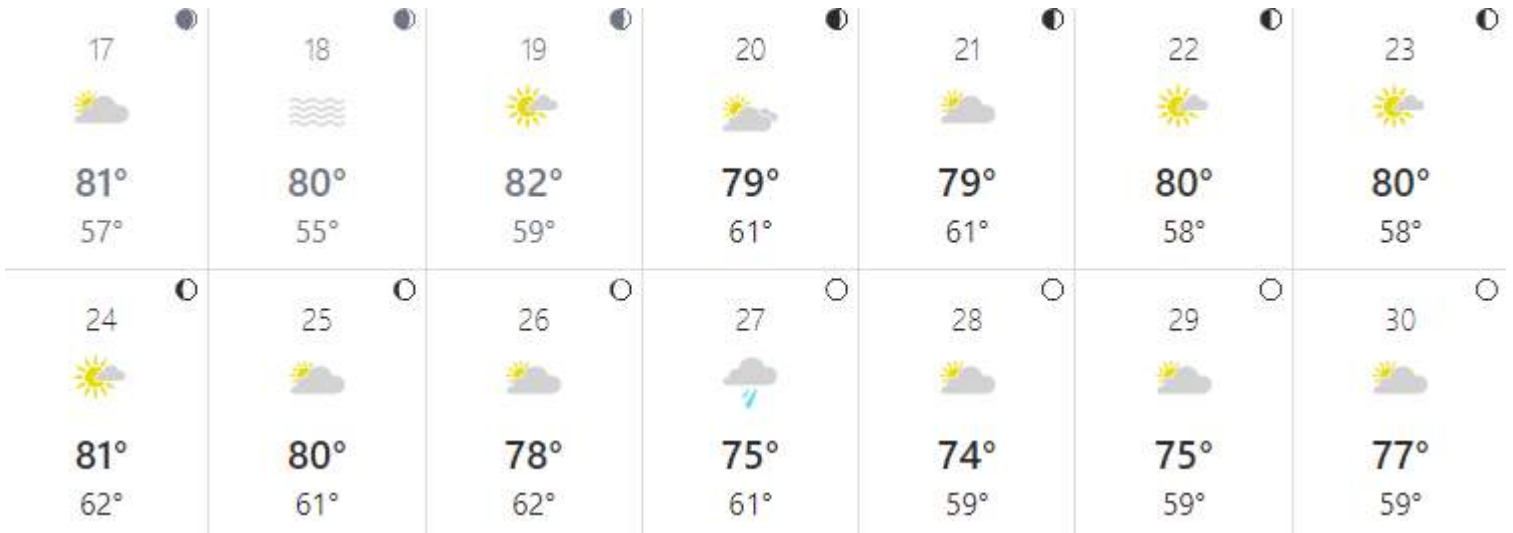

## MANPOWER

MANPOWER GRAPH



## SAFETY REPORT

- Days without an accident: 112
- Days without lost time: 112

## MILESTONE TRACKING

- Construction Start: April 10, 2023
- Current Contract Completion Date: June 10, 2024
