

CURRENT CONSTRUCTION ACTIVITIES

LAST WEEK

- Continued MEP In-Wall Rough-in
- Continued Steel Decking at the Apparatus Bay
- Completed Setting of the Metal Pan Stairs
- Continued MEP Overhead Rough-in at the First Floor
- Began Setting Cold-formed Trusses at the Roof

THIS WEEK

- Continue MEP in-wall Rough-in
- Continue MEP Overhead Rough-in at the First Floor
- Continue Detailing Metal Pan Stairs
- Continue Installation of Cold-Formed Truss Roof Decking
- Begin Installation of Cold-formed Exterior Wall Framing at the First Floor

+ JOBSITE PHOTOS



Continued MEP Rough in on first floor




Continue Detailing Metal Pan Stairs




Continued Installation of Cold Form Trusses

WEATHER

Weather delays last week: 0

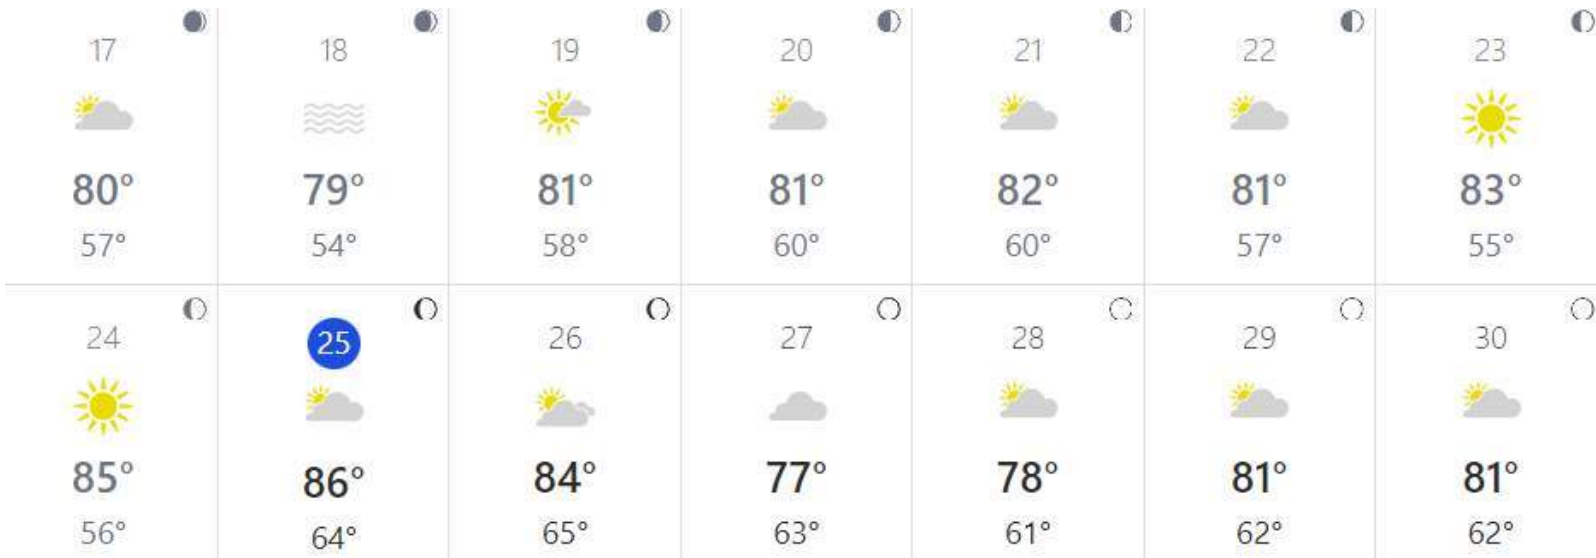

MANPOWER

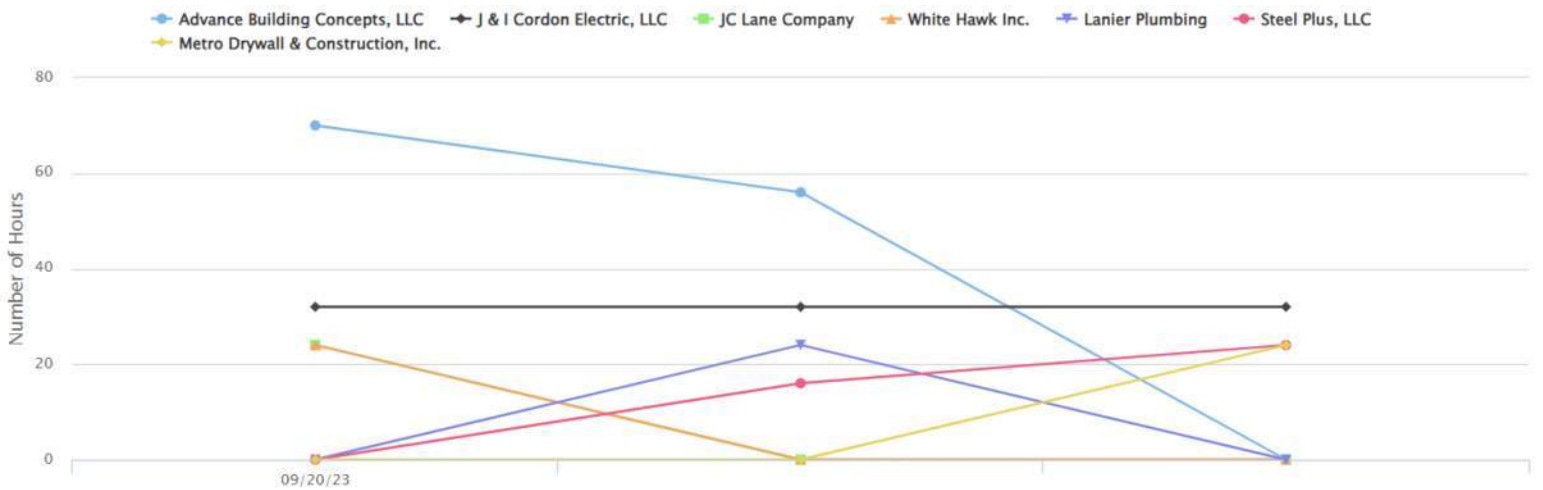

SAFETY REPORT

- Days without an accident: 115
- Days without lost time: 115

MILESTONE TRACKING

- Construction Start: April 10, 2023
- Current Contract Completion Date: June 10, 2024
