Weekly Report #4

September 20th, 2023

TOTAL CONSTRUCTION ACTIVITIES

THIS WEEK - WEEK ENDING 09/23/2023

- Continue hauling off unsuitable material
- Continued grading
- Continued building pad preparations
- Continued export of dirt


NEXT WEEK - WEEK ENDING 9/30/2023

- Continue grading
- Continued building pad preparations
- Begin building foundation prep work
- Continue export of unsuitable soil

Weekly Report #4

September 20th, 2023

★ JOBSITE PHOTOS

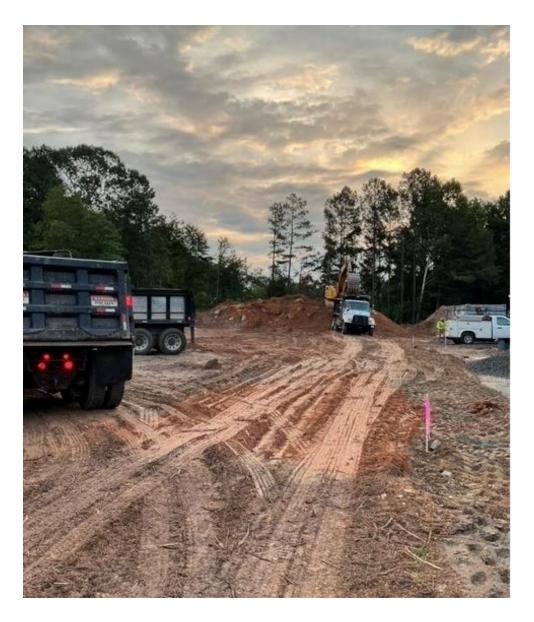

Continued Export of Dirt and Unsuitable Materials



Weekly Report #4

September 20th, 2023



Continued Grading



Weekly Report #4

September 20th, 2023



Continued Grading



Weekly Report #4

September 20th, 2023



Continued Building Pad Preparations



Weekly Report #4

September 20th, 2023



Continued Building Pad Preparations



Weekly Report #4

September 20th, 2023

★ WEATHER

Weather delays last week: 0

10	11	12	13	14	15	16
**	**	→	7	*		-
84°	89°	87°	85°	78°	74°	71°
66°	68°	69°	67°	67°	63°	63°
17	18	19	20	21	22	23 O
*	*	≱₩	*	***	*	*
80°	78°	80°	80°	79°	78°	79°
56°	55°	59°	62°	60°	60°	60°



• TBD

Weekly Report #4

September 20th, 2023

SAFETY REPORT

• Days without an accident: 22

• Days without lost time: 22

★ MILESTONE TRACKING

• Construction Start: August 21, 2023

• Current Contract Completion Date: May 17, 2024
