

CURRENT CONSTRUCTION ACTIVITIES


THIS WEEK - WEEK ENDING 09/30/2023

- Continued export of unsuitable material and dirt.
- Beginning to haul in material to begin backfilling the building pad.
- Continued building pad preparations (building pad passed the sub grade proof roll).
- Begin foundation work 09/27.

NEXT WEEK - WEEK ENDING 10/07/2023

- Begin pouring the footings.
- Get slab to grade and prepare for MEP underground rough.
- Begin preparations on the slab for concrete.
- Continue export of unsuitable soil

 JOBSITE PHOTOS

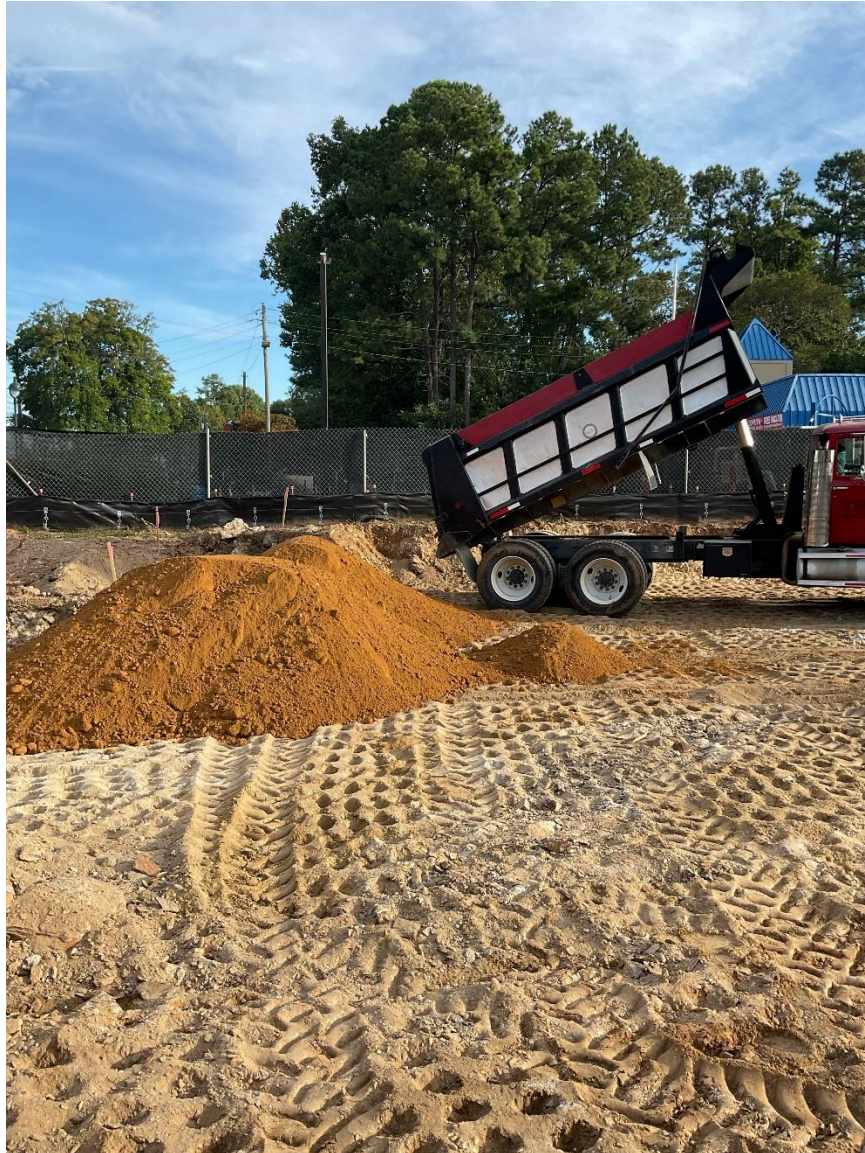

Hauling In Material to Begin Backfilling the Building Pad



Continued Grading



Continued Grading

















Continued Export of Unsuitable Materials and Dirt



Continued Building Pad Preparations

WEATHER

Weather delays last week: 0

17  80° 57°	18  79° 55°	19  81° 58°	20  80° 61°	21  81° 60°	22  80° 57°	23  83° 55°
24  85° 58°	25  85° 63°	26  83° 64°	27  74° 61°	28  77° 60°	29  80° 62°	30  80° 61°

MANPOWER

- TBD

SAFETY REPORT

- Days without an accident: 27
- Days without lost time: 27

MILESTONE TRACKING

- Construction Start: August 21, 2023
- Current Contract Completion Date: May 17, 2024
