

## CURRENT CONSTRUCTION ACTIVITIES

### LAST WEEK

---

- Continued MEP Overhead Rough-in at the First Floor
- Continued Completed Detailing for Metal Pan Stairs
- Completed Exterior Metal Stud Framing at the First Floor
- Continued Installation of Cold Form Trusses, Outriggers, and Roof Decking

### THIS WEEK

---

- Continue MEP Overhead Rough-in at the First Floor
- Continue MEP Overhead Rough-in at the Apparatus Bay
- Continue Installation of Cold-Formed Trusses, Outriggers, and Roof Decking
- Begin Installation of Cold-formed Exterior Wall Framing at the Second Floor
- Pour Remaining Building Footings at the Main Entrance and Generator Pad
- Pour Metal Pan Stairs

+ JOBSITE PHOTOS



Continued Exterior Framing at the First and Second Floor




Continued Installation of Roof Decking



Formwork for Generator Pad at the Electrical Room


# WEATHER

Weather delays last week: 0

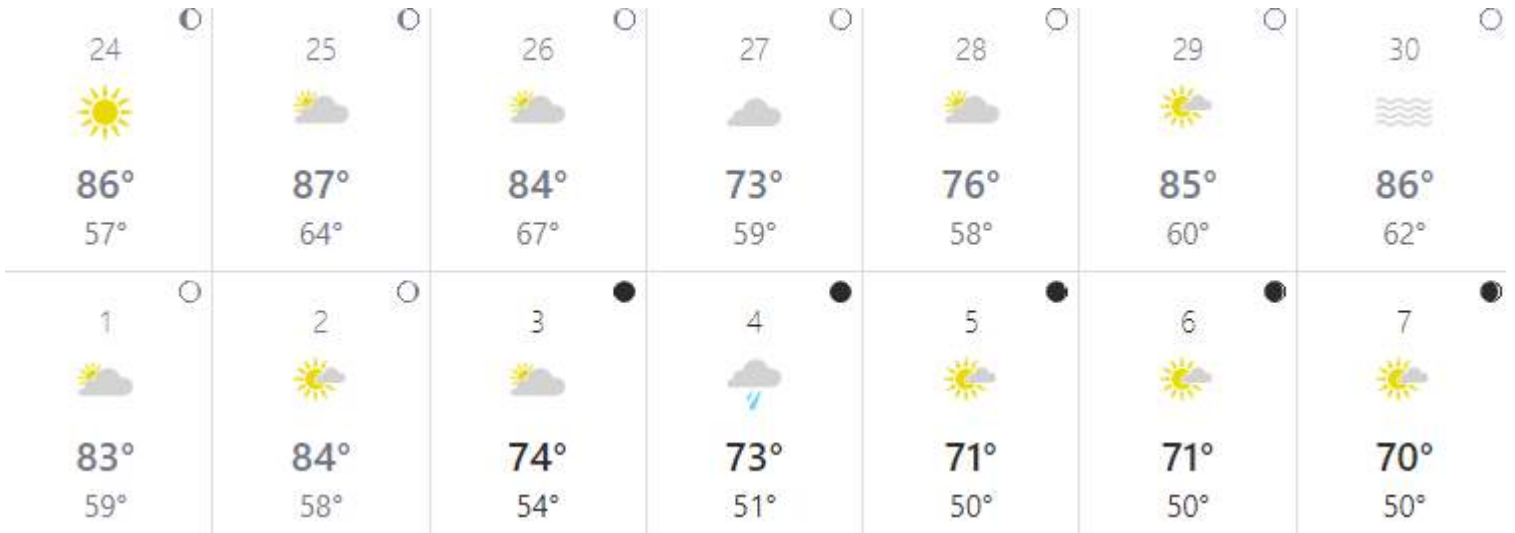

# MANPOWER

MANPOWER GRAPH

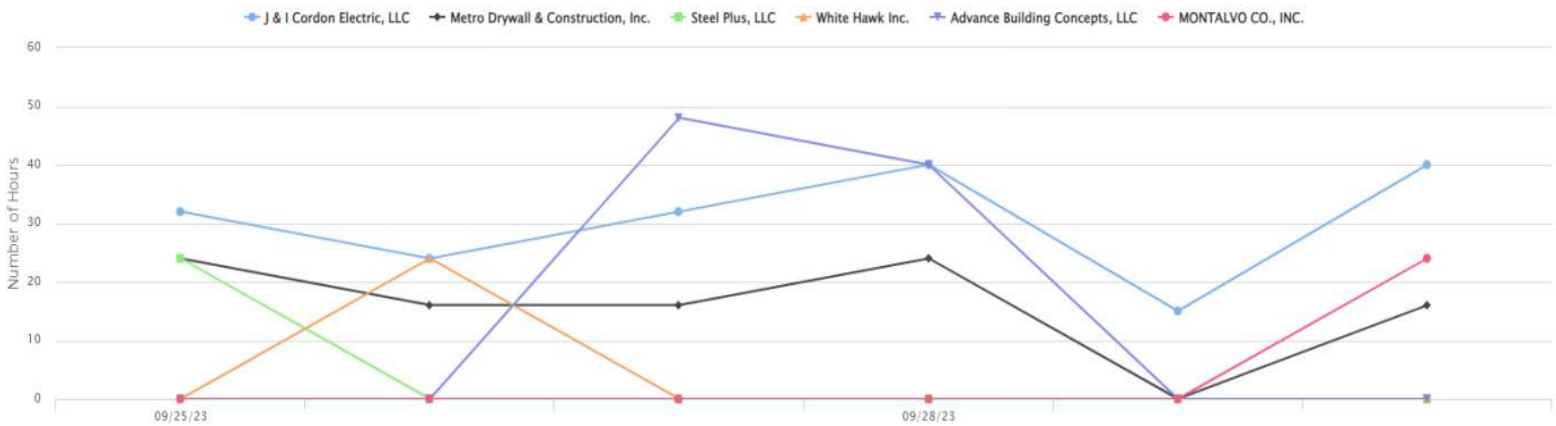

## SAFETY REPORT

- Days without an accident: 121
- Days without lost time: 121

## MILESTONE TRACKING

- Construction Start: April 10, 2023
- Current Contract Completion Date: June 10, 2024
