

+ CURRENT CONSTRUCTION ACTIVITIES

LAST WEEK

- Continued MEP Overhead Rough-in at the First Floor and Apparatus Bay
- Installed Steel Beams In Front of Main and Generator Room Entrances.
- Poured Metal Pan Stairs
- Continued Exterior Metal Stud Framing at the Second Floor.
- Began Installation of Exterior Sheathing at the First and Second Floor.

THIS WEEK

- Continue MEP Overhead Rough-in on the First Floor.
- Complete MEP Below-Grade Rough-in at Apparatus Bay.
- Continue Sheathing on First and Second Floor.
- Complete Apparatus Bay Slab on Grade Preparation.

+ JOBSITE PHOTOS



Sheathing Installation on Both First and Second Floor.



Continue MEP Inwall Rough In and Sheathing



Prepping Apparatus Bay for Slab on Grade Pour

WEATHER


Weather delays last week: 0

< Sep Oct 2023 View Nov >

SUN	MON	TUE	WED	THU	FRI	SAT
1 ☀️ 82° 58°	2 ☀️ 83° 57°	3 ☀️ 83° 58°	4 ☀️ 83° 58°	5 ☀️ 81° 63°	6 ☁️ 75° 56°	7 ☀️ 67° 44°
8 ☀️ 67° 41°	9 🌙 -- 51°	10 ☀️ 79° 58°	11 ☁️ 73° 56°	12 ☁️ 66° 60°	13 ☁️ 67° 61°	14 ☀️ 73° 51°

MANPOWER

MANPOWER GRAPH

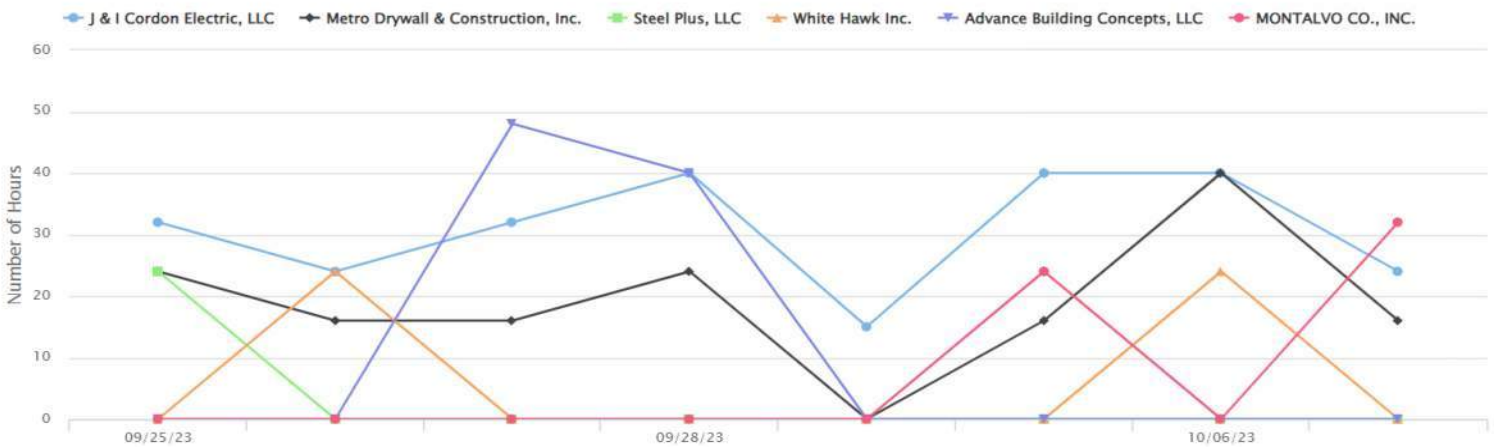

SAFETY REPORT

- Days without an accident: 128
- Days without lost time: 128

MILESTONE TRACKING

- Construction Start: April 10, 2023
- Current Contract Completion Date: June 10, 2024
