

## + CURRENT CONSTRUCTION ACTIVITIES

### LAST WEEK

---


- Continued MEP Interior Wall and Overhead Rough-in at the First Floor
- Completed Concrete Prep for Apparatus Bay Slab-on-Grade Pour
- Continued Interior Framing on First Floor
- Continued Exterior Soffit Framing at the Covered Poarch
- Completed Trench Drains Installation at the Apparatus Bay
- Completed Exterior Sheathing on First and Second Floor

### THIS WEEK

---

- Pour Concrete Slab on Grade at the Apparatus Bay
- Prep and Pour Footings for Retaining Wall at Spalding Rd Entrance
- Continue Interior Framing on first Floor
- Begin TPO and Roof Install
- Continue MEP Interior Rough in on First and Second Floor
- Begin Installation of Exterior Fluid-Applied Waterproofing

+ JOBSITE PHOTOS

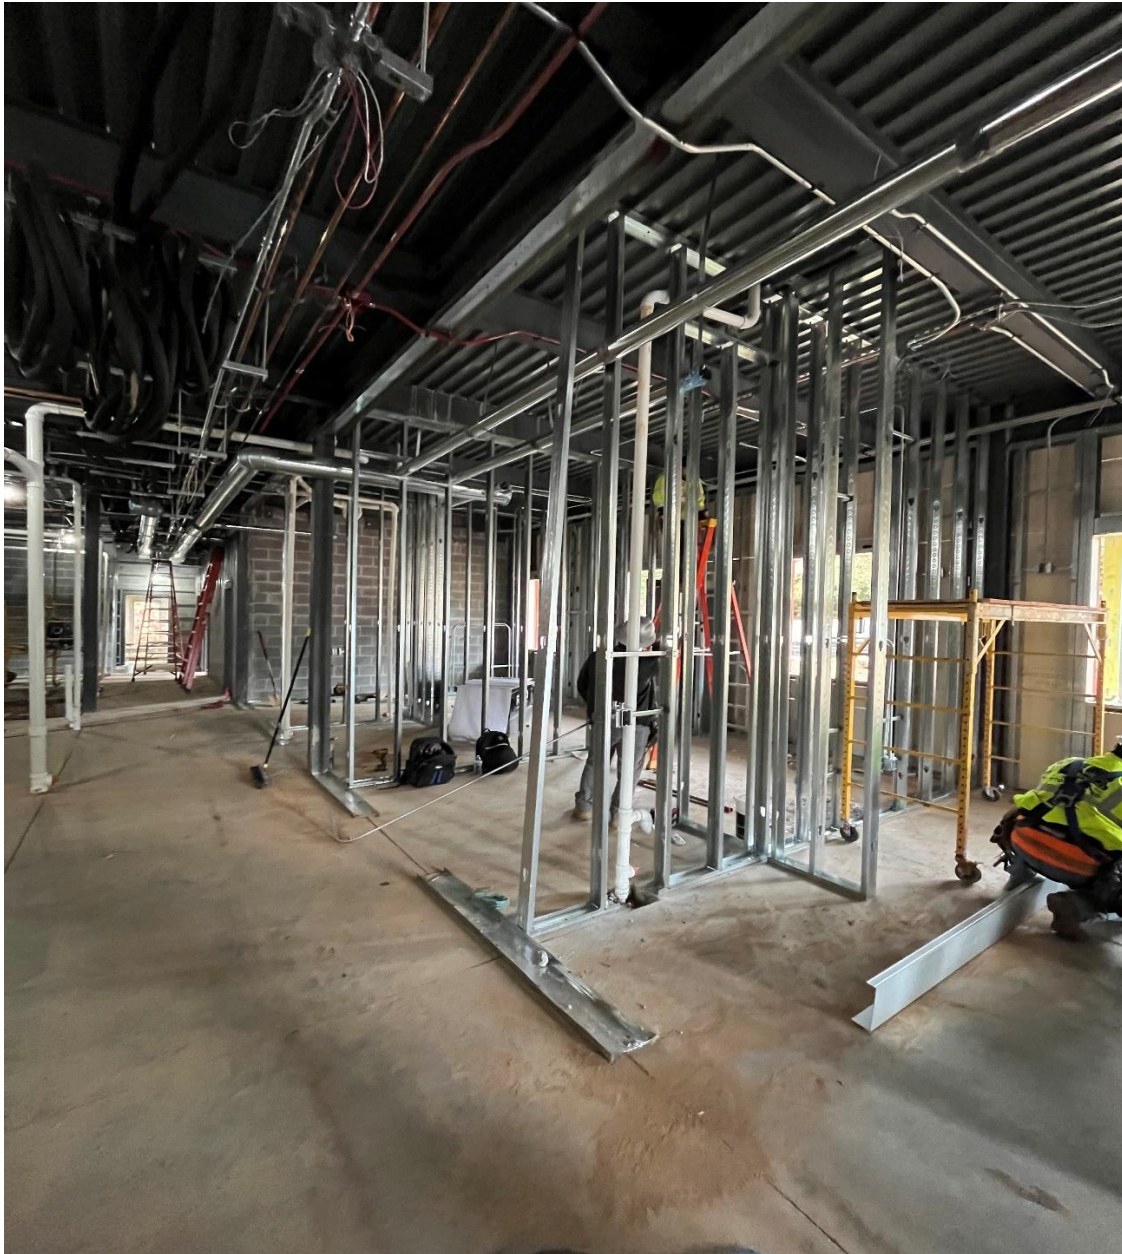

Began Interior Framing on First Floor.





Completed Concrete Prep at Apparatus Bay.






Completed Exterior Sheathing on First and Second Floor.




## WEATHER

Weather delays last week: 1

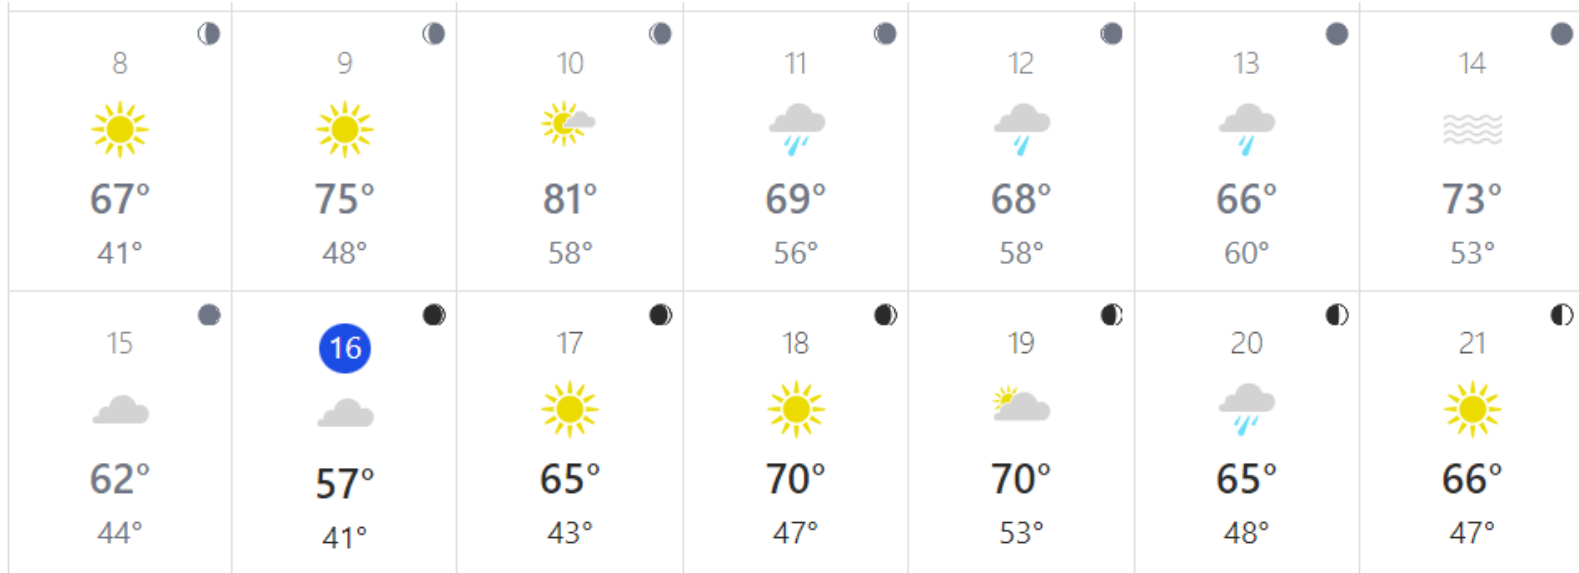

## MANPOWER

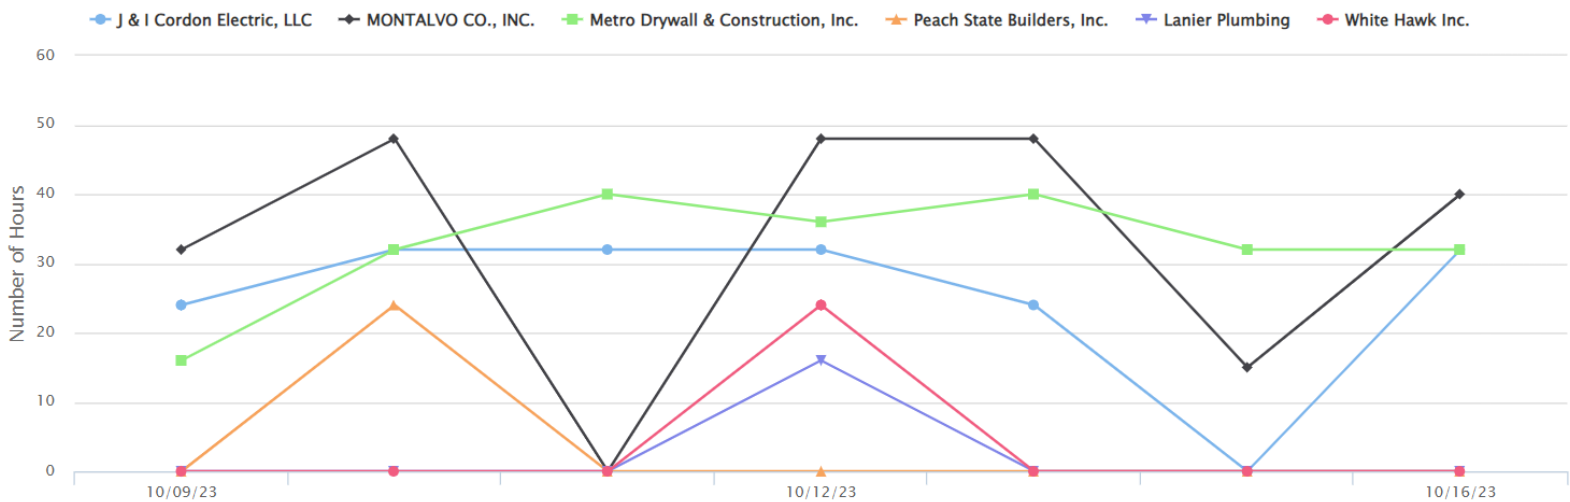

## SAFETY REPORT

- Days without an accident: 135
- Days without lost time: 135

## MILESTONE TRACKING

- Construction Start: April 10, 2023
- Current Contract Completion Date: June 10, 2024
