

CURRENT CONSTRUCTION ACTIVITIES

THIS WEEK - WEEK ENDING 10/28/2023

- Begin pouring the slab.
- Form and pour the stem wall.
- Delivery of the PEMB.
- Begin pouring the SOG.


NEXT WEEK - WEEK ENDING 11/04/2023

- Erecting the PEMB.

 JOBSITE PHOTOS



Prep For Slab

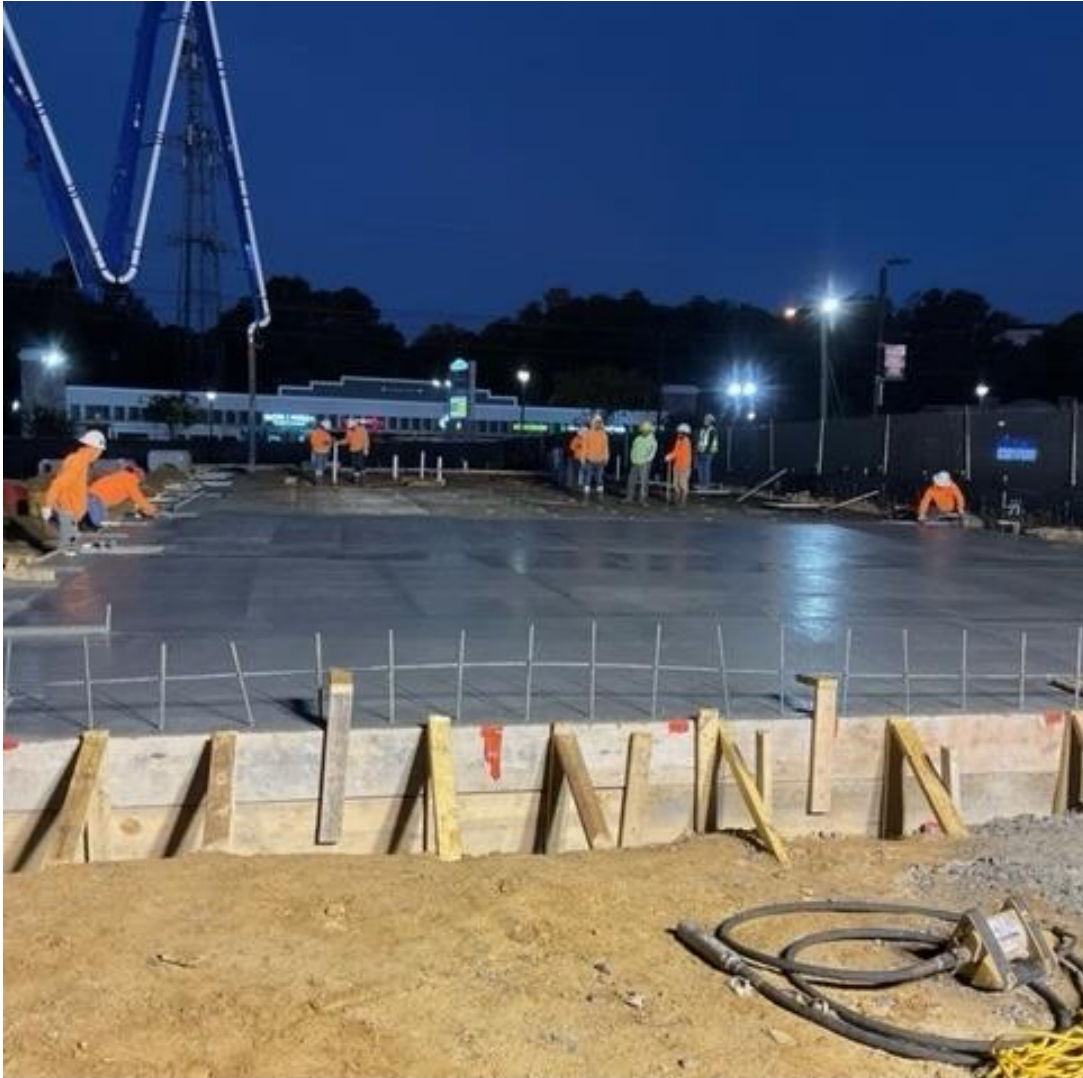

Pour SOG

















Float SOG



Completed Pouring SOG

 WEATHER

Weather delays last week: 0

22  77° 46°	23  71° 45°	24  72° 48°	25  75° 56°	26  76° 56°	27  78° 56°	28  81° 57°
29  82° 59°	30  79° 51°	31  71° 41°	1  57° 35°	2  58° 40°	3  62° 44°	4  65° 47°

SAFETY REPORT

- Days without an accident: 47
- Days without lost time: 47

MILESTONE TRACKING

- Construction Start: August 21, 2023
- Current Contract Completion Date: March 19, 2024
