

## + CURRENT CONSTRUCTION ACTIVITIES

### LAST WEEK

---

- Continued MEP Interior Wall Rough-in on First Floor
- Completed Pour of Concrete Retaining Wall at Spalding Entrance
- Completed Interior Framing on First Floor
- Completed Second Floor Hat-Channel Install
- Completed Exterior Sheathing Fluid-Applied Waterproofing
- Began Overhead Drywall Install at Second Floor
- Completed Blocking on First Floor
- Completed Window Flashing at the First and Second Floors

### THIS WEEK

---

- Begin Install of Wood Windows on First and Second Floor
- Begin Interior Wall Framing on Second Floor
- Begin overhead Duct Work Install on second Floor
- Continue MEP Interior Rough-in on First and Second Floor
- Begin Brick Masonry Mockup at Spalding Entrance
- Continue Overhead Rough-in At Apparatus Bay

+ JOBSITE PHOTOS



Completed Hack Channel Install and Began Sheet Rock Installation.




Installed Flashing on all First and Second Floor Windows



Completed Concrete Retaining Wall at Spalding Entrance


## WEATHER

Weather delays last week: 0

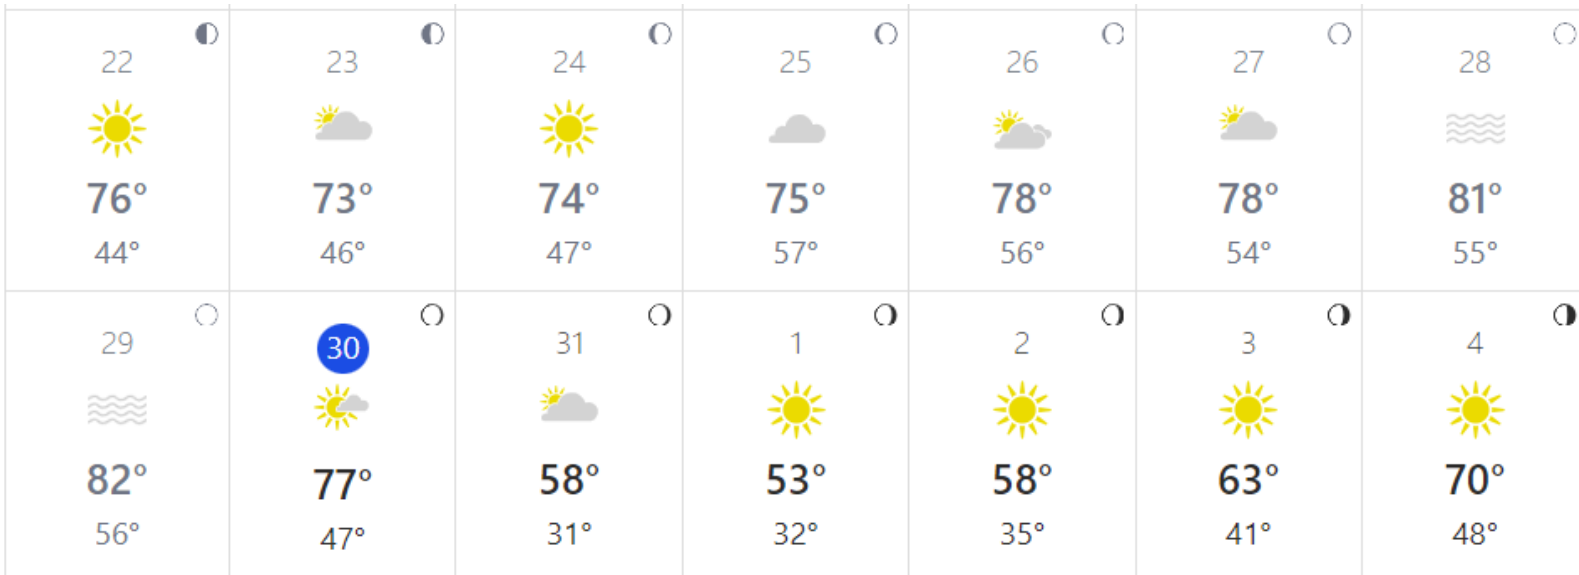

## MANPOWER

### MANPOWER GRAPH

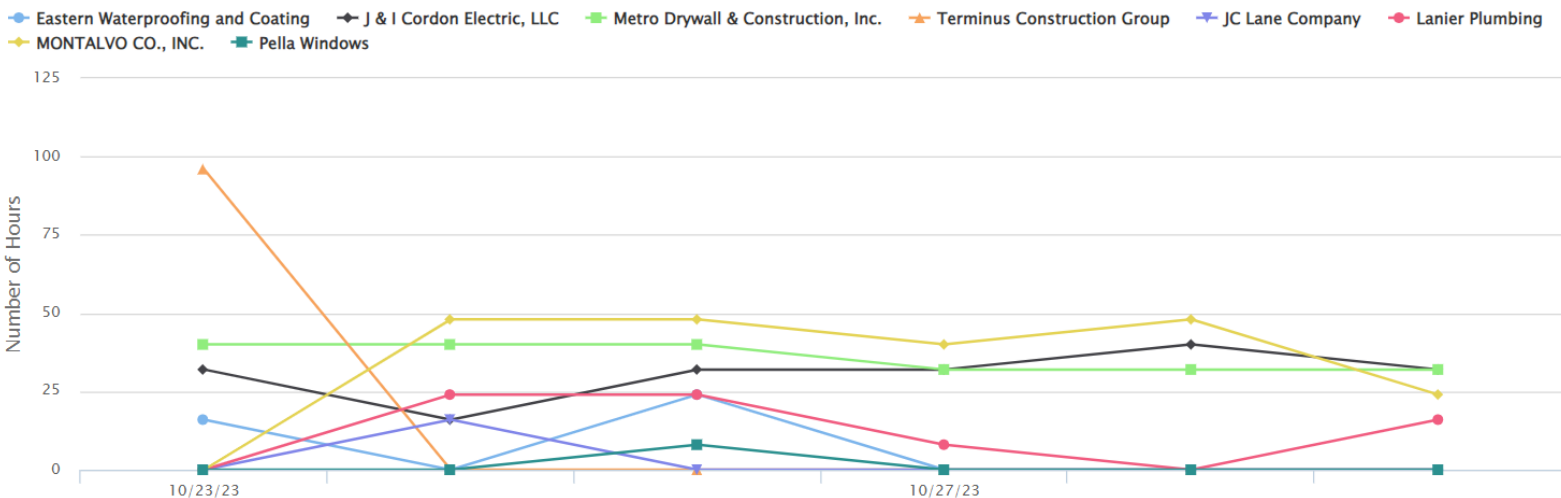

## SAFETY REPORT

- Days without an accident: 145
- Days without lost time: 145

## MILESTONE TRACKING

- Construction Start: April 10, 2023
- Current Contract Completion Date: June 10, 2024
