

CURRENT CONSTRUCTION ACTIVITIES

LAST WEEK

- Began Drip Edge Install Around Below Grade Brick
- City of Atlanta Continued Working on Water Vault Install
- Continued Backfill Around the Building
- Completed Wood Window and Door Install for Entire Building
- Continued Overhead Rough-in on Second Floor
- Continued Interior Wall Rough-in on Second Floor
- Began Staking and Fine Grading for Curb Installation
- Began Brick Mockup with Cast Stone.

THIS WEEK

- Building Mock-up Review
- Continue Installation of Brick Veneer and Cast Stone
- City of Atlanta to Complete Water Vault Install
- Continue Second Floor Interior Rough-in
- Continue Backfill Around Building
- Complete Pour of Curb and Gutter

+ JOBSITE PHOTOS



Continued Brick Veneer at Retaining Wall




Continued Brick Mockup with Cast Stone



City of Atlanta Continued Working on Water Vault Install


WEATHER

Weather delays last week: 0

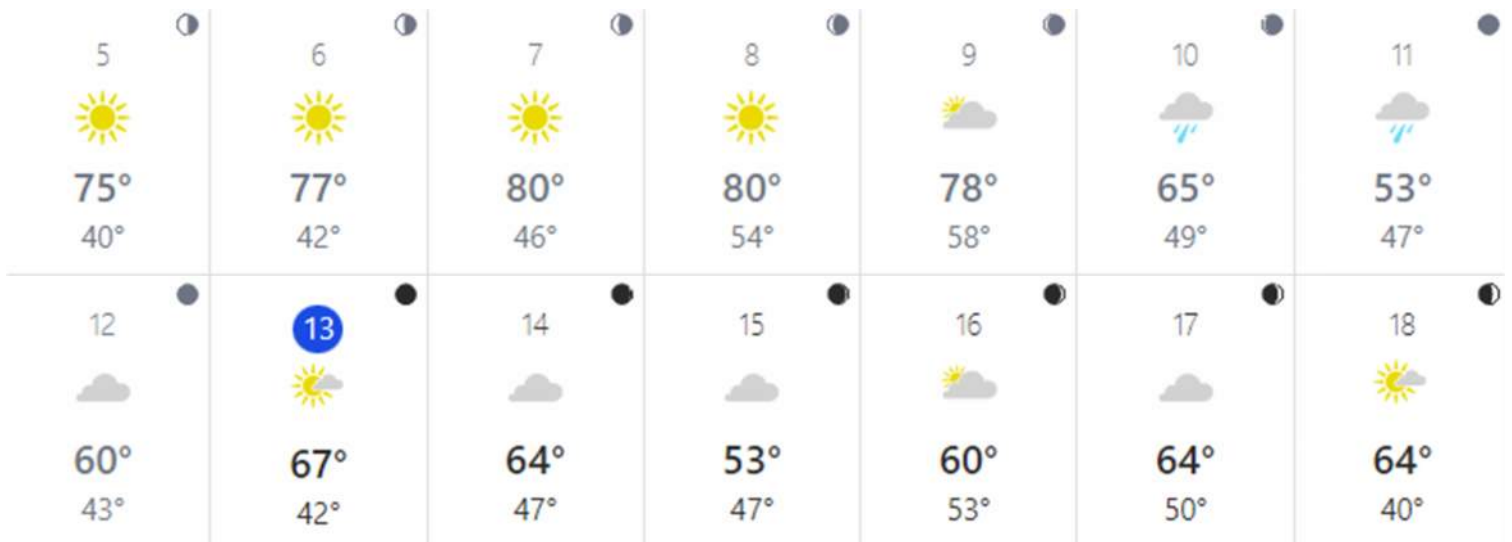

MANPOWER


 Eastern Waterproofing and Coating J & I Cordon Electric, LLC JC Lane Company Lanier Plumbing Metro Drywall & Construction, Inc. South-East Water & Sewer Gainesville Fire Protection MONTALVO CO., INC. Performance Construction Services, LLC

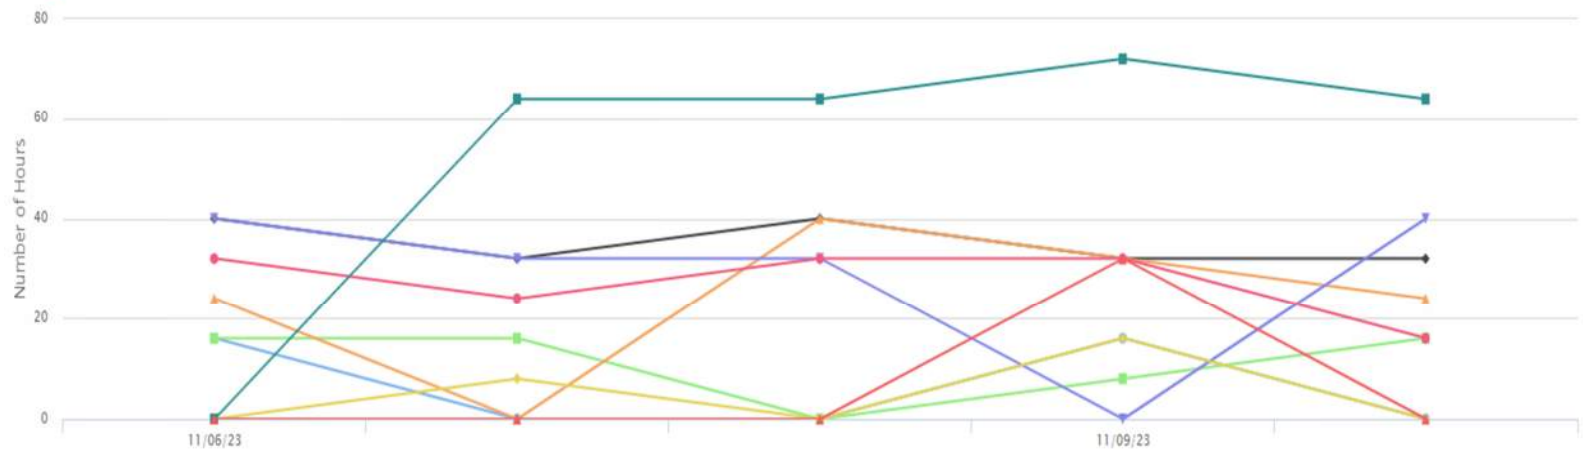

SAFETY REPORT

- Days without an accident: 150
- Days without lost time: 150

MILESTONE TRACKING

- Construction Start: April 10, 2023
- Current Contract Completion Date: June 10, 2024
