

## CURRENT CONSTRUCTION ACTIVITIES

### LAST WEEK

---

- Continued Duct Work Installation in Attic Space
- Continued MEP Overhead Installation on Second Floor
- Continued Panel Install in Generator Room
- Continued Brick and Cast Stone Installation
- Heavy Timber Trusses Delivered
- Completed Sink Carrier Install in Deacon Room
- Continued High Impact Sheet Rock Installation

### THIS WEEK

---

- Begin Timber Truss Installation
- Continue Curb and Gutter at Mt Vernon Entrance
- Continue MEP Overhead Installation on Second Floor
- Continue High Impact Sheet Rock Installation at Stairwell
- Begin Drainage Pipe Installation at Spalding Dr Entrance
- Continue Brick Veneer and Cast Stone Installation

 JOBSITE PHOTOS



Continued Attic Space Duct Work Installation





Continued Brick Veneer and Cast Stone Installation




Continued High Impact Sheet Rock Installation in Stairwell




## WEATHER

Weather delays last week: 0

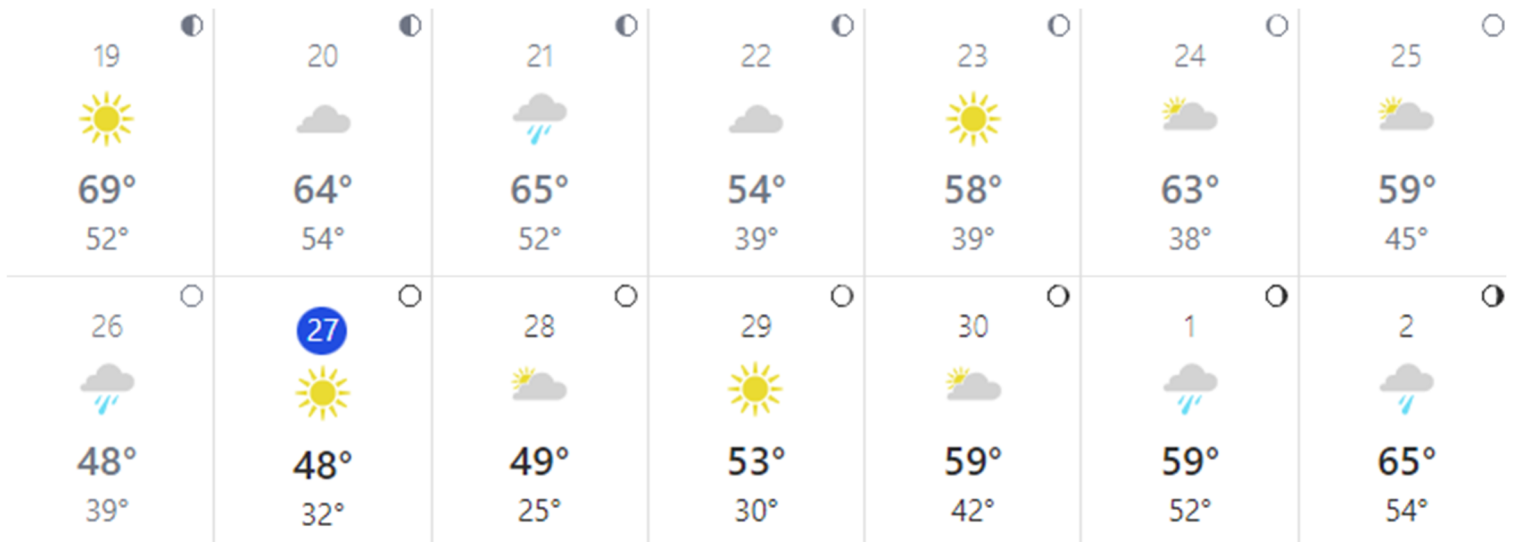

## MANPOWER

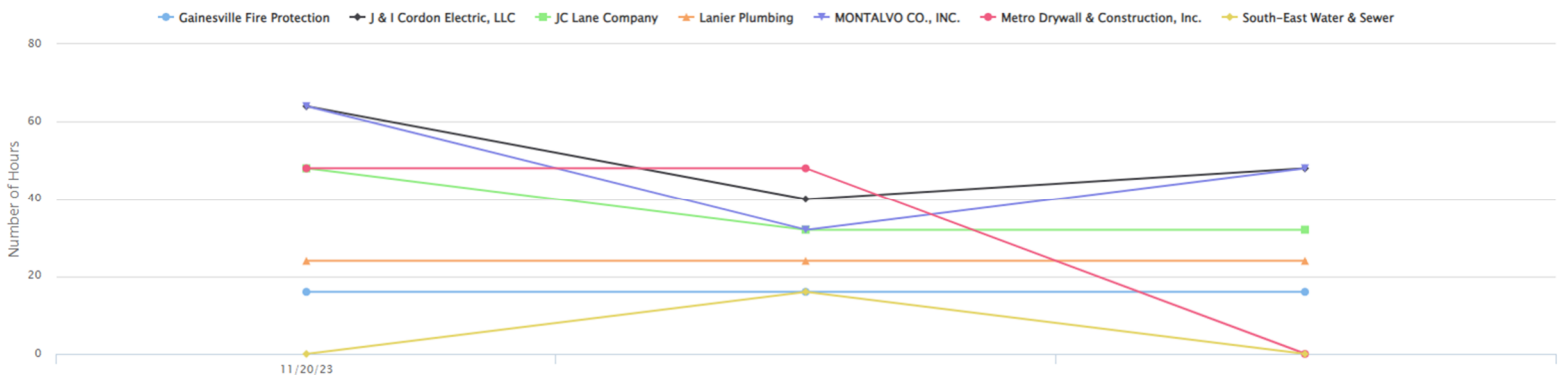

## SAFETY REPORT

- Days without an accident: 160
- Days without lost time: 160

## MILESTONE TRACKING

- Construction Start: April 10, 2023
- Current Contract Completion Date: June 10, 2024
