

+ CURRENT CONSTRUCTION ACTIVITIES

LAST WEEK

- Continued MEP Interior Wall Rough-in at First Floor
- Began Window Installation on First and Second Floor
- Began Below Grade Brick Installation
- Completed Steel Railing Installation at Second Floor Porch
- Continued Overhead Drywall Installation on Second Floor
- Began Second Floor Interior Framing
- Began Second Floor Duct Work Installation.
- Completed Steel Framing for Apparatus Bay Doors

THIS WEEK

- Continue Interior Wall Framing at Second Floor
- Continue Overhead Duct Work Installation at second Floor
- Continue MEP Interior Rough-in at First and Second Floor
- Continue Brick Masonry Mockup at Spalding Entrance
- Continue Overhead Rough-in at Apparatus Bay
- Begin Backfilling Dirt at Mount Vernan Entrance
- Begin Sheet Rock Install on First Floor Interior Walls

 JOBSITE PHOTOS



Completed Metal Railing Installation at Second Floor Porch.



Began Window Installation on the First and Second Floor.



Continued Second Floor Interior Installation on Second Floor.


WEATHER

Weather delays last week: 0

SUN	MON	TUE	WED	THU	FRI	SAT
29 ☉ ☁ 82° 56°	30 ☉ ☁ 82° 47°	31 ☉ ☁ 60° 32°	1 ☉ ☀ 55° 29°	2 ☉ ☀ 57° 30°	3 ☉ ☀ 65° 35°	4 ☉ ☀ 71° 40°
5 ☉ ☀ 75° 42°	6 ☉ ☀ 76° 45°	7 ☉ ☀ 79° 48°	8 ☉ ☀ 80° 53°	9 ☉ ☁ 79° 58°	10 ☉ ☁ 69° 50°	11 ☉ ☁ 64° 48°

MANPOWER

MANPOWER GRAPH

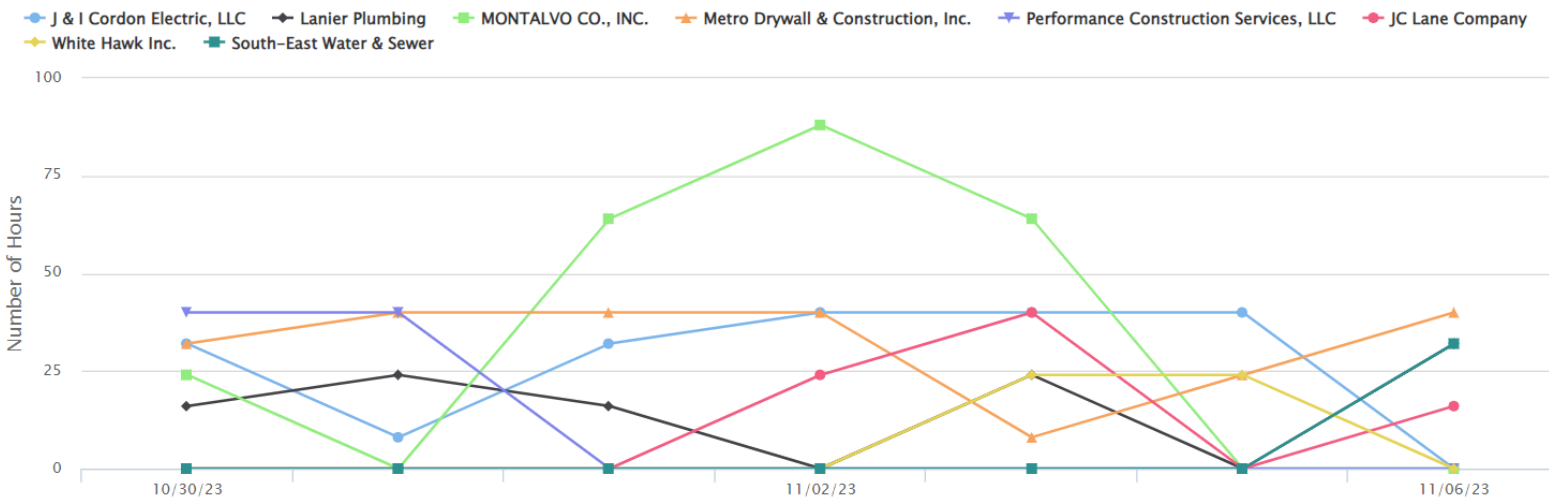

SAFETY REPORT

- Days without an accident: 150
- Days without lost time: 150

MILESTONE TRACKING

- Construction Start: April 10, 2023
- Current Contract Completion Date: June 10, 2024
