

## + CURRENT CONSTRUCTION ACTIVITIES

### LAST WEEK

---

- Continued Brick Veneer and Cast Stone Installation
- Continued MEP Overhead Installation on Second Floor
- Continued Panel Install in Generator Room
- Generator Installed in Generator Room
- Heavy Timber Trusses Installed
- Water Vault Installed at Mt Vernon
- Completed Curb and Gutter at Mt Vernon

### THIS WEEK

---

- HVAC Units to be installed
- Begin Shingle and Roofing Install
- Begin Oil and Water Separator Install
- Continue In-Wall and Overhead MEP Installation
- Continue Brick Veneer and Cast Stone Installation
- Addressing Engineer's Reports

 JOBSITE PHOTOS



Curb and Gutter Completed at Mt Vernon




Heavy Timber Trusses Installed



Generator Installed in Generator Room


## WEATHER

Weather delays last week: 0

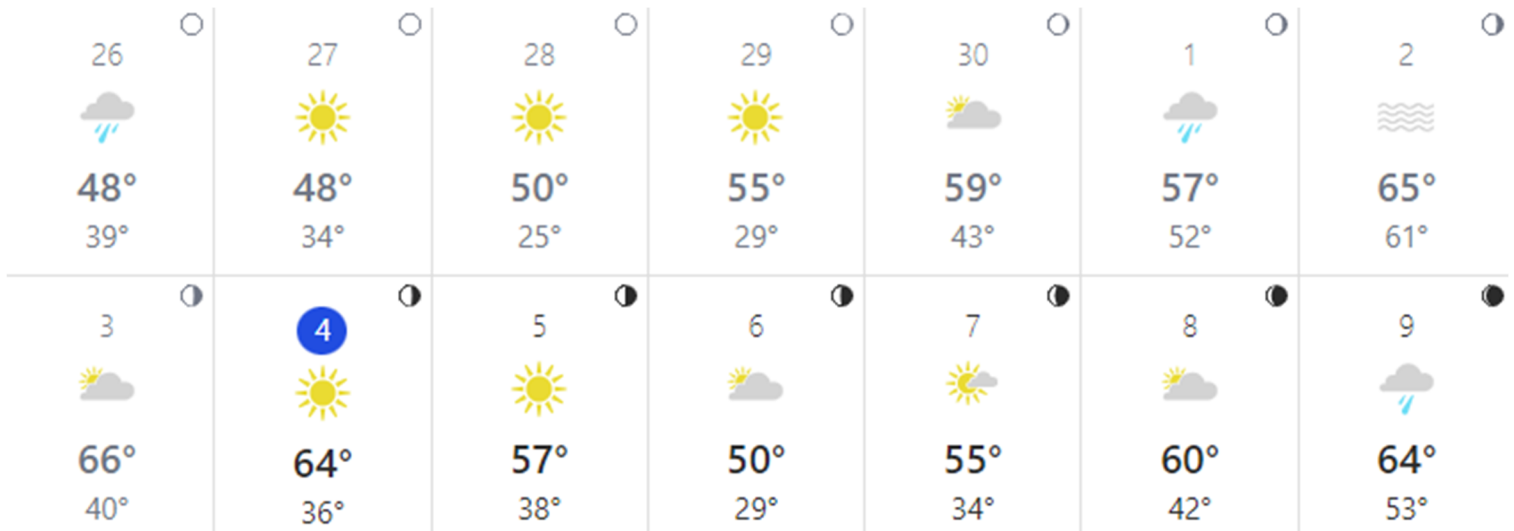

## MANPOWER

◆ Advance Building Concepts, LLC 
 ◆ Gainesville Fire Protection 
 ◆ J & I Cordon Electric, LLC 
 ◆ JC Lane Company 
 ◆ Lanier Plumbing 
 ◆ MONTALVO CO., INC. 
 ◆ Metro Drywall & Construction, Inc. 
 ◆ KB Contracting of GA LLC 
 ◆ South-East Water & Sewer

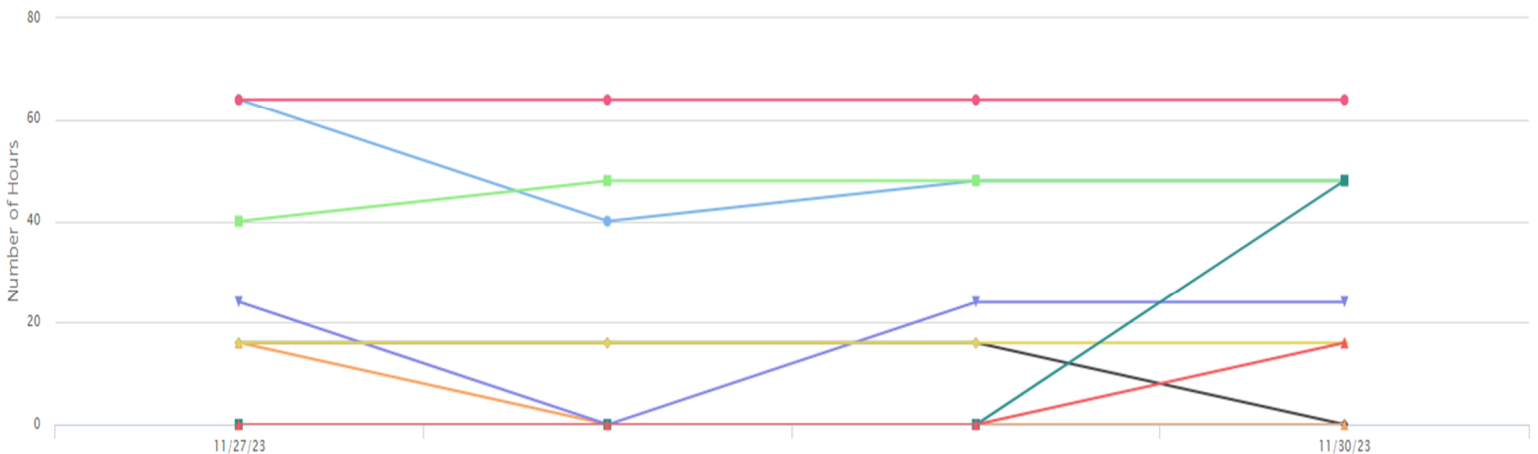

## SAFETY REPORT

- Days without an accident: 165
- Days without lost time: 165

## MILESTONE TRACKING

- Construction Start: April 10, 2023
- Current Contract Completion Date: June 10, 2024
