

+ CURRENT CONSTRUCTION ACTIVITIES

LAST WEEK

- Began Installing Bifold Doors at Apparatus Bay
- HVAC Rooftop Units Were Installed
- Continued Shingle Roofing Underlayment at Gabel End-Walls
- Continued In-Wall and Overhead MEP Installation
- Began Brick Veneer and Cast Stone Installation on Mt Vernon Side
- Tied in Fire Line, and Installed BFP at Water Meter
- Began Installing Header Curb and Sleaving and Prep for Mt Vernon Parking Lot

THIS WEEK

- Begin Shingle Roofing Installation
- Continue Bifold Doors Installation at Apparatus Bay
- Continue Installing Header Curb and Sleaving and Prep for Mt Vernon Parking Lot
- Continue In-Wall and Overhead MEP Installation on Second Floor
- Continue Brick Veneer and Cast Stone Installation

+ JOBSITE PHOTOS



Began Installing Header Curb and Sleaving and Prep for Mt Vernon Parking Lot




HVAC Rooftop Units Were Installed




Began Installing Bifold Doors at Apparatus Bay

WEATHER

Weather delays last week: 0

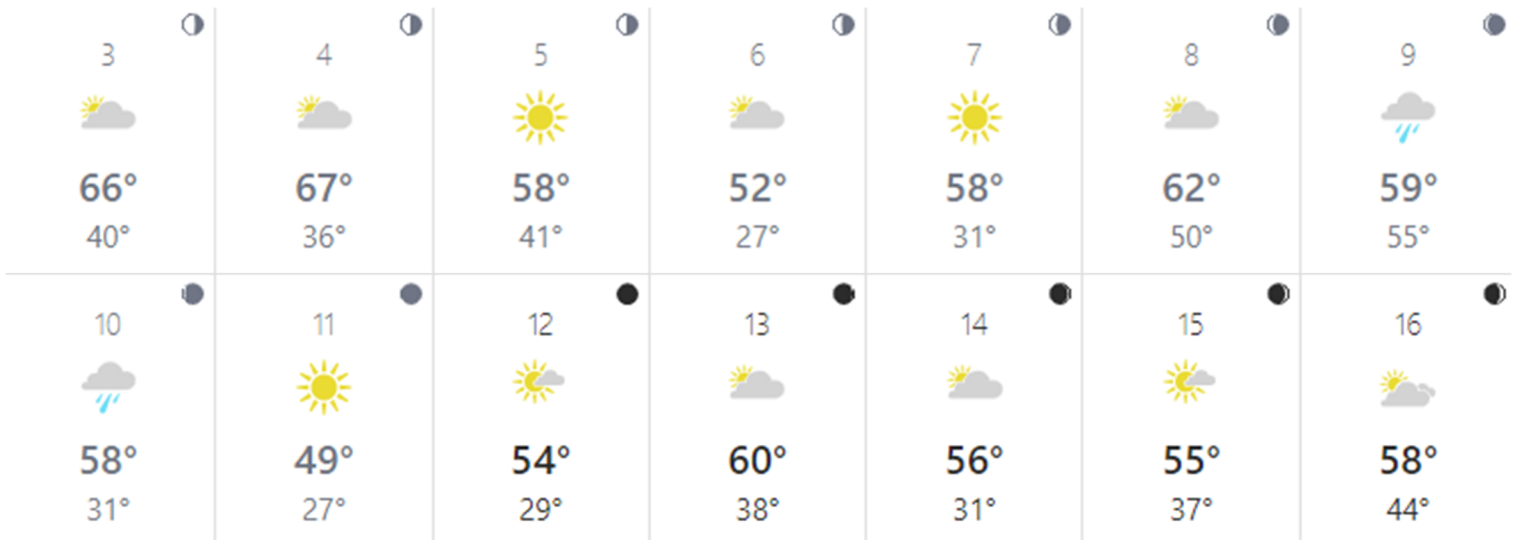

MANPOWER

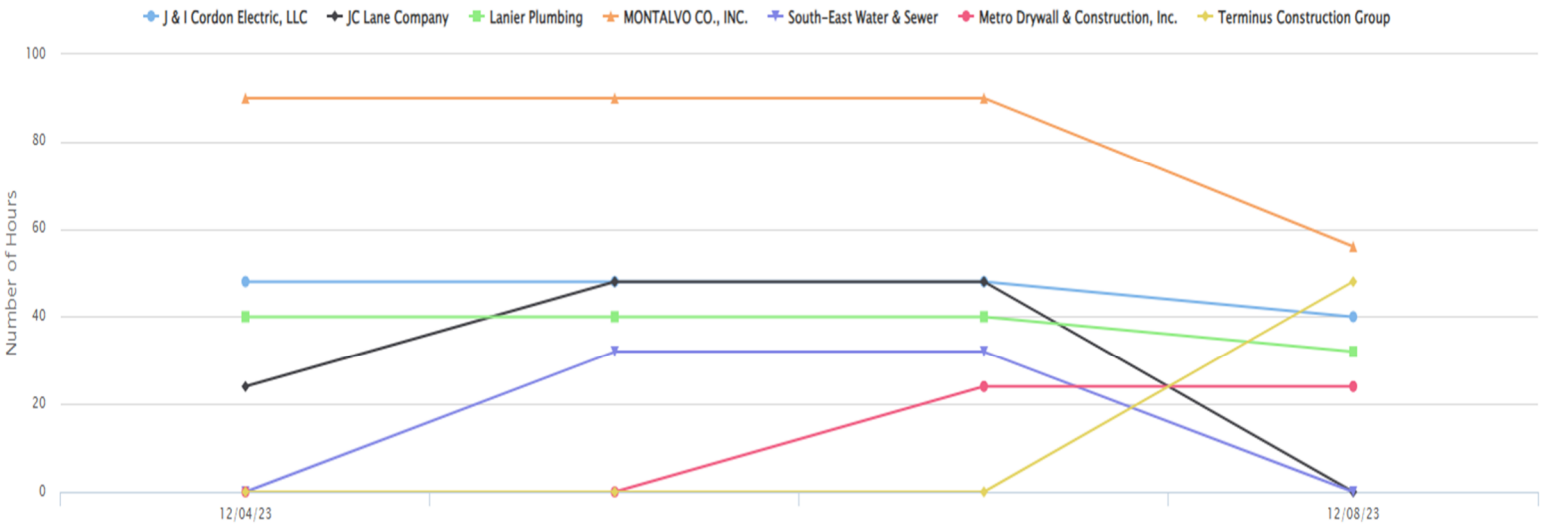

SAFETY REPORT

- Days without an accident: 170
- Days without lost time: 170

MILESTONE TRACKING

- Construction Start: April 10, 2023
- Current Contract Completion Date: June 10, 2024
