

+ CURRENT CONSTRUCTION ACTIVITIES

LAST WEEK - WEEK ENDING 12/02/2023

- Continue electrical overhead rough-in on level 3.
- Begin mechanical PIU/VAV rough-in on level 3.
- Begin mechanical overhead rough-in on level 2.
- Continue joist augmentation on level 1.
- Begin fireproofing on level 1.
- Continue slab demolition on the basement.
- Begin joist augmentation on the basement.
- Begin stair 1 steel installation on the roof.
- Continue exterior demo brick/glass/lintel/kicker.
- Begin installing storm line "A".
- Begin grading at sally port.

THIS WEEK - WEEK ENDING 12/09/2023

- Continue electrical overhead rough-in on level 3.
- Continue mechanical PIU/VAV rough-in on level 3.
- Begin interior framing on level 3.
- Continue mechanical overhead rough-in on level 2.
- Continue slab demolition on the basement.
- Continue joist augmentation on the basement.
- Continue stair 1 steel installation on the roof.
- Continue exterior demo brick/glass/lintel/kicker.
- Continue installing U/G utilities.
- Continue grading at Sally Port.
- Begin preparations for footings at sally port.

+ JOBSITE PHOTOS



Continue Mechanical PIU/VAV Rough-In On Level 3



Continue Grading At Sally Port



Continue Exterior Demo Brick/Glass/Lintel/Kicker - North Face



Continue Exterior Demo Of Brick/Glass/Lintel/Kicker



Joist Augmentation On Level 1




Continue Installing U/G Utilities



Continue Exterior Demo of Brick/Glass/Lintel/Kicker



Mechanical Overhead Rough-in On Level 2

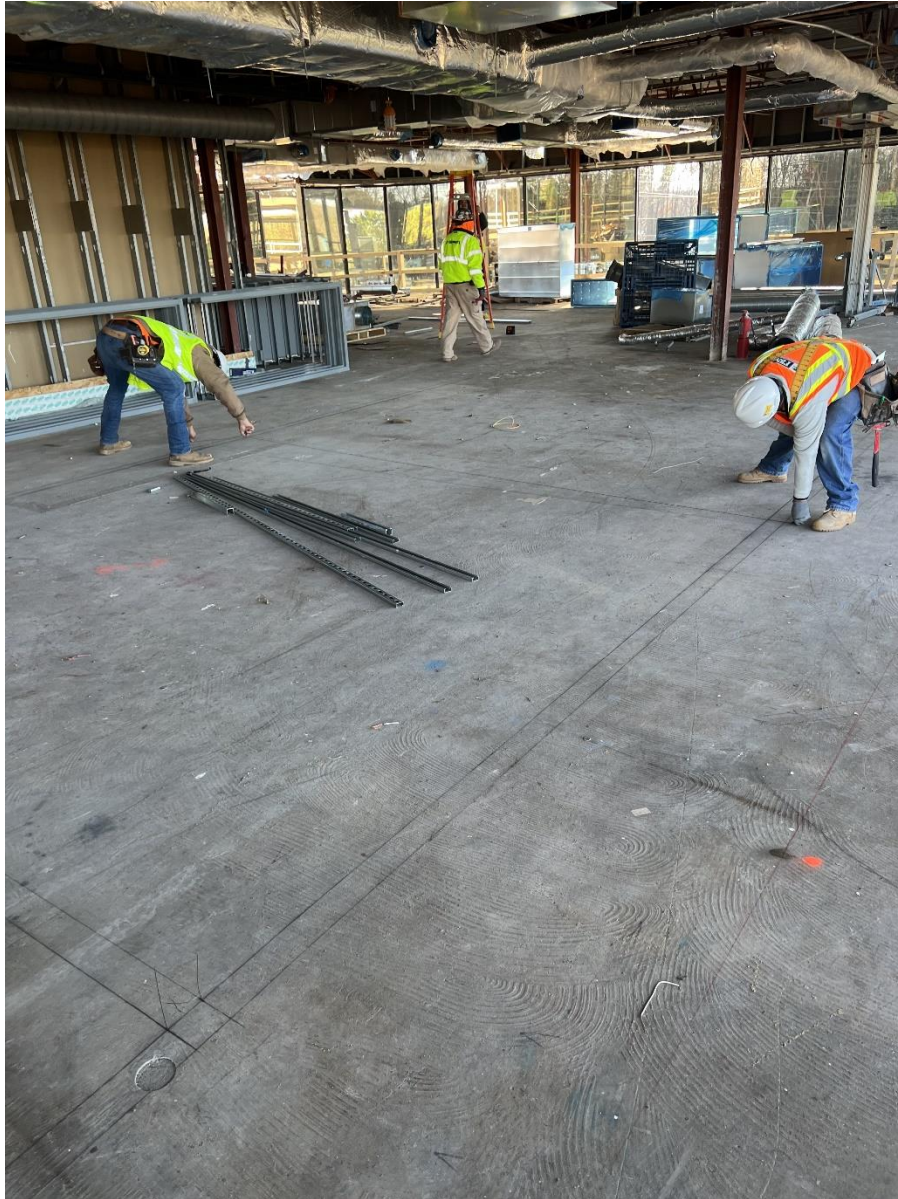















Begin Interior Framing On Level 3



Continue Installing U/G Utilities

 WEATHER

Weather delays last week: 0

26  47° 39°	27  49° 34°	28  50° 25°	29  55° 31°	30  59° 43°	1  53° 50°	2  64° 61°
3  66° 41°	4  67° 36°	5  -- 39°	6  51° 29°	7  57° 34°	8  60° 46°	9  64° 56°

SAFETY REPORT

- Days without an accident: 95
- Days without lost time: 95

MILESTONE TRACKING

- Construction Start: August 21, 2023
- Current Contract Completion Date: Mar 14, 2025
