

CURRENT CONSTRUCTION ACTIVITIES

LAST WEEK - WEEK ENDING 12/09/2023

- Continue electrical overhead rough-in on level 3.
- Continue mechanical PIU/VAV rough-in on level 3.
- Begin interior framing on level 3.
- Continue mechanical overhead rough-in on level 2.
- Continue slab demolition on the basement.
- Continue joist augmentation on the basement.
- Continue stair 1 steel installation on the roof.
- Continue exterior demo brick/glass/lintel/kicker.
- Continue installing U/G utilities.
- Continue grading at Sally Port.
- Begin preparations for footings at sally port.


THIS WEEK - WEEK ENDING 12/16/2023

- Continue electrical overhead rough-in on level 3.
- Continue mechanical PIU/VAV rough-in on level 3.
- Continue interior framing on level 3.
- Continue mechanical overhead rough-in on level 2.
- Begin fireproofing in basement.
- Continue joist augmentation in basement.
- Continue exterior demo brick/glass/lintel/kicker.
- Begin exterior framing at East elevation.
- Continue installing U/G utilities.
- Begin grading for retaining wall.
- Continue preps for footings at sally port foundation wall and footings for CMU walls at basement.

+ JOBSITE PHOTOS



Continue Mechanical PIU/VAV Rough-In On Level 3

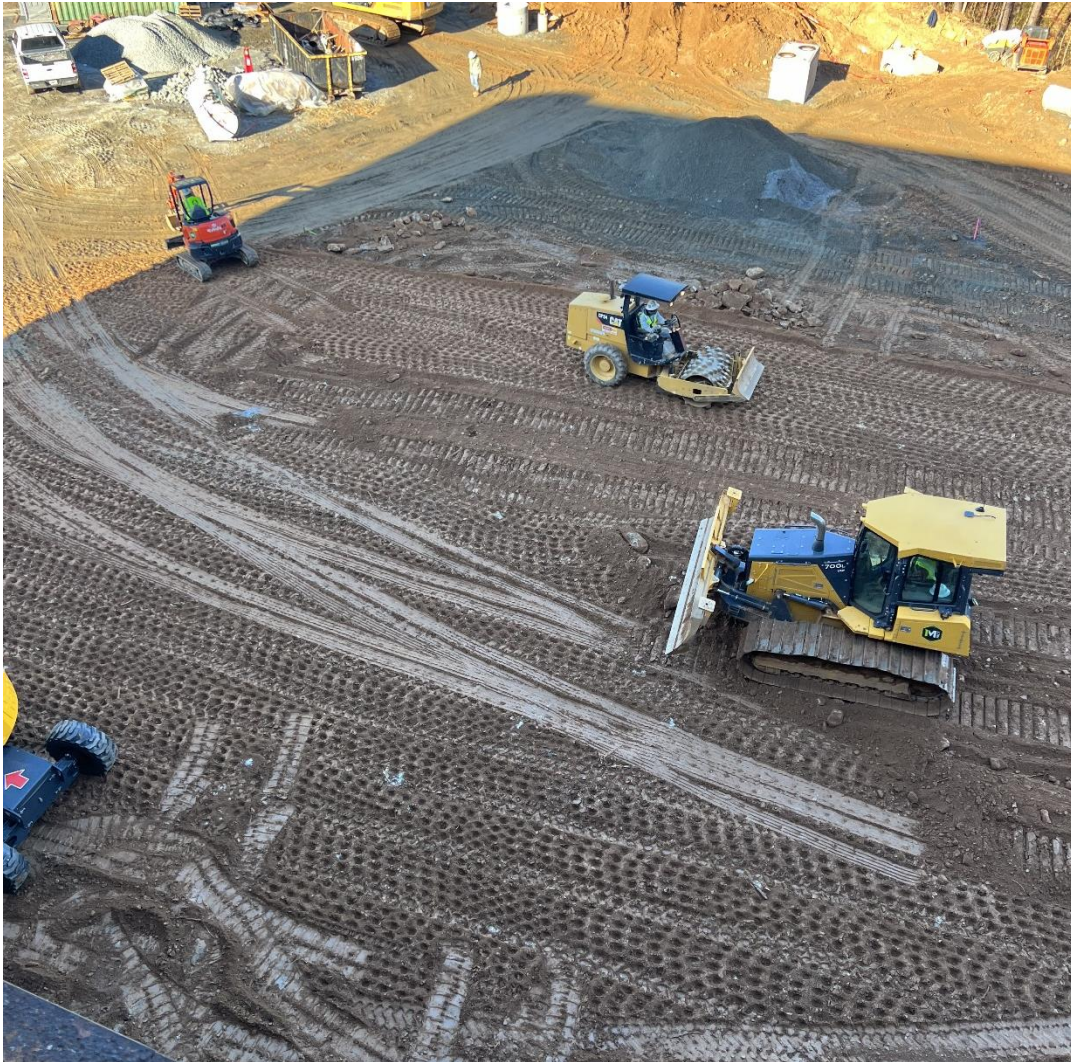

Continue Grading At Sally Port



Continue Exterior Demo Brick/Glass/Lintel/Kicker - North Face



Continue Plumbing Overhead Rough-In On Level 3



Joist Augmentation On Basement




Continue Installing U/G Utilities



Continue Installing U/G Utilities



Mechanical Overhead Rough-in On Level 2

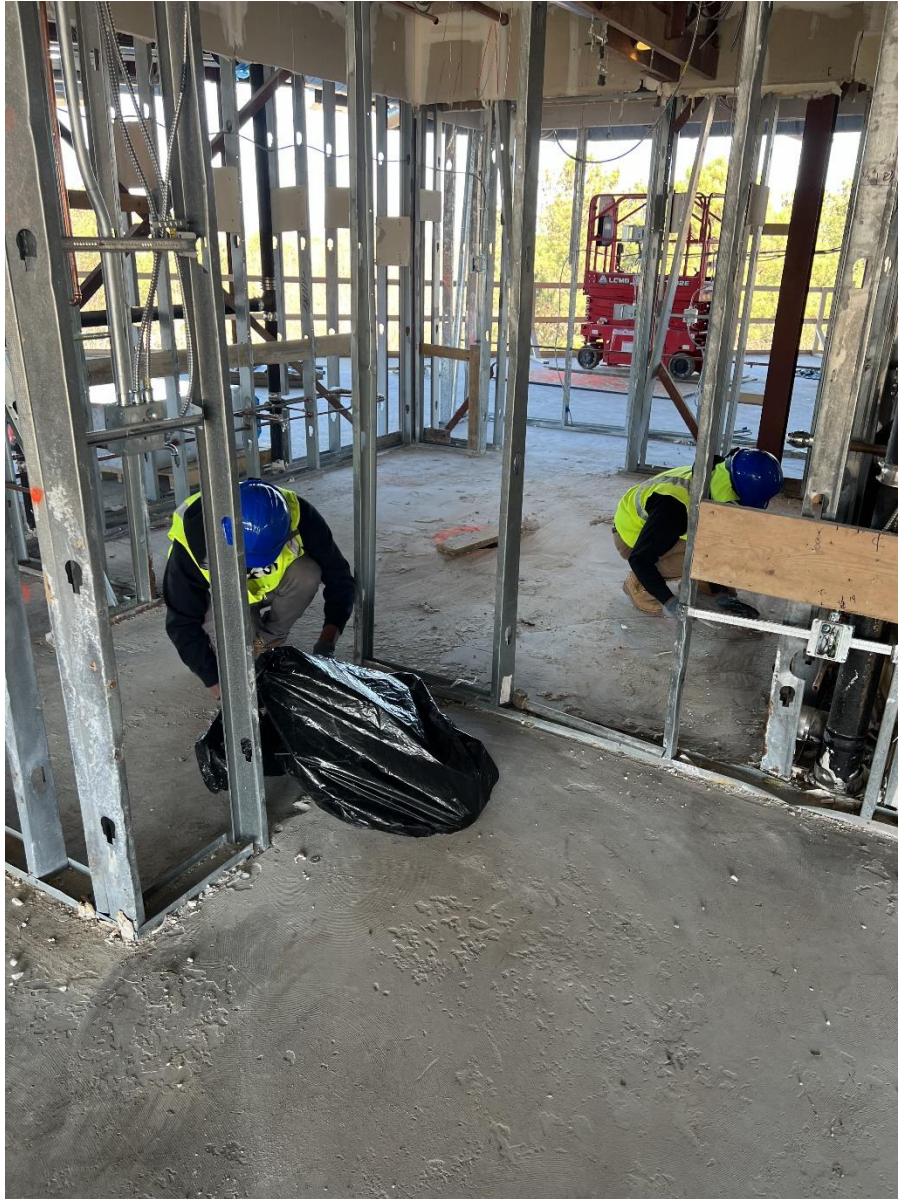















Continue Interior Framing On Level 3



Begin Fireproofing Basement

 WEATHER

Weather delays last week: 0

3  66° 41°	4  67° 36°	5  58° 41°	6  53° 28°	7  59° 34°	8  62° 49°	9  56° 53°
10  59° 31°	11  51° 30°	12  -- 31°	13  58° 38°	14  55° 31°	15  54° 37°	16  55° 45°

SAFETY REPORT

- Days without an accident: 100
- Days without lost time: 100

MILESTONE TRACKING

- Construction Start: August 21, 2023
- Current Contract Completion Date: Mar 14, 2025
