

+ CURRENT CONSTRUCTION ACTIVITIES

LAST WEEK

- Continued Installing RCP Piping for Storm Line
- Completed Bifold Door Installation at Apparatus Bay
- Continued Double-Siding on Second Floor with High Impact Sheet Rock
- Continued Overhead MEP Installation on Second Floor
- Continued Brick Veneer and Cast Stone Installation
- Continued Exterior Hollow Metal Door Installation


THIS WEEK

- Continue Brick Veneer and Cast Stone Installation
- Continue Double-Siding on Second Floor
- Continue Overhead MEP Installation on Second Floor
- Begin Hanging Hard Ceilings
- Continue Fire Sprinkler Head Installation

 JOBSITE PHOTOS



Continued Brick Veneer and Cast Stone Installation

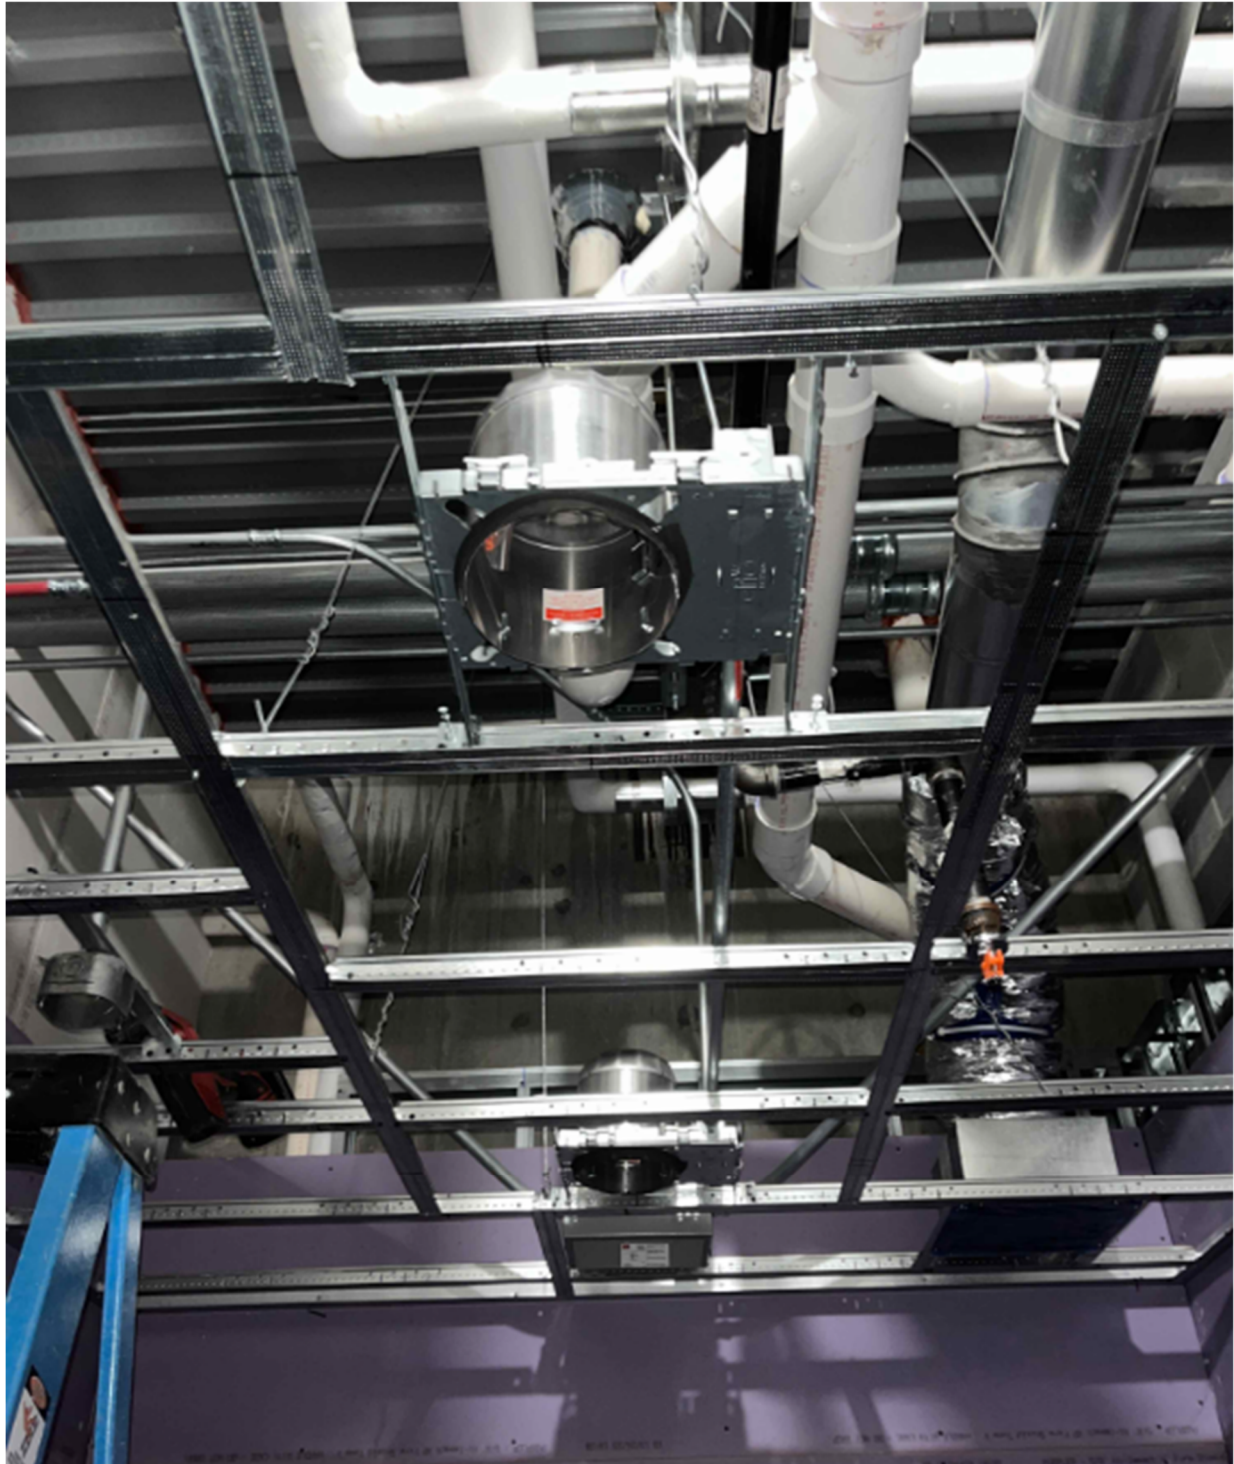















Continued Overhead MEP Installation on Second Floor




Continued Double-Siding on Second Floor with High Impact Sheetrock

WEATHER

Weather delays last week: 0

31  57° 37°	1  46° 27°	2  52° 26°	3  46° 32°	4  53° 28°	5  51° 36°	6  48° 39°
7  48° 28°	8  -- 42°	9  54° 33°	10  46° 30°	11  56° 38°	12  60° 29°	13  42° 26°

MANPOWER

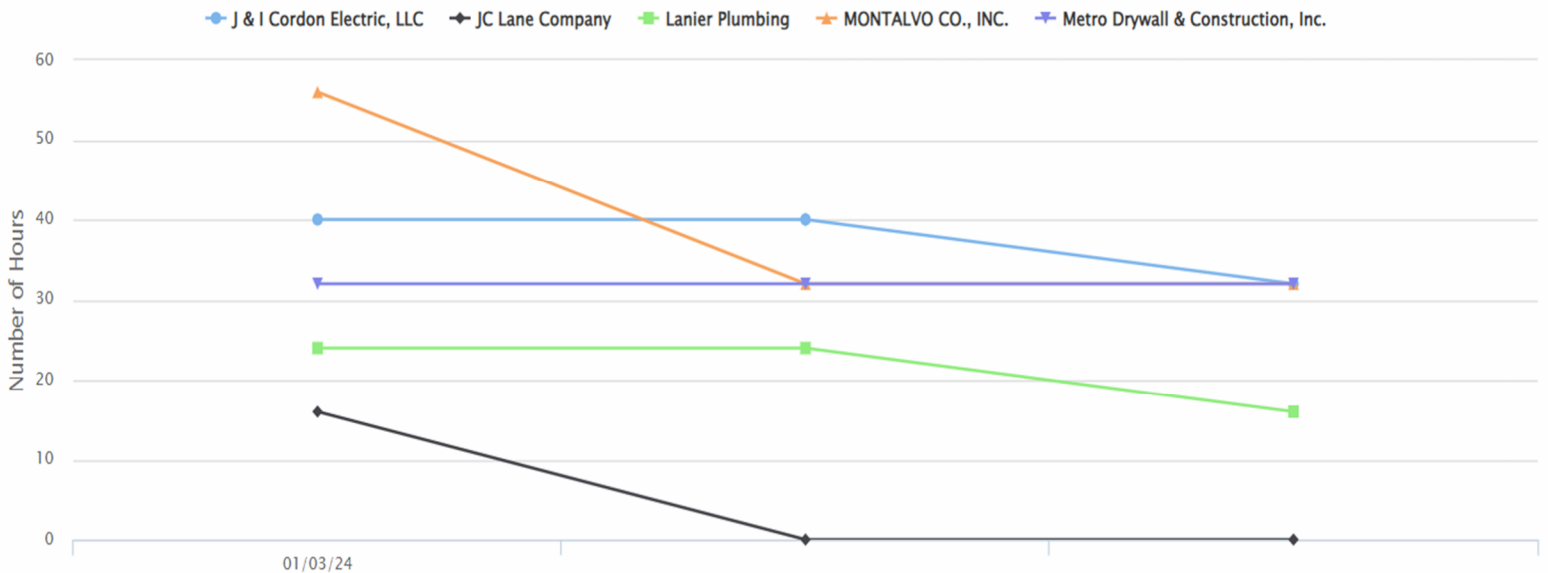

SAFETY REPORT

- Days without an accident: 190
- Days without lost time: 190

MILESTONE TRACKING

- Construction Start: April 10, 2023
- Current Contract Completion Date: June 10, 2024
