

CURRENT CONSTRUCTION ACTIVITIES

LAST WEEK

- Completed Partial SOG Pour at Level 1
- Completed Installation of Foundation Drain
- Began Backfill at Foundation Wall

THIS WEEK

- Receive and Begin Structural Steel at First Floor
- Passed Pressure Test at Spalding Sewer Tie-in
- Complete Pour for Kitchen Slab-on-Grade
- Begin Exterior and Interior CMU Walls
- Begin MEP In-Wall Rough-in
- Continue Foundation Wall Backfill

 JOBSITE PHOTOS



Structural Steel Delivery




Backfill at Foundation Wall



Exterior Concrete Masonry at Level 1


WEATHER

Weather delays last week: 0

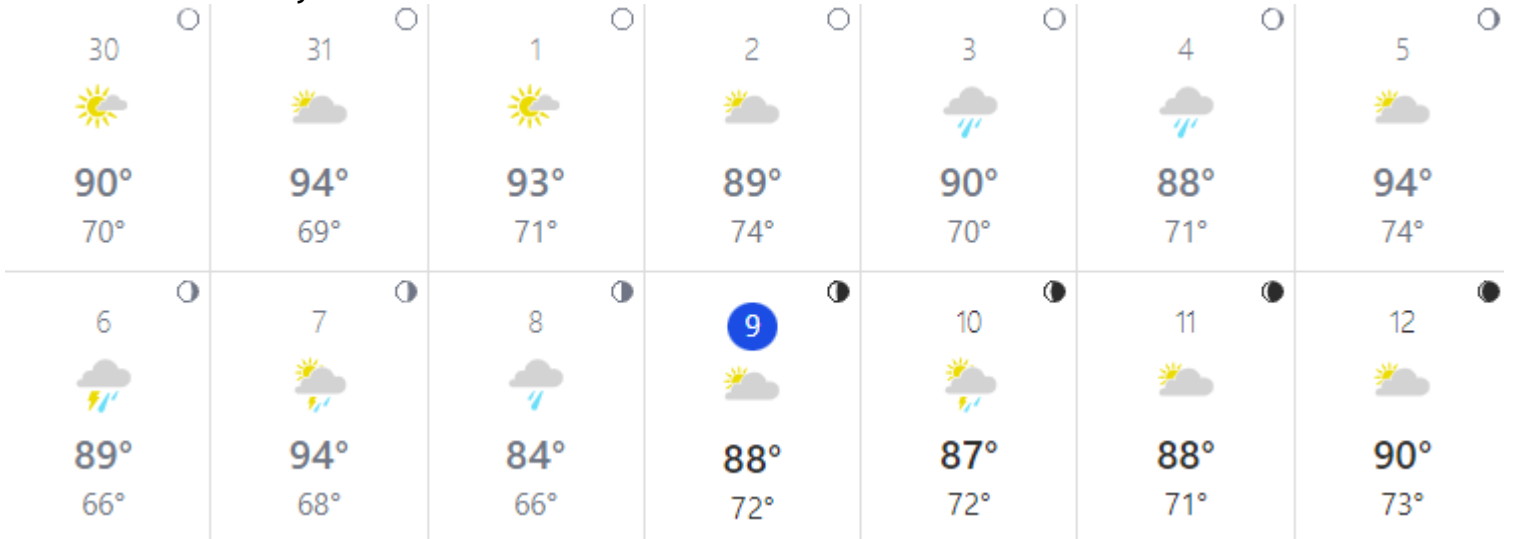

MANPOWER

MANPOWER GRAPH

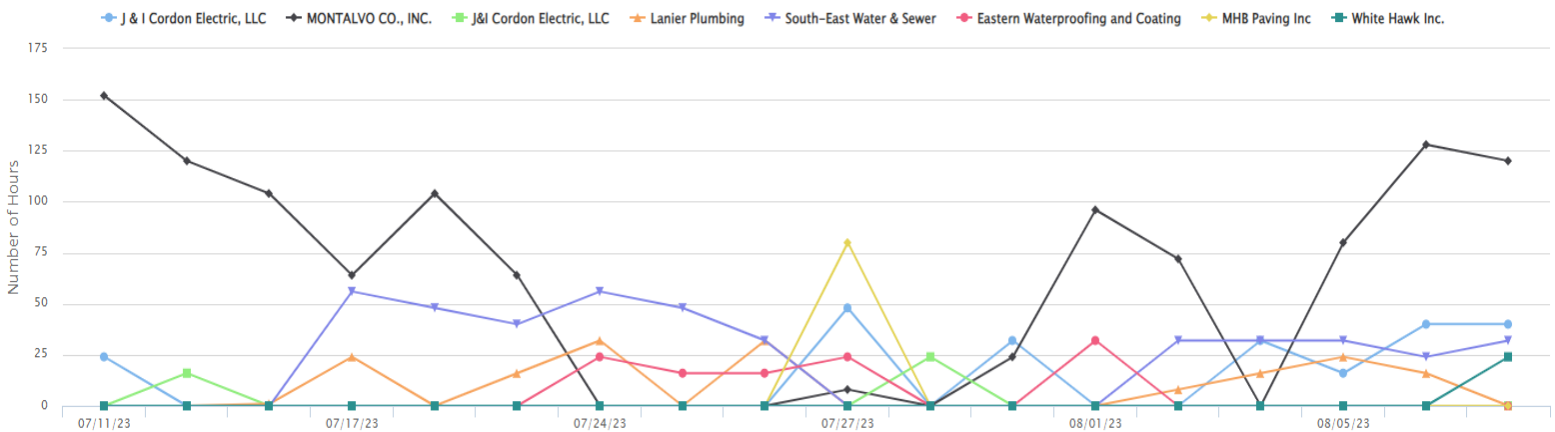

SAFETY REPORT

- Days without an accident: 82
- Days without lost time: 82

MILESTONE TRACKING

- Construction Start: April 10, 2023
- Current Contract Completion Date: June 10, 2023
