

CURRENT CONSTRUCTION ACTIVITIES

LAST WEEK

- Received and Began Shaking Out Structural Steel
- Continued Backfill at Foundation Wall
- Began Interior and Exterior CMU Walls
- Began MEP Interior Wall Rough-in
- Passed Pressure Test at Spalding Sewer Tie-in

THIS WEEK

- Begin Setting Structural Steel
- Continue MEP in-wall Rough-in
- Continue Interior and Exterior CMU Walls
- Continue CIP Lintels at the Apparatus Bay

+ JOBSITE PHOTOS



Exterior CMU Installation at the First Floor




Formwork for CIP Lintels at the Apparatus Bay



Exterior Concrete Masonry/ Rough-in at Level 1

WEATHER

Weather delays last week: 3

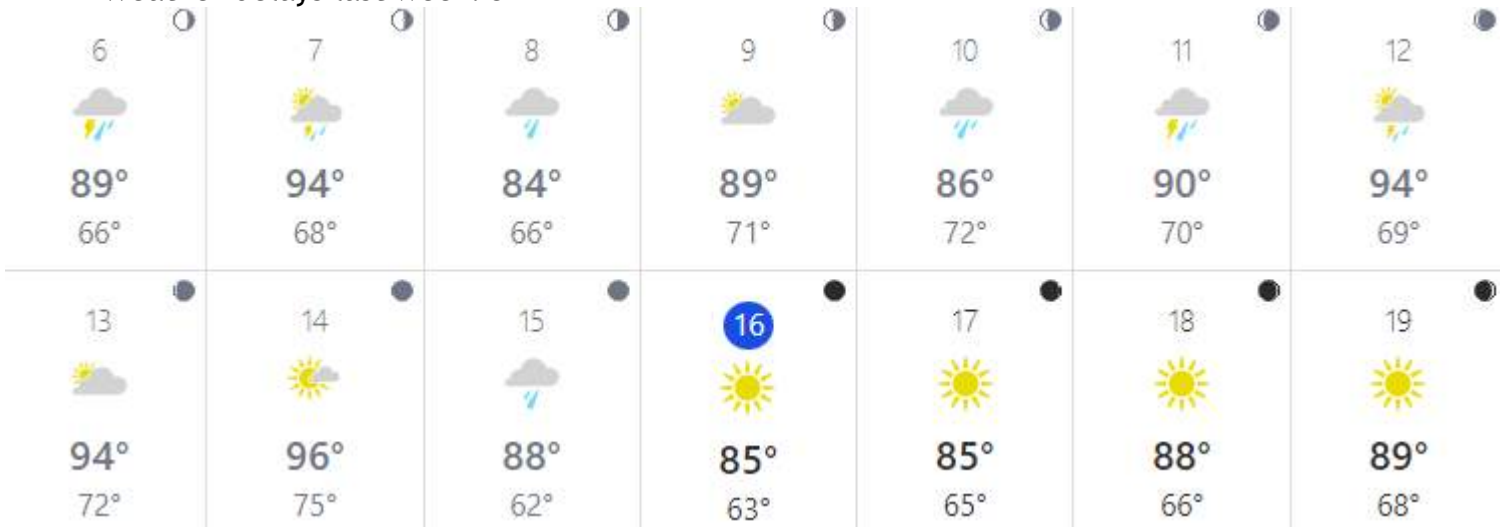

MANPOWER

MANPOWER GRAPH



SAFETY REPORT

- Days without an accident: 87
- Days without lost time: 87

MILESTONE TRACKING

- Construction Start: April 10, 2023
- Current Contract Completion Date: June 10, 2023
