

CURRENT CONSTRUCTION ACTIVITIES

LAST WEEK

- Thanksgiving Lunch for Subs, City, and Fire
- City of Atlanta Completed Water Vault Install
- Began Circuit Board Installation in Generator Room
- Continued Brick and Cast Stone Installation
- Poured Curb and Gutter at Mount Vernon Entrance
- Completed Water Line Installation from Vaults to Building
- Continued MEP Overhead Installation on the Second Floor
- Continued High Impact Sheet Rock Installation

THIS WEEK

- Continue Circuit Board Installation
- Continue Installation of Brick Veneer and Cast Stone
- Continue MEP Overhead Installation on Second Floor
- Continue Sheet Rock Installation
- Timber Truss Delivery
- Continue MEP In-Wall Rough in at the Second Floor

JOBSITE PHOTOS



Poured Curb and Gutter at Mt Vernon Entrance




Continued Brick and Cast Stone Installation




Hosted On-Site Thanksgiving Lunch for Subcontractors, City of Sandy Springs, and Fire Department

WEATHER

Weather delays last week: 0

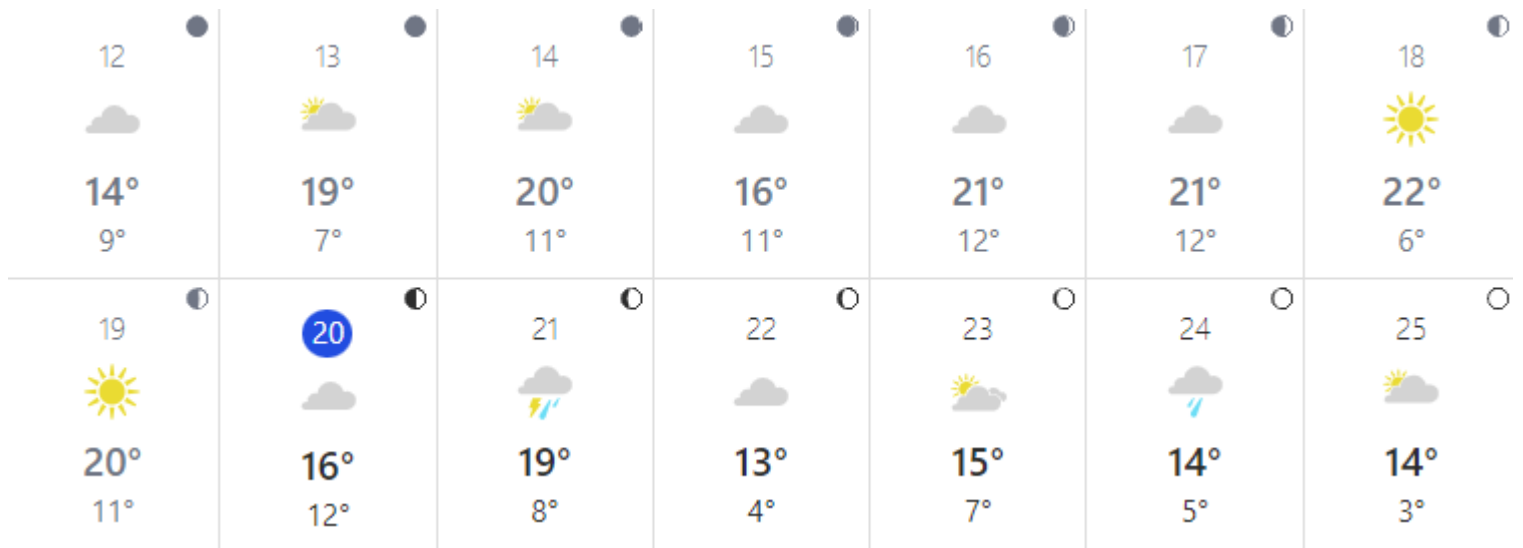

MANPOWER

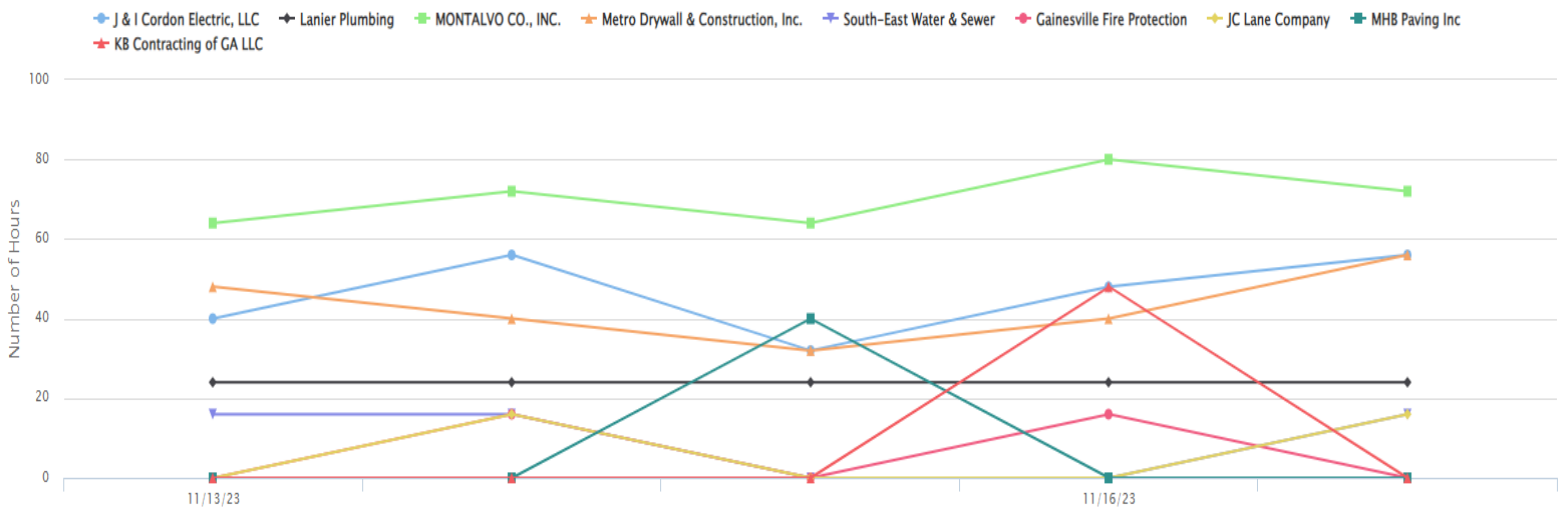

SAFETY REPORT

- Days without an accident: 155
- Days without lost time: 155

MILESTONE TRACKING

- Construction Start: April 10, 2023
- Current Contract Completion Date: June 10, 2024
