

## + CURRENT CONSTRUCTION ACTIVITIES

### LAST WEEK - WEEK ENDING 12/30/2023

---


- MEP Interior wall rough-in completed
- Plumbing and electrical overhead rough-in completed
- Mechanical ductwork run throughout office area
- Trench was poured back for additional restroom; electrical and plumbing in wall rough was complete.
- OCS structure was set; Storm drain tied in at right of way
- Graded the back of site

### THIS WEEK - WEEK ENDING 1/06/2024

---

- GAB delivered for site grading
- Spread GAB & Compacted around back of lot
- HVAC delivery of equipment; Continue HVAC rough-in
- Installation of curb around pond and completion of flumes
- Backfilled behind curb poured to date around back of lot
- Rock hauled off that was found when excavating pond
- Installation of window frames
- Complete pond excavation
- Complete gas line installation from building to gas meter

 JOBSITE PHOTOS

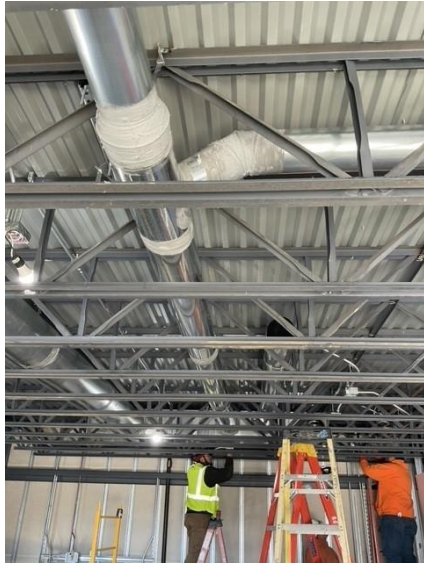

MEP Overhead & In-Wall Rough-In



Added Restroom Concrete Pourback and In-Wall Rough-in





## Pond Excavation



















Site Grading & Compaction, Backfilling Along Curb, Rock Removal

 WEATHER

Weather delays last week: 2

17  53° 40°	18  56° 27°	19  46° 24°	20  52° 26°	21  59° 34°	22  59° 39°	23  66° 41°
24  65° 55°	25  62° 58°	26  61° 49°	27  59° 38°	28  50° 31°	29  46° 32°	30  45° 29°

**\*\*12/25-12/26:** Job site received approximately 1.75” of rain over the course of two days which prevented sitework and site clean up for two additional days (12/26-12/27).

## SAFETY REPORT

- Days without an accident: 99
- Days without lost time: 99

## MILESTONE TRACKING

- Construction Start: August 21, 2023
- Current Contract Completion Date: March 19, 2024
