

## CURRENT CONSTRUCTION ACTIVITIES

### LAST WEEK - WEEK ENDING 12/30/2023

---

- Plumbing & electrical R/I - Level 3
- MEP R/I - Level 2
- Mechanical R/I level 1
- Beam augmentation level 1
- Fireproofing basement
- Interior & exterior framing (interior level 3, exterior at NE elevation)
- Installing U/G storm line "C"
- Saw cutting for footings for new columns in basement
- F/R/P for footings at Sally Port, Interior columns (columns & CMU)
- Exterior demo, demo punch, site clean up

### THIS WEEK - WEEK ENDING 01/06/2024

---

- Plumbing & electrical O/H & in-wall R/I - Level 3
- MEP R/I - Level 2
- Mechanical R/I level 1
- Beam augmentation level 1,2,3
- Fireproofing basement
- Interior & exterior framing/sheathing ( interior level 3, exterior at NE elevation, Interior Level 2)
- Installing U/G storm line "C"
- FRP for Slab tie-ins around interior columns
- Installing U/G storm line "C"
- Waterproofing at Sally Port & Elevator Pit foundation walls
- Sally Port U/G utility rough-in

 JOBSITE PHOTOS



Fireproofing Basement



## Beam Augmentation



Exterior Framing



## Sallyport



### Concrete Work for Interior Columns




Waterproofing Elevator Pit Walls




## Underground Utilities Installation



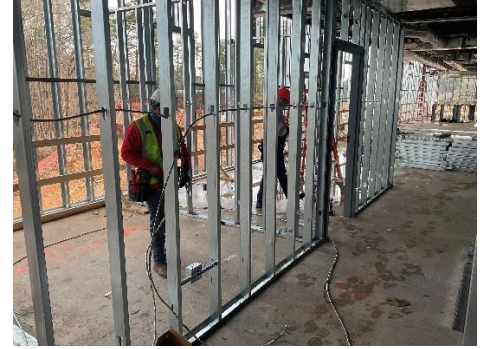



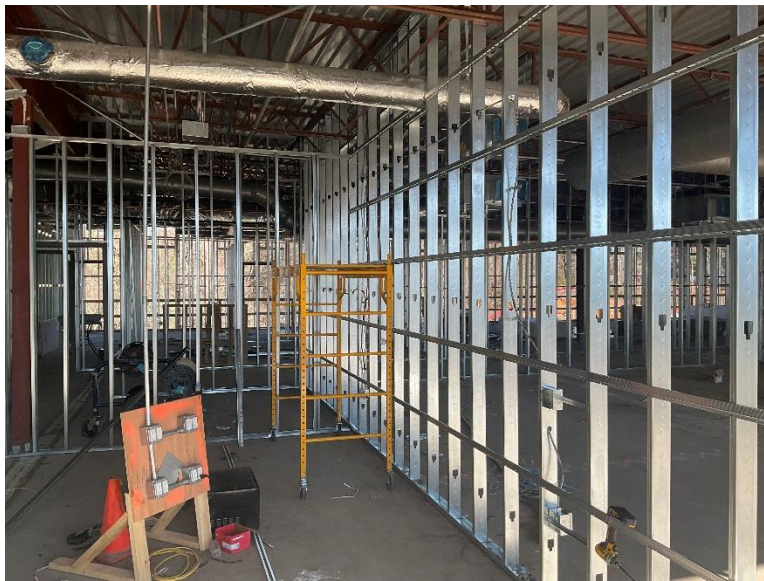











### MEP Rough-in



## Interior Framing

 WEATHER

Weather delays last week: 2

17  53° 40°	18  56° 27°	19  46° 24°	20  52° 26°	21  59° 34°	22  59° 39°	23  66° 41°
24  65° 55°	25  62° 58°	26  61° 49°	27  59° 38°	28  50° 31°	29  46° 32°	30  45° 29°

**\*\*12/25-12/26:** Job site received approximately 1.75” of rain over the course of two days which prevented sitework and site clean up for two additional days (12/26-12/27).

## SAFETY REPORT

- Days without an accident: 117
- Days without lost time: 117

## MILESTONE TRACKING

- Construction Start: August 21, 2023
- Current Contract Completion Date: Mar 14, 2025
