

+ CURRENT CONSTRUCTION ACTIVITIES

LAST WEEK - WEEK ENDING 01/06/2024

- Plumbing & Electrical O/H & In-wall Rough-In - Level 3
- MEP Rough-In - Level 2
- Mechanical Rough-In level 1
- Beam augmentation level 1,2,3
- Fireproofing basement
- Interior & exterior framing/sheathing
 - Interior level 3 & 2; Exterior at NE elevation
- Form / Rebar / Pour for Slab tie-ins around interior columns
- Installing U/G storm line "C"
- Waterproofing at Sally Port & Elevator Pit foundation walls
- Sally Port U/G utility rough-in

THIS WEEK - WEEK ENDING 01/13/2024

- Plumbing & Electrical O/H & In-wall Rough-In - Level 3
- MEP Rough-In - Level 2
- Mechanical Rough-In level 1
- Beam augmentation level 1,2,3
- Fireproofing basement
- Sally Port U/G utility rough-in
- Continue setting interior columns/beams at basement
- Setting first courses of block at CMU walls at Sally Port
- Slab edge remediation
- Metal panel mock-up
- Heavy Civil to install foundation drain at Sally Port FW per RFI 067
- Installing U/G storm line "C"

 JOBSITE PHOTOS



Electrical In-Wall



Fireproofing Basement



Setting Interior Columns/Beams at Basement



Sallyport




Concrete Work for Interior Columns



Waterproofing Elevator Pit Walls



Site Utilities Installation

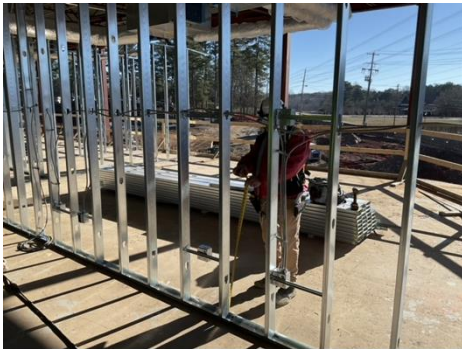

MEP Rough-in

















Interior Framing



Slab Edge Remediation

 WEATHER

Weather delays this week: 1

31  57° 39°	1  48° 27°	2  53° 28°	3  46° 32°	4  55° 31°	5  50° 34°	6  49° 39°
7  48° 29°	8  50° 37°	9  51° 32°	10  46° 31°	11  56° 38°	12  56° 29°	13  43° 25°

- ** SSPHQ jobsite received roughly 2-3” of rain over night and throughout the day (1/8-1/9). With that said, no site work or exterior building work will be completed on 1/9 and possible limited exterior work on 1/10. The amount of work activities at the interior of the building is also limited on 1/9 due to exposed floors to elements and rainwater still coming in through the roof.

SAFETY REPORT

- Days without an accident: 122
- Days without lost time: 122

MILESTONE TRACKING

- Construction Start: August 21, 2023
- Current Contract Completion Date: Mar 14, 2025
