

CURRENT CONSTRUCTION ACTIVITIES

LAST WEEK

- Installed Water Vault and Continued Installing Storm Piping
- Continued Stairwell Ceiling Install
- Continued Double-Siding on Second Floor with High Impact Sheet Rock
- Continued Overhead MEP Installation on Second Floor
- Continued Brick Veneer and Cast Stone Installation
- Continued Exterior Hollow Metal Door Installation

THIS WEEK

- Continue Brick Veneer and Cast Stone Installation
- Continue Double-Siding on Second Floor
- Continue Overhead MEP Installation on Second Floor
- Continue Hanging Hard Ceilings
- Continue Fire Sprinkler Head Installation
- Continue Hollow Metal Door Installation

 JOBSITE PHOTOS



Installed Water Vault and Continued Storm Piping




Began Installing Exterior Brick Columns



Continued Installing Hard Ceiling in Stairwell


WEATHER

Weather delays last week: 0

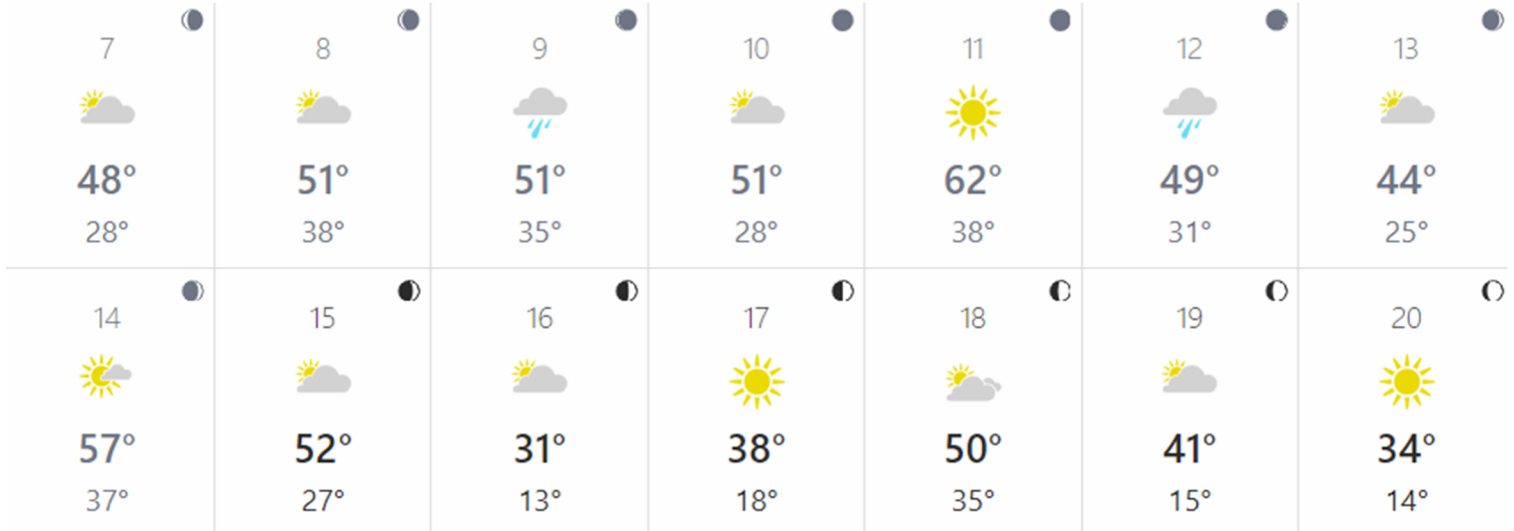

MANPOWER

◆ Gainesville Fire Protection
 ◆ J & I Cordon Electric, LLC
 ◆ JC Lane Company
 ◆ MONTALVO CO., INC.
 ◆ Metro Drywall & Construction, Inc.
 ◆ Lanier Plumbing
◆ South-East Water & Sewer

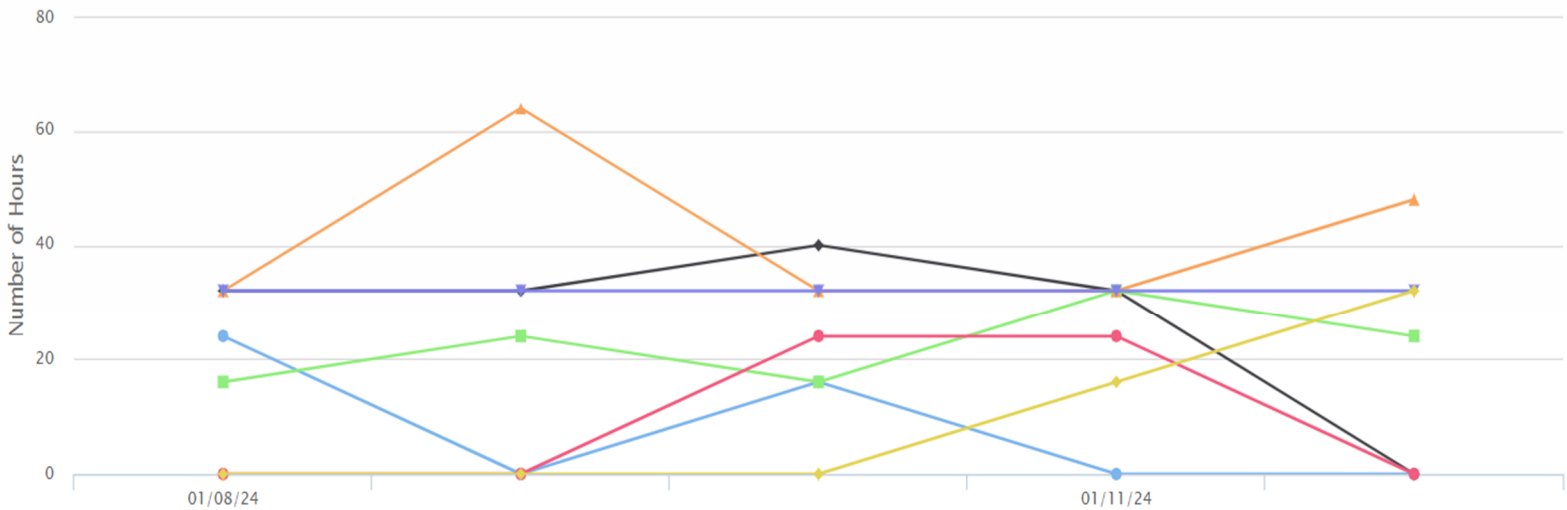

SAFETY REPORT

- Days without an accident: 195
- Days without lost time: 195

MILESTONE TRACKING

- Construction Start: April 10, 2023
- Current Contract Completion Date: June 10, 2024
