

+ CURRENT CONSTRUCTION ACTIVITIES

LAST WEEK

- Completed Water Vault Installation
- Began Prepping Footings for Screen Wall
- Began Prepping Parking Lot for Permeable Pavers
- Began Mudding on First and Second Floor
- Continued Overhead MEP Installation on Second Floor
- Continued Brick Veneer and Cast Stone Installation
- Continued Hollow Metal Door Installation

THIS WEEK

- Continue Brick Veneer and Cast Stone Installation
- Continue Mudding on First and Second Floor
- Continue Screen Wall Footer Installation
- Continue Hanging Hard Ceilings
- Continue Prep for Permeable Pavers at Mt Vernon Parking
- Begin Installing Glass in all Door Frames
- Continue Hollow Metal Door Installation

 JOBSITE PHOTOS



Began Prepping Parking Lot for Permeable Pavers




Began Mudding on First and Second Floor





Began Prepping Screen Wall Footings


WEATHER

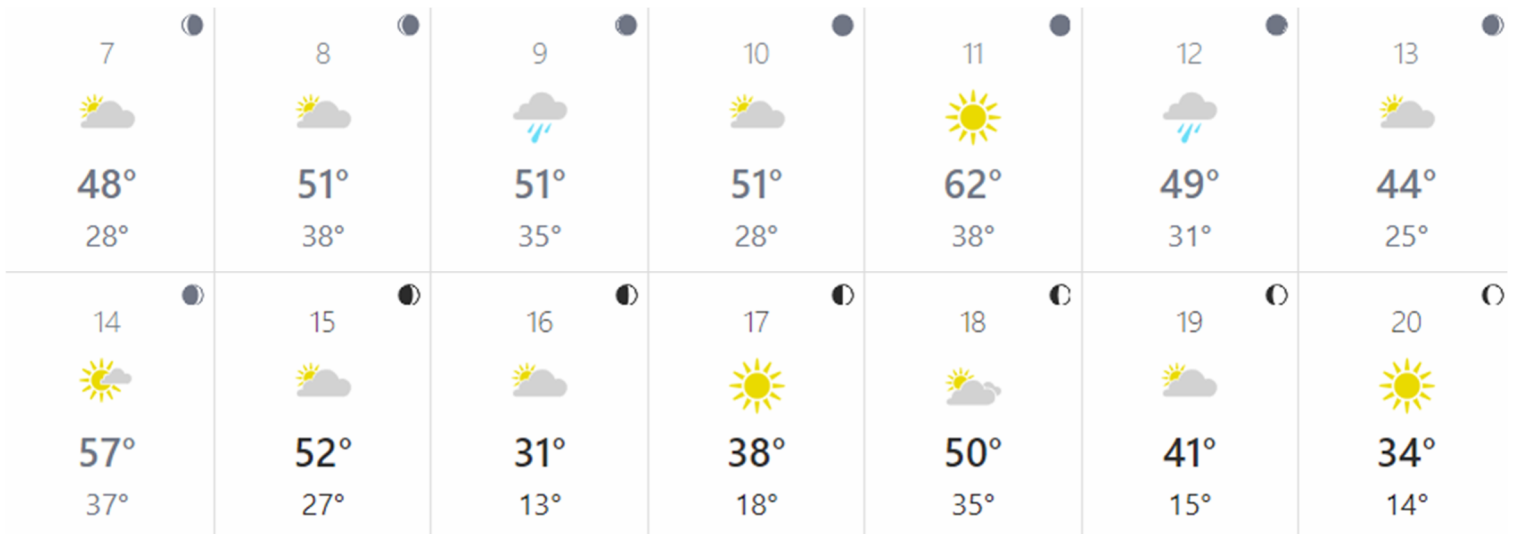Weather delays last week: 0



MANPOWER

 J & I Cordon Electric, LLC
  Lanier Plumbing
  MONTALVO CO., INC.
  South-East Water & Sewer
  Davis Engineering & Surveying, LLC
  GC&E Systems Group, LLC
  JC Lane Company
  Metro Drywall & Construction, Inc.

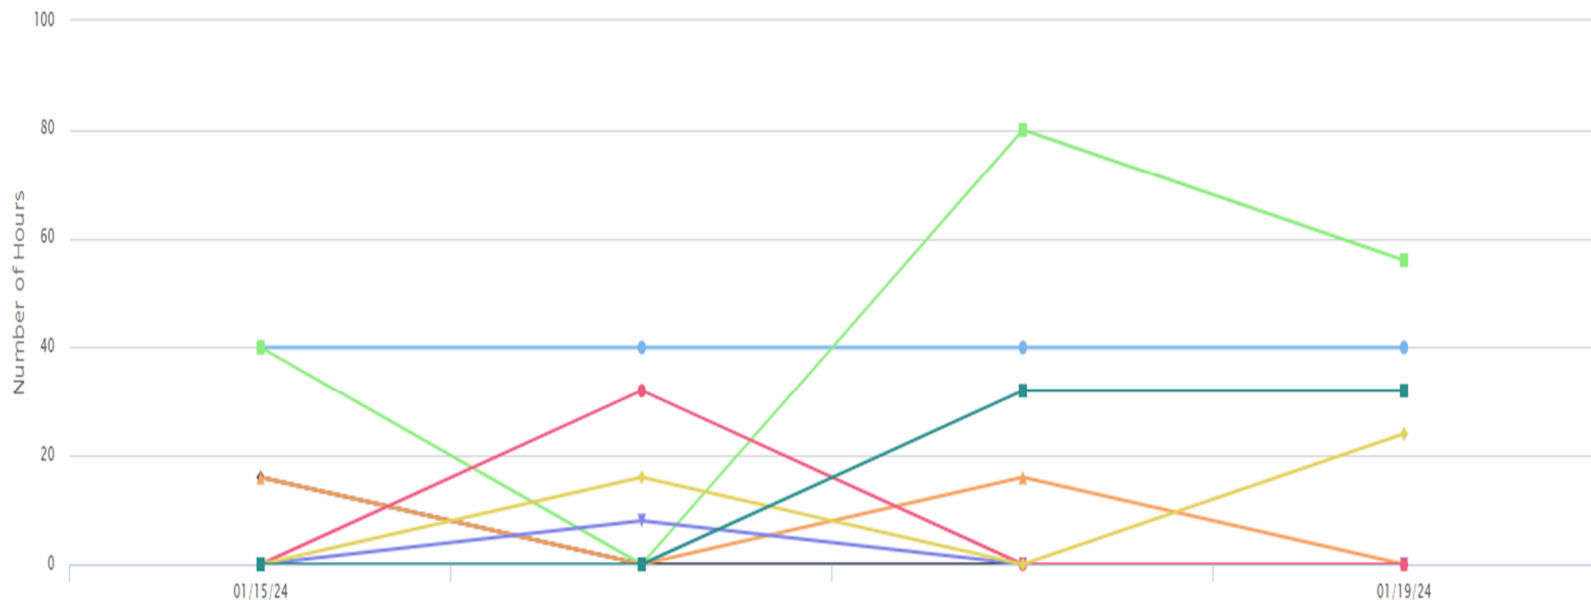

SAFETY REPORT

- Days without an accident: 200
- Days without lost time: 200

MILESTONE TRACKING

- Construction Start: April 10, 2023
- Current Contract Completion Date: June 10, 2024
