

+ CURRENT CONSTRUCTION ACTIVITIES

LAST WEEK

- Began Priming for Paint on First Floor
- Continued Mudding on Second Floor
- Completed Permeable Pavers Installation at Mt Vernon Parking
- Continued Screen Wall Installation
- Poured Curb and Gutter at Spalding Dr Entrance
- Continued Brick Veneer and Cast Stone Installation
- Began Prepping Spalding Dr Entrance for Concrete

THIS WEEK

- Continue Brick Veneer and Cast Stone Installation
- Begin Painting on First Floor
- Continue Wall Finishing for Primer and Paint on Second Floor
- Continue Screen Wall Installation
- Continue Concrete Apron Installation at Spalding Dr and Apparatus Bay
- Begin Installing Acoustical Ceiling on First Floor

 JOBSITE PHOTOS



Continued Screen Wall Installation




Began Priming for Paint on First Floor



Began Prepping for Concrete Apron at Spalding Dr Entrance and Apparatus Bay


WEATHER

Weather delays last week: 0

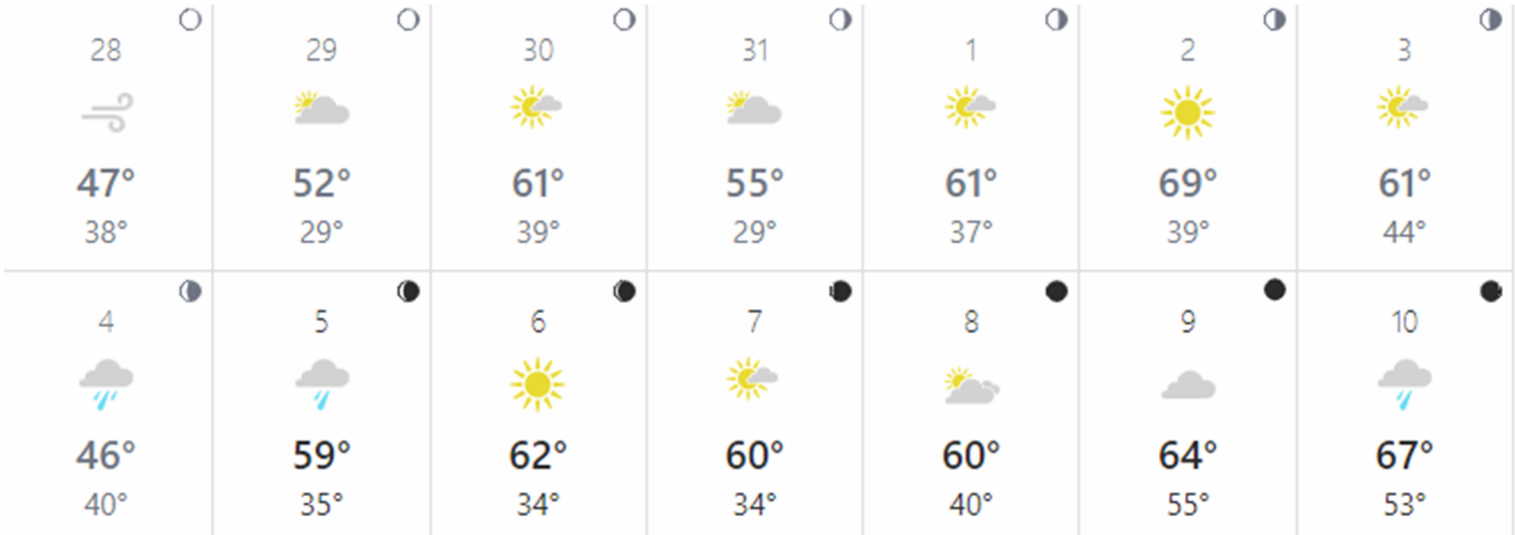

MANPOWER

- J & I Cordon Electric, LLC
- MONTALVO CO., INC.
- Metro Drywall & Construction, Inc.
- Paverstone Construction
- Performance Construction Services, LLC
- JC Lane Company
- South-East Water & Sewer
- KB Contracting of GA LLC
- Lanier Plumbing
- Terminus Construction Group
- Southern Painting LLC

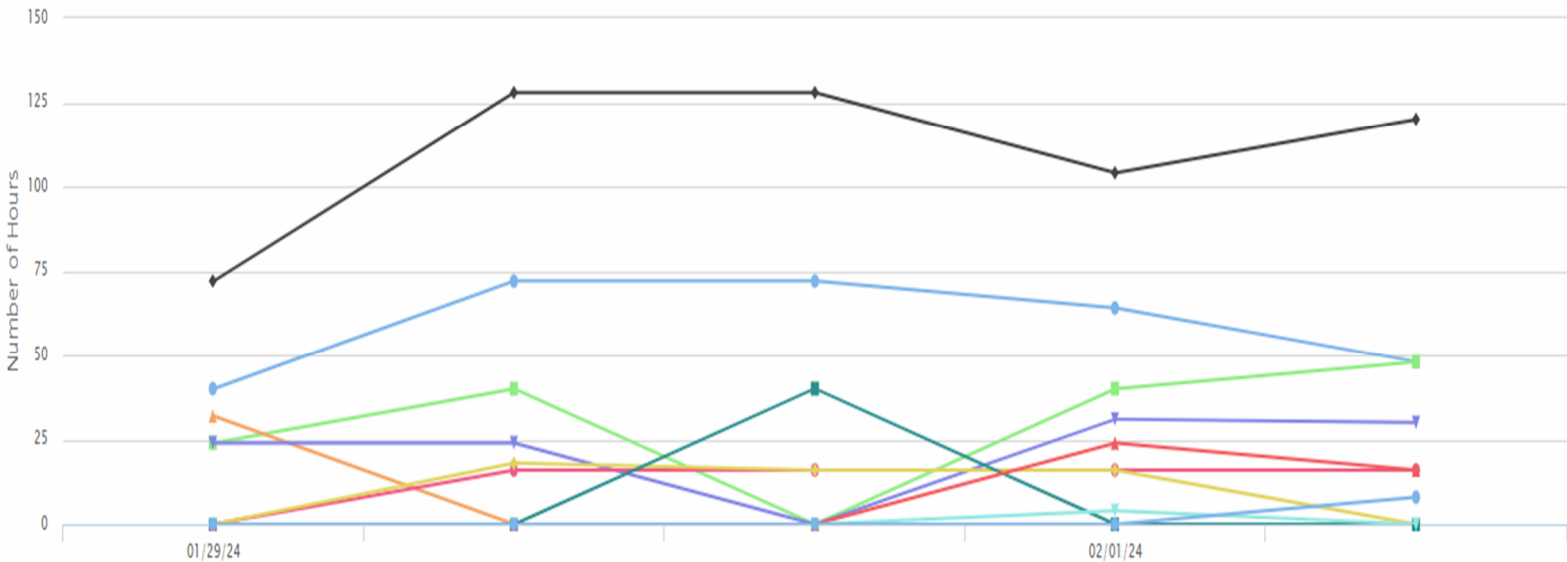

SAFETY REPORT

- Days without an accident: 210
- Days without lost time: 210

MILESTONE TRACKING

- Construction Start: April 10, 2023
- Current Contract Completion Date: June 10, 2024
