

CURRENT CONSTRUCTION ACTIVITIES

LAST WEEK

- Poured Concrete Driveway to Apparatus Bay
- Began Trench Drain and Concrete Apron at Spalding Entrance
- Continued interior Primer and Paint
- Continued Installing Brick Veneer and Cast Stone Pillars for Site Fence
- Continued Screen Wall Installation
- Continued Brick Veneer and Cast Stone Installation on Building
- Continued Acoustical Ceiling and Fixture Installation
- Began Installing Fiber Cement Soffit and Siding


THIS WEEK

- Continue Trench Drain and Concrete Apron at Spalding Entrance
- Finish Interior Paint and Primer
- Continue Installation of Site Fence Pillars
- Finish Screen Wall Installation
- Continue Trench Drain and Concrete Apron at Spalding Drive
- Continue Installing Acoustical Ceiling and Lighting Fixtures
- Continue Installing Fiber Cement Soffit and Siding
- Finish Brick Install on Building

 JOBSITE PHOTOS



Continued Installing Brick Veneer and Cast Stone Pillars for Site Fence

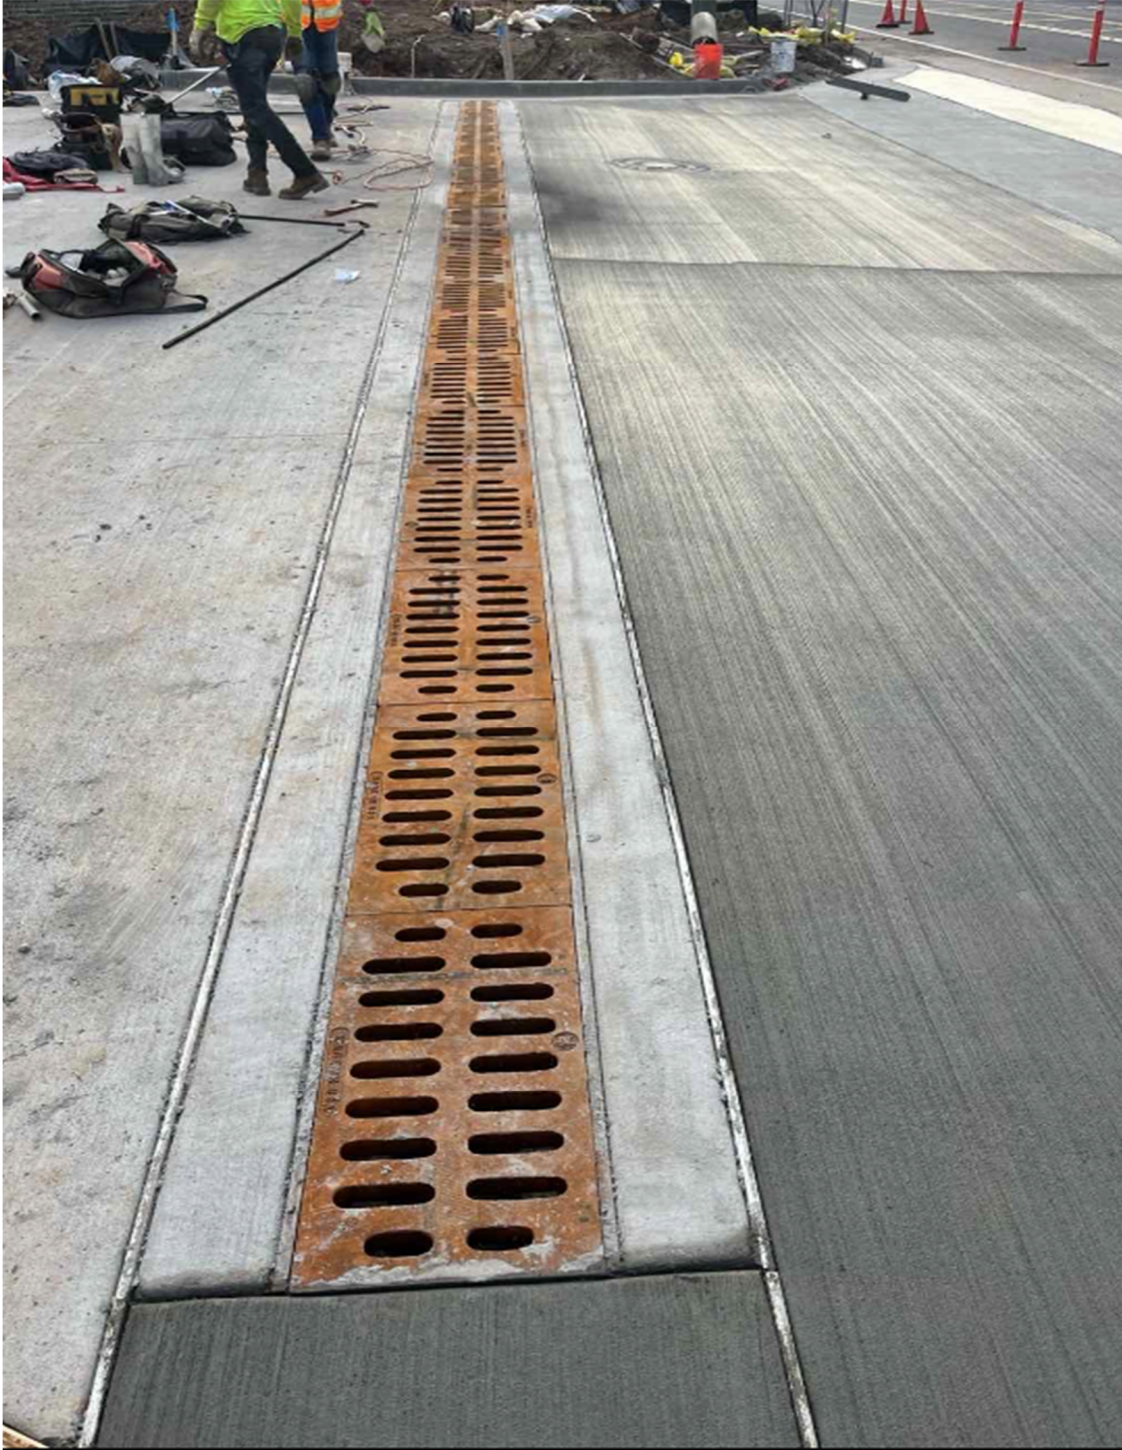


Began Trench Drain and Concrete Apron Install at Spalding Entrance









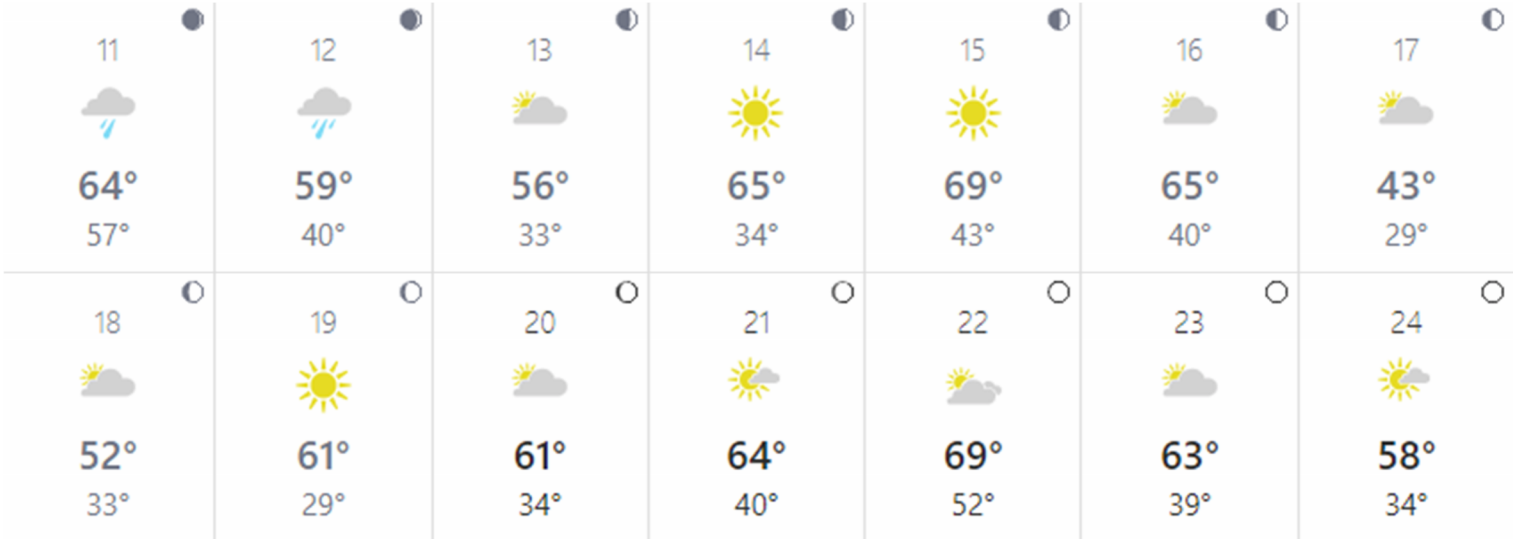


Began Installing Fiber Cement Soffit and Siding


WEATHER

Weather delays last week: 0



MANPOWER

 J & I Cordon Electric, LLC
  Metro Drywall & Construction, Inc.
  MONTALVO CO., INC.
  NetPlanner Systems, Inc.
  Performance Construction Services, LLC
  KB Contracting of GA LLC
  Lanier Plumbing
 South-East Water & Sewer
  Gainesville Fire Protection

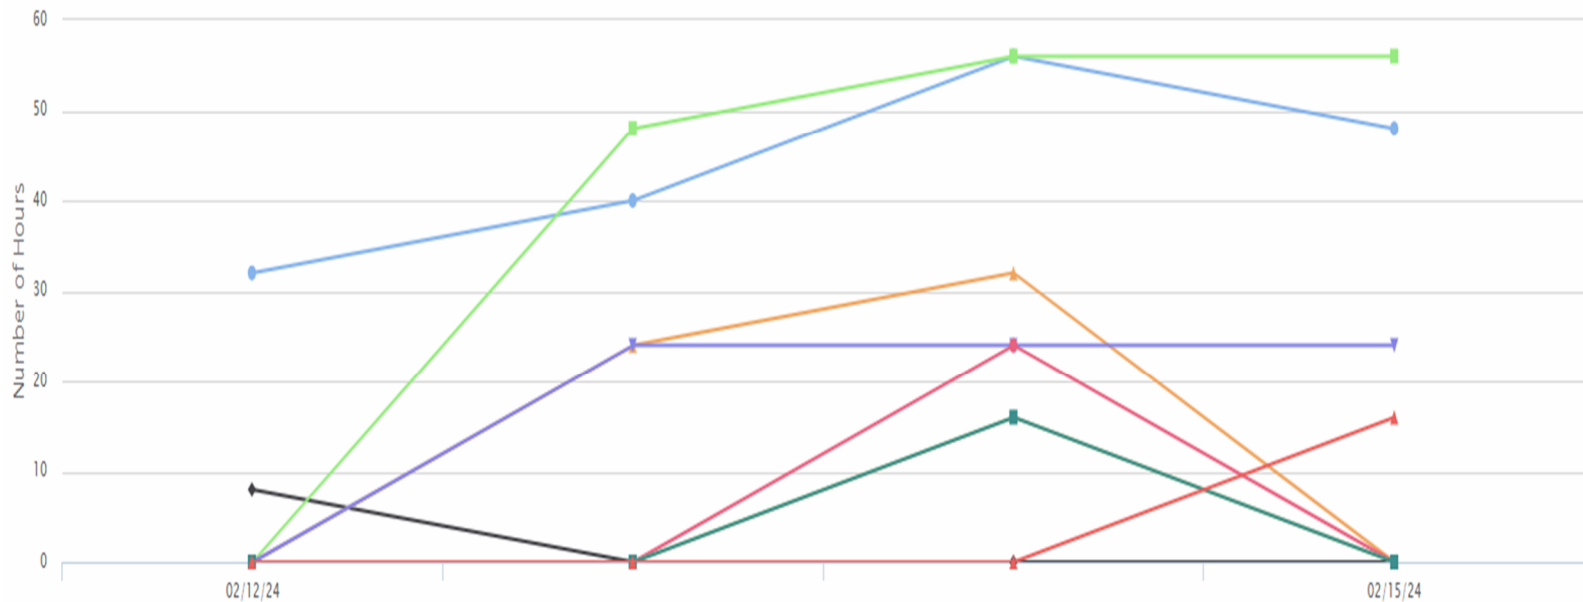

SAFETY REPORT

- Days without an accident: 220
- Days without lost time: 220

MILESTONE TRACKING

- Construction Start: April 10, 2023
- Current Contract Completion Date: June 10, 2024
