

CURRENT CONSTRUCTION ACTIVITIES

LAST WEEK

- Completed Insulated Hard Ceilings Installation on First Floor
- Completed Installation of Brick Veneer and Cast Stone Tops at Site Fence Pilasters
- Continued Installation of Remaining Brick Veneer and Cast Stone Surrounds on the Building
- Continued Sub-Framing and Fiber Cement Soffit and Siding Installation
- Continued Duct Work on Second Floor
- Continued Acoustical Ceiling Installation on Second Floor
- Continued Fixture and Lighting Installation on First and Second Floor
- Continued Interior Prep and Primer for Paint on Second Floor
- Continued Grading at Mt Vernon and Adjacent Sides of Building
- Began Grading at Spalding Side of Building
- Began Prepping Bathrooms for Wall Tile

THIS WEEK

- Continue Sub-Framing and Fiber Cement Soffit and Siding Installation
- Continue Acoustical Ceiling Installation on Second Floor
- Continue Fixture and Lighting Installation on Second Floor
- Continue Interior Prep and Primer for Paint on Second Floor
- Continue Grading Throughout the Project Site
- Continue Fire Pole Installation
- Begin Installing Wall Tile in the First Floor Bathrooms
- Begin Installing Grease Duct at Chimney
- Begin Installing Sidewalks at Spalding Dr

 JOBSITE PHOTOS



Completed Installation of Insulated Hard Ceilings on First Floor




Continued Grading Throughout the Project Site



Continued Sub-Framing and Fiber Cement Soffit and Siding Installation


WEATHER

Weather delays last week: 0

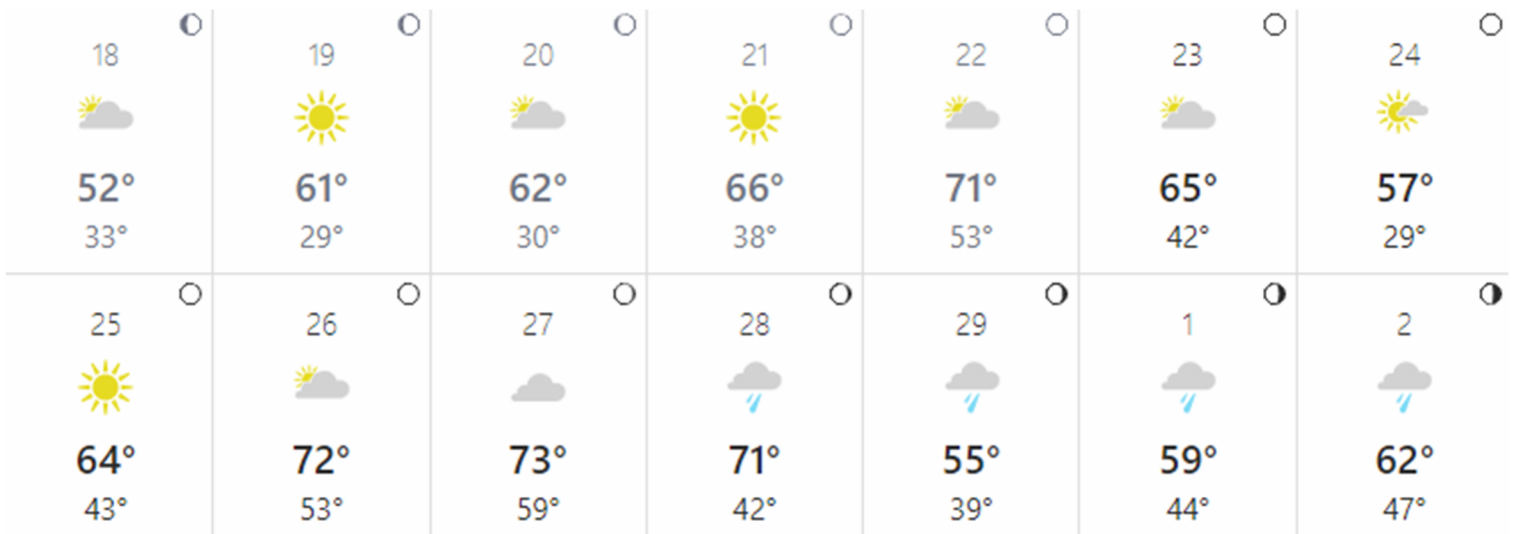

MANPOWER

- ◆ Gainesville Fire Protection
- ◆ J & I Cordon Electric, LLC
- ◆ MONTALVO CO., INC.
- ◆ NetPlanner Systems, Inc.
- ◆ Performance Construction Services, LLC
- ◆ South-East Water & Sewer
- ◆ JC Lane Company
- ◆ Metro Drywall & Construction, Inc.
- ◆ Eastern Waterproofing and Coating
- ◆ Lanier Plumbing
- ◆ Florworx of Atlanta, LLC
- ◆ Peach State Builders, Inc.

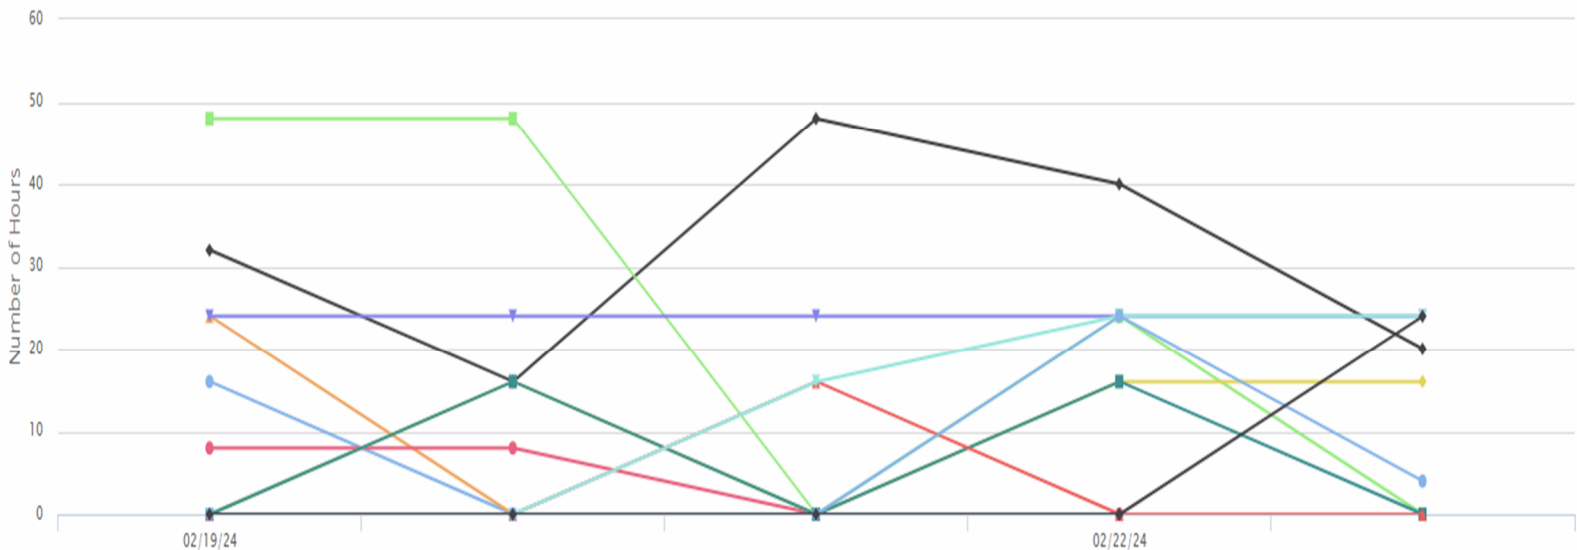

SAFETY REPORT

- Days without an accident: 225
- Days without lost time: 225

MILESTONE TRACKING

- Construction Start: April 10, 2023
- Current Contract Completion Date: June 10, 2024
