

CURRENT CONSTRUCTION ACTIVITIES

LAST WEEK - WEEK ENDING 01/13/2024

- Plumbing & Electrical O/H & In-wall Rough-In - Level 3
- MEP Rough-In - Level 2
- Mechanical Rough-In level 1
- Beam augmentation level 1,2,3
- Fireproofing basement
- Sally Port U/G utility rough-in
- Continue setting interior columns/beams at basement
- Setting first courses of block at CMU walls at Sally Port
- Slab edge remediation
- Metal panel mock-up
- Heavy Civil to install foundation drain at Sally Port FW per RFI 067
- Installing U/G storm line "C"


THIS WEEK - WEEK ENDING 01/20/2024

- Plumbing & electrical O/H & in-wall R/I - Level 3
- MEP R/I - Level 2
- Mechanical R/I level 1
- Joist web member augmentation level 1,2,3
- Fireproofing basement
- Sally Port U/G utility rough-in
- Installing U/G storm line "C"
- Interior & exterior framing/sheathing
 - Interior levels 2 & 3; exterior at South elevation
- Bring Court/Admin Wing up to grade
- Begin E/F/R for footings at Court/Admin wing
- Back Fill at Sally Port foundation wall
- Existing CMU wall remediation
- U/G Sanitary Line replacement at basement

JOBSITE PHOTOS



Electrical Rough-In

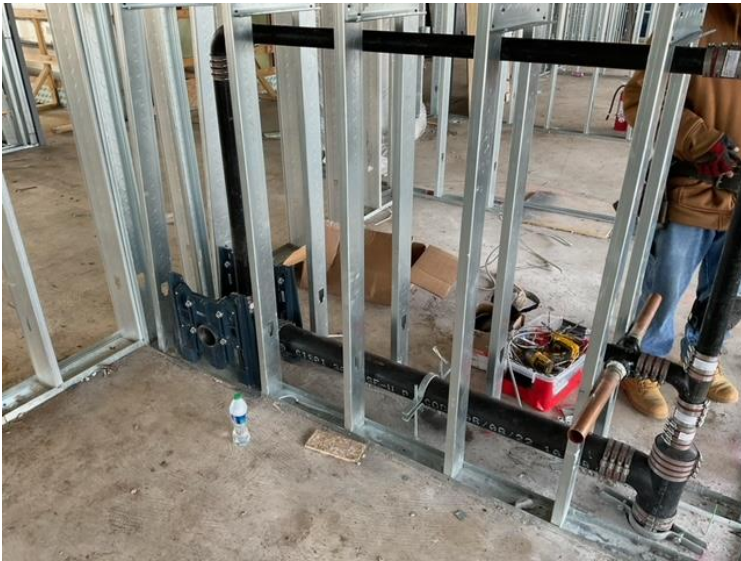

Plumbing Rough-In



Fireproofing Basement



Mechanical Rough-In



CMU First Courses At Sally Port



Joist Web Member Augmentation



CMU First Courses Interior Footings

















Interior Framing



Exterior Framing

 WEATHER

Weather delays this week: 1

7  48° 29°	8  50° 37°	9  53° 35°	10  49° 28°	11  61° 37°	12  46° 32°	13  44° 26°
14  56° 37°	15  60° 33°	16  31° 13°	17  38° 19°	18  48° 36°	19  42° 15°	20  34° 14°

- **SSPHQ jobsite received roughly .56” of rain overnight (1/15-/16) causing the site to be muddy thus not allowing site work to continue 1/16. Also, with the rain and freezing temperatures through out the day (1/16) certain areas of the building are deemed unsafe to work in due to ice on the floor causing a slip hazard.
- Total Weather Delays: 4

SAFETY REPORT

- Days without an accident: 127
- Days without lost time: 127

MILESTONE TRACKING

- Construction Start: August 21, 2023
- Current Contract Completion Date: Mar 14, 2025
