

+ CURRENT CONSTRUCTION ACTIVITIES


LAST WEEK - WEEK ENDING 01/20/2024

- Plumbing & Electrical O/H & In-wall R/I - Level 3
- MEP R/I - Level 2
- Mechanical R/I level 1
- Joist web member augmentation level 1,2,3
- Fireproofing basement
- Installing U/G storm line "C"
- Interior & exterior framing/sheathing
 - Interior level 2 & 3; Exterior at South elevation
- Existing CMU wall remediation
- Excavating for detention pond area

THIS WEEK - WEEK ENDING 01/27/2024

- Plumbing & Electrical O/H & In-wall R/I - Level 3
- MEP R/I - Level 2
- Mechanical R/I level 1
- Plumbing Stack line remediation
- Joist web member & beam augmentation level 1,2,3
- Interior & exterior framing/sheathing
 - Exterior at South/Southeast elevation; Interior Level 2
- U/G Sanitary Line replacement at basement
- Setting geo-fabric, #57 stone, & perforated CMP for detention pond.
- Chiller Tank drained via Environmental Remedies

JOBSITE PHOTOS

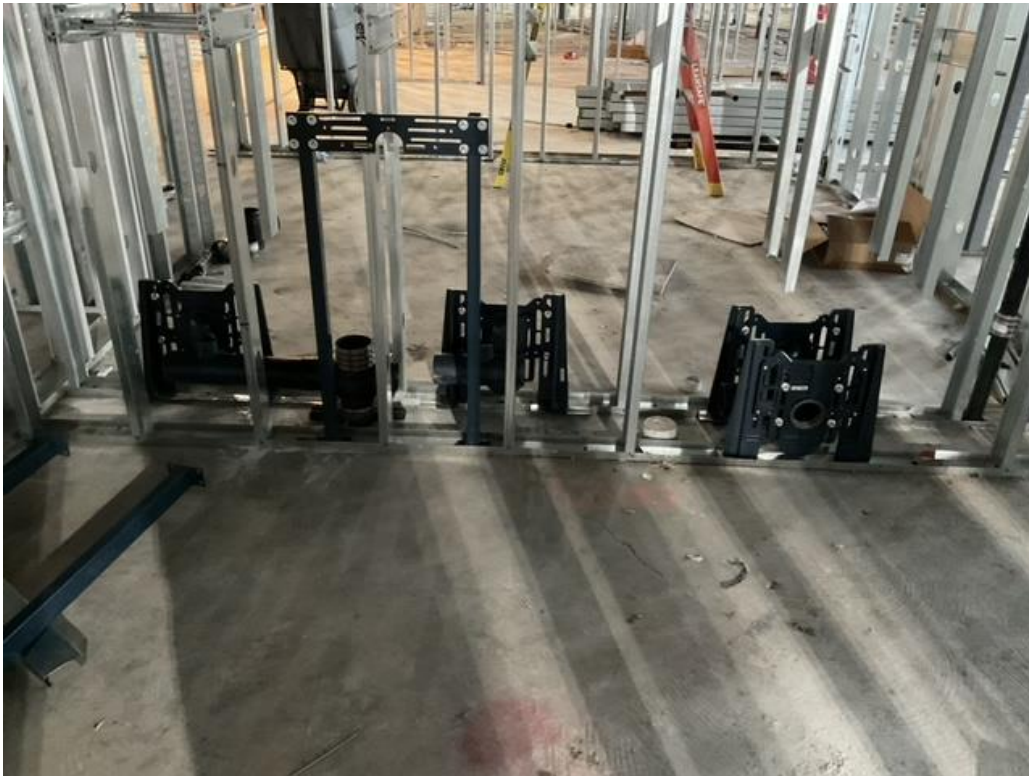

In Wall Plumbing Rough-In



Plumbing Rough-In



Fireproofing Basement



Mechanical Rough-In



CMU Wall Remediation




Joist Web Member Augmentation



CMU First Courses Interior Footings



Interior Framing

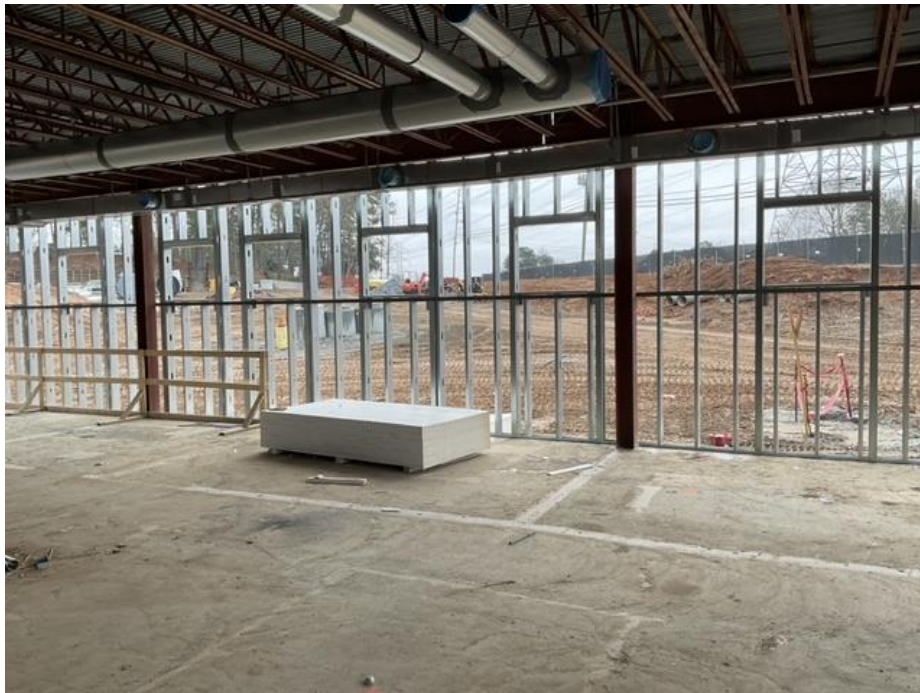

Exterior Framing

















Installation Of 96" Underground Detention Pond



Electrical Rough-In

 WEATHER

Weather delays this week: 0

14  56° 37°	15  60° 33°	16  34° 11°	17  37° 20°	18  51° 38°	19  41° 15°	20  31° 11°
21  41° 25°	22  48° 38°	23  48° 45°	24  55° 54°	25  67° 60°	26  68° 58°	27  65° 46°

- ** We do anticipate delays the second half of the week of 1/26 due to forecasted weather.
- Total Weather Delays: 4

SAFETY REPORT

- Days without an accident: 132
- Days without lost time: 132

MILESTONE TRACKING

- Construction Start: August 21, 2023
- Current Contract Completion Date: Mar 14, 2025
