

CURRENT CONSTRUCTION ACTIVITIES

LAST WEEK - WEEK ENDING 02/03/2024

- Plumbing & Electrical O/H & In-wall R/I - Level 3
- MEP O/H R/I - Level 2
- Mechanical & Electrical O/H R/I - Level 1
- Mechanical O/H R/I - Basement
- Relocation of fire lines that conflicted with structure and/or HVAC duct
- Existing plumbing stack line remediation
- Joist web member & beam augmentation - Level 1,2,3
- Interior & exterior framing/sheathing
 - Exterior - Plan North elevation & radiuses
 - Interior - Level 2
- Completed installation of geo-fabric, 57 stone, & 96" perforated CMP for 160'x21' detention pond
- Main Drilling & Boring conducted test drilling at future Sanitary sewer line location 1/29-1/30 to measure depth and density of present rock. This work was performed under Reeves Young Heavy Civil.
- Additional hand rails installed as needed - Level 1


THIS WEEK - WEEK ENDING 02/10/2024

- Plumbing & Electrical O/H & in-wall R/I - Level 3
- Mechanical tie -in (PIU-VAV) - Level 3
- MEP O/H R/I - Levels 1 & 2
- Existing plumbing stack line remediation
- Installing brick lintels/kickers at radiuses & beam augmentation - Levels 1,2 & 3
- Interior & exterior framing/sheathing
 - Exterior - Plan North/ North West elevation & radiuses
 - Interior - Level 2
- Continue site utility installation
- Remediation of existing Sanitary Sewer Manholes & piping scheduled to start 2/8/24.
- PM on existing generator scheduled for 2/8/24 with Nixon Power.

 JOBSITE PHOTOS




In Wall Plumbing Rough-In

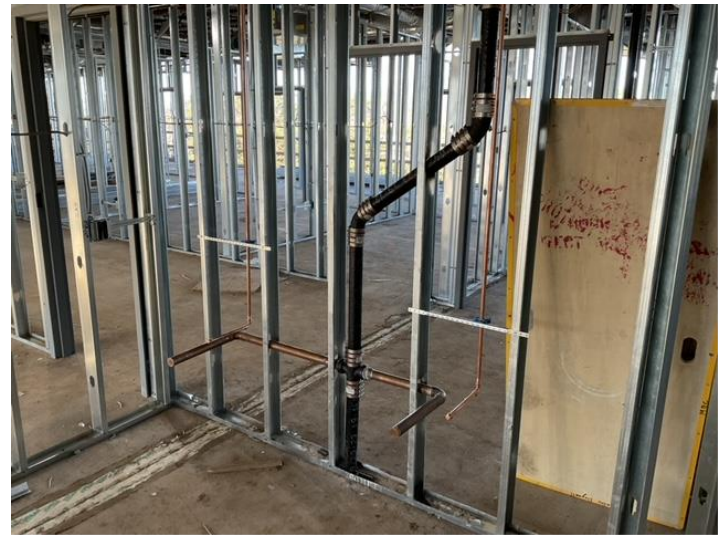

Plumbing Rough-In




Mechanical Rough-In

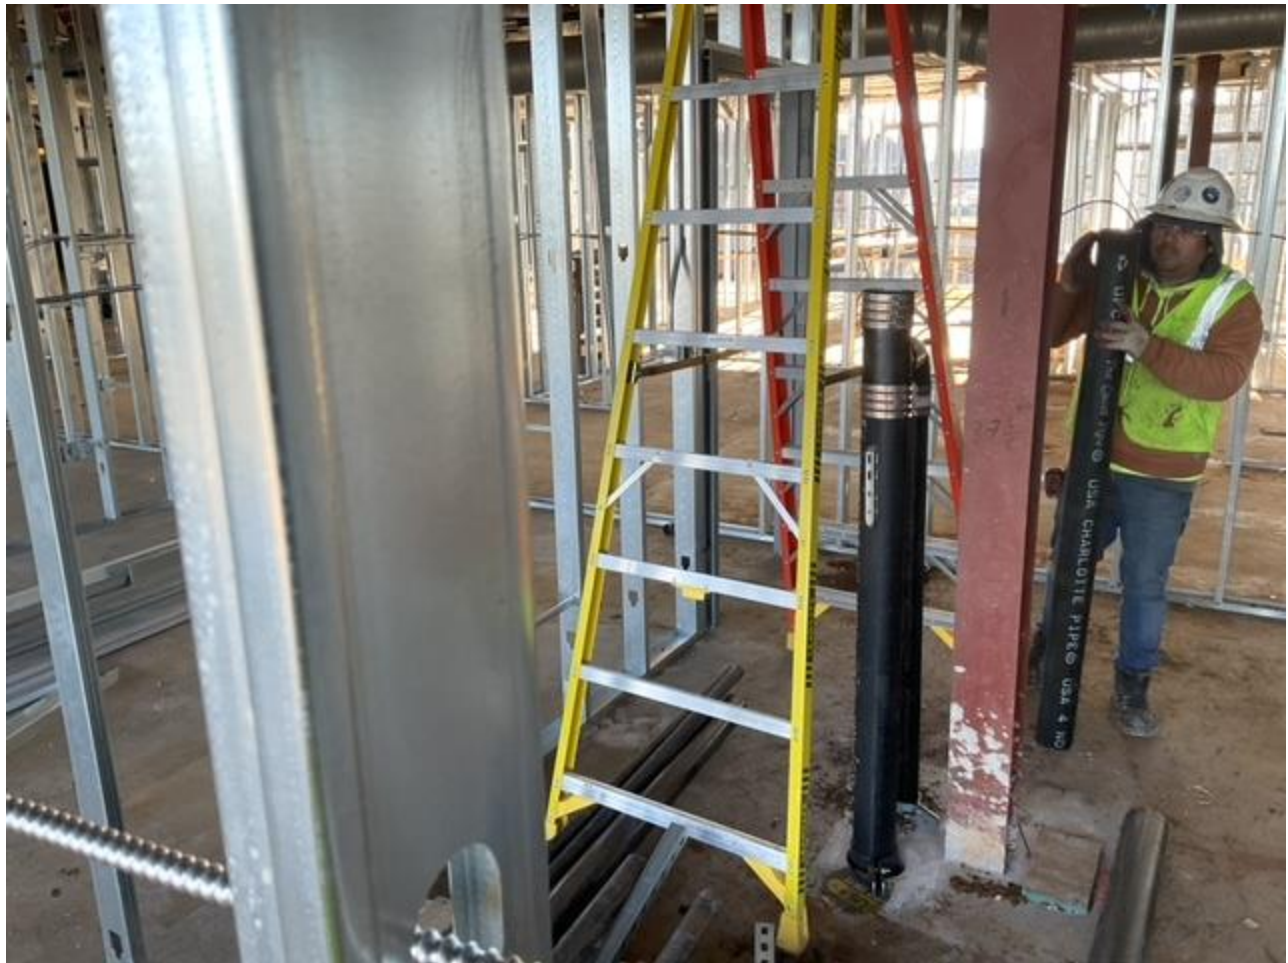

Plumbing Stack Line Rework



Grading/Backfill At Newly Installed Detention Pond

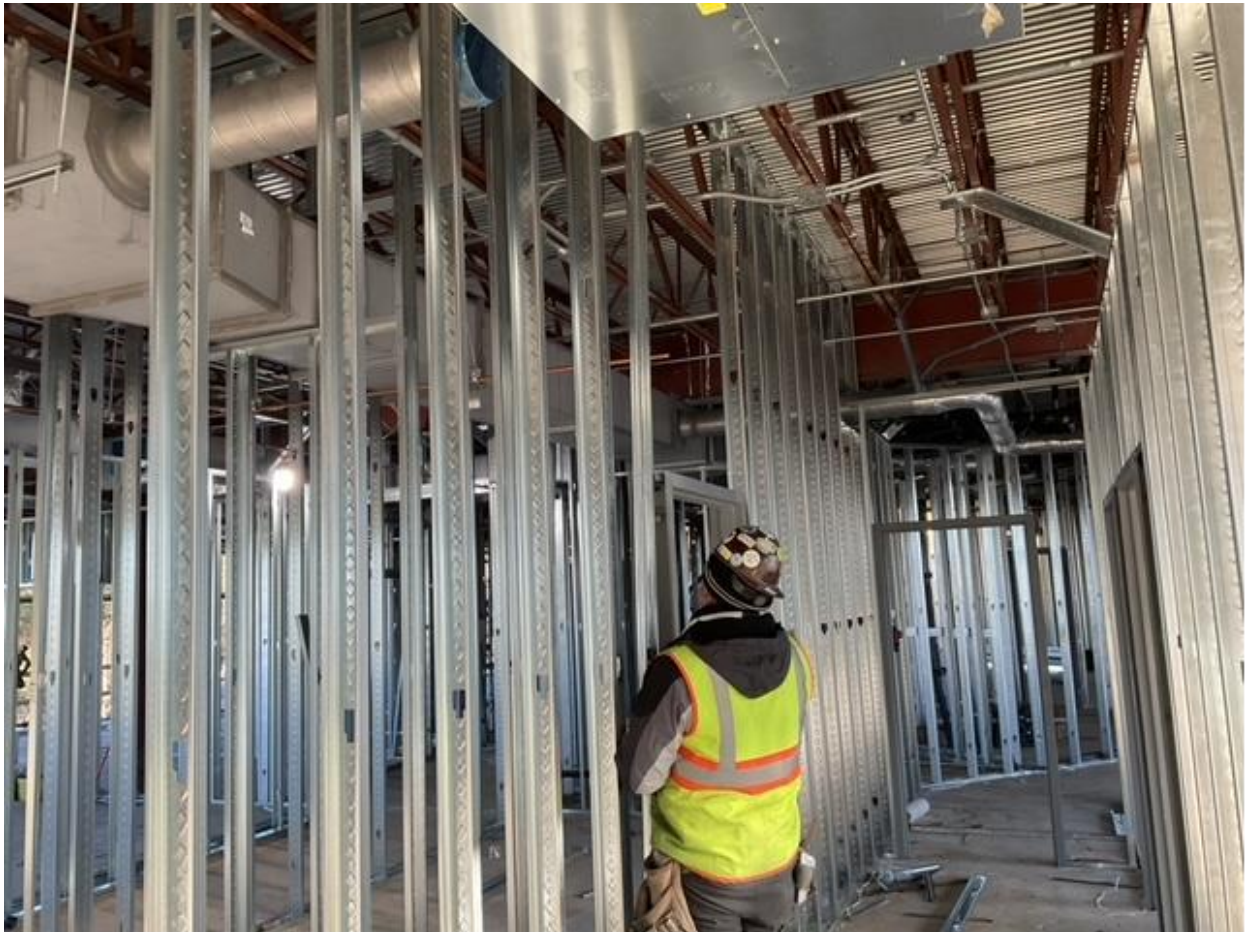

Interior Framing



Exterior Sheathing

















Installation Of 96" Underground Detention Pond



Electrical Rough-In

 WEATHER

Weather delays this week: 0

28  47° 37°	29  54° 29°	30  60° 39°	31  56° 30°	1  62° 40°	2  70° 44°	3  60° 40°
4  46° 40°	5  62° 34°	6  62° 34°	7  59° 34°	8  60° 42°	9  64° 55°	10  66° 53°

- Total Weather Delays: 7

SAFETY REPORT

- Days without an accident: 144
- Days without lost time: 144

MILESTONE TRACKING

- Construction Start: August 21, 2023
- Current Contract Completion Date: Mar 14, 2025
