

+ CURRENT CONSTRUCTION ACTIVITIES


LAST WEEK - WEEK ENDING 02/10/2024

- Tile bathroom walls and Fiber Reinforced Plastic completed.
- Poured second portion of the concrete drive.
- Interior exposed steel was painted.
- Interior walls were primed.
- Ceiling grid was hung.
- Installed light fixtures and diffusers from ceiling.

THIS WEEK - WEEK ENDING 02/17/2024

- Plumbing trim out.
- Electrical trim out of devices.
- Generator install.
- Light pole install.
- Irrigation install.
- Fuel canopy.
- Brick install on buildings.
- Brick columns for fence line.

 JOBSITE PHOTOS

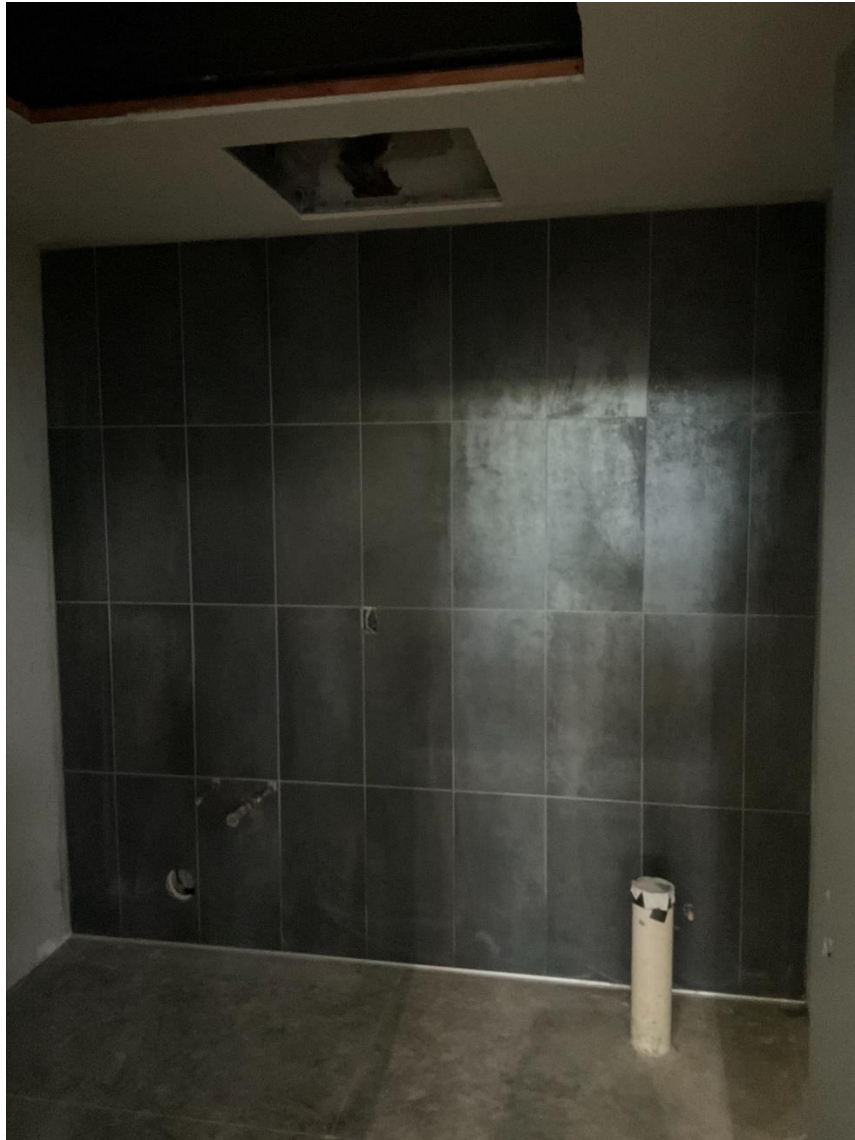

Wall Tile Install Completed



Wall Tile and FRP Install Completed



Second Portion Of Drive Poured



Light Fixtures Hung



Ceiling Grid Hung



Steel Painted



Interior walls Primed

WEATHER

Weather delays last week: 0

4 46° 40°	5 62° 34°	6 65° 36°	7 59° 34°	8 58° 43°	9 63° 49°	10 66° 56°
11 66° 57°	12 59° 39°	13 55° 33°	14 63° 36°	15 65° 42°	16 65° 41°	17 50° 33°

- Total Weather Delays: 3

SAFETY REPORT

- Days without an accident: 135
- Days without lost time: 135

MILESTONE TRACKING

- Construction Start: August 21, 2023
- Current Contract Completion Date: March 19, 2024
