

## CURRENT CONSTRUCTION ACTIVITIES

### LAST WEEK

---

- Completed Sub-Framing and Continued Fiber Cement Soffit and Siding Installation
- Continued Acoustical Ceiling Installation on Second Floor
- Continued Light Fixture Installation at the First and Second Floors
- Continue Interior Prep and Primer for Paint on Second Floor
- Continued Grading Throughout the Project Site
- Began Installing Floor and Wall Tile in the First Floor Bathrooms
- Completed Subgrade Prep at Spalding Drive for Sidewalks
- Completed AGL Installation of Exterior Gas Supply Line and Meter
- Began Cleaning Exterior Brick Vener and Cast Stone

### THIS WEEK

---

- Continue Fiber Cement Soffit and Siding Installation
- Continue Light Fixture Installation at The First and Second Levels
- Complete First Coat of Paint at the First Floor
- Begin First Coat of Paint at the Second Floor
- Continue Setting Final OCS Structure at Site Retaining Pond
- Completed Installation of Floor and Wall Tile at the First Floor Restrooms
- Begin Installation of Floor and Wall Tile at the Second Floor Restrooms
- Begin Installation of Formwork in Prep for Sidewalks at Spalding Dr
- Complete Installation of Compressed Air System
- Complete Installation of Thermostats at the First and Second Floors for Unit Start-up
- Continue Cleaning Exterior Brick Veneer and Cast Stone

## + JOBSITE PHOTOS



Completed Installation of Hardie Soffit at Second Floor Building Entrance



Completed Soffit Sub-Framing at Covered Porch





Continued Floor and Wall Tile Installation at First Floor Restrooms


## WEATHER

Weather delays last week: 0



## MANPOWER

MANPOWER GRAPH

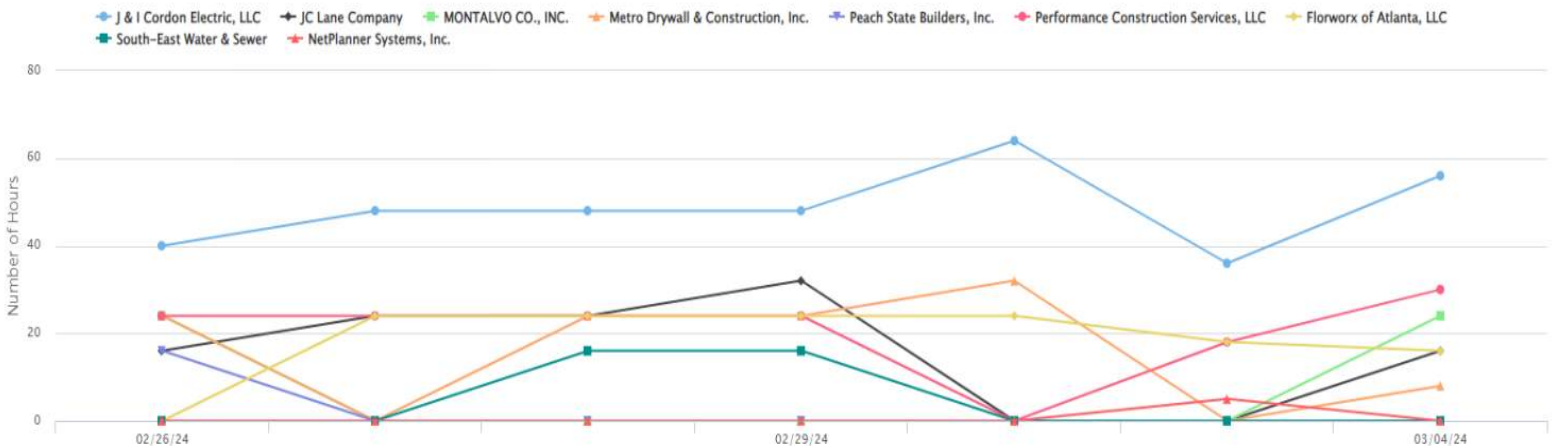

## SAFETY REPORT

- Days without an accident: 230
- Days without lost time: 230

## MILESTONE TRACKING

- Construction Start: April 10, 2023
- Current Contract Completion Date: June 10, 2024
