

CURRENT CONSTRUCTION ACTIVITIES

LAST WEEK

- Continued Fiber Cement Soffit and Siding Installation
- Continued Light Fixture Installation at The First and Second Levels
- Completed First Coat of Paint at the First Floor
- Began First Coat of Paint at the Second Floor
- Completed Installation of Floor and Wall Tile at the First Floor Restrooms
- Began Installation of Floor and Wall Tile at the Second Floor Restrooms
- Began Installation of Formwork in Prep for Sidewalks at Spalding Dr
- Continued Installation of Compressed Air System
- Completed Installation of Thermostats at the First and Second Floors for Unit Start-up
- Continued Cleaning Exterior Brick Veneer and Cast Stone

THIS WEEK

- Complete Fiber Cement Soffit and Siding Installation
- Continue Light Fixture Installation at The First and Second Levels
- Continue First Coat of Paint at the Second Floor
- Continue Installation of Floor and Wall Tile at the Second Floor Restrooms
- Complete Pour of Sidewalks at Spalding Dr
- Complete Installation of Compressed Air System
- Complete Cleaning Exterior Brick Veneer and Cast Stone

+ JOBSITE PHOTOS



Installation of First Coat and Light Fixtures at Stairwell




Sidewalk Formwork Prep for Concrete Pour This Afternoon



Continued Overhead Electrical at the Apparatus Bay


WEATHER

Weather delays last week: 0

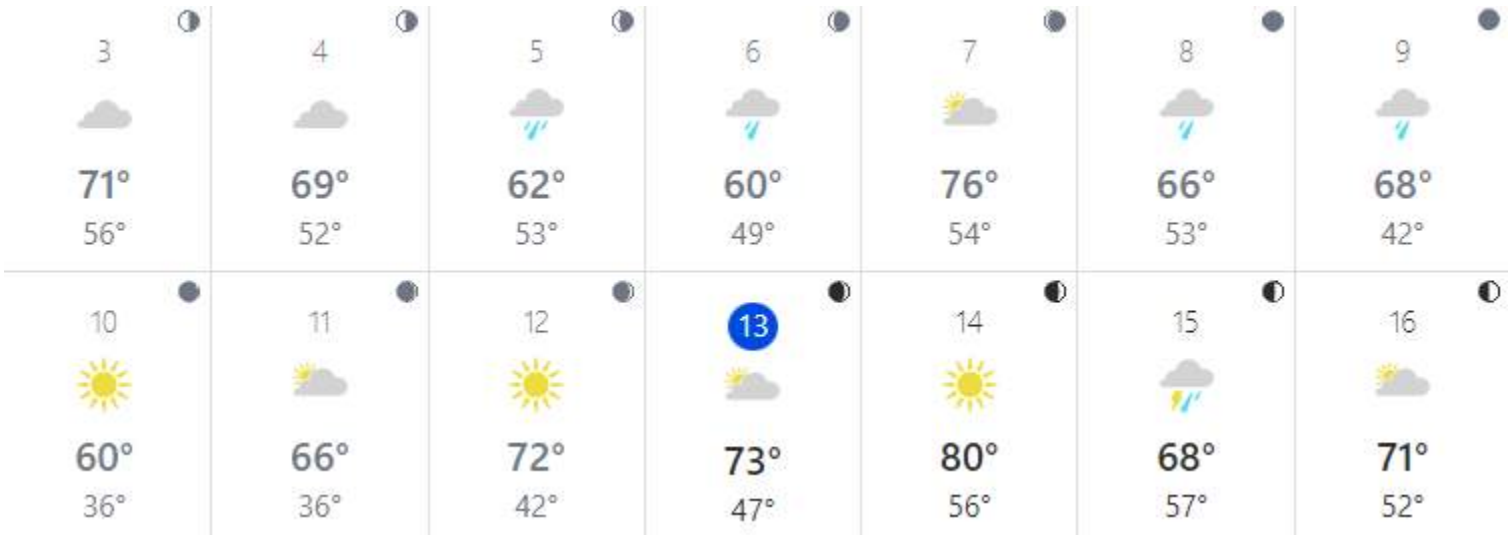

MANPOWER

MANPOWER GRAPH

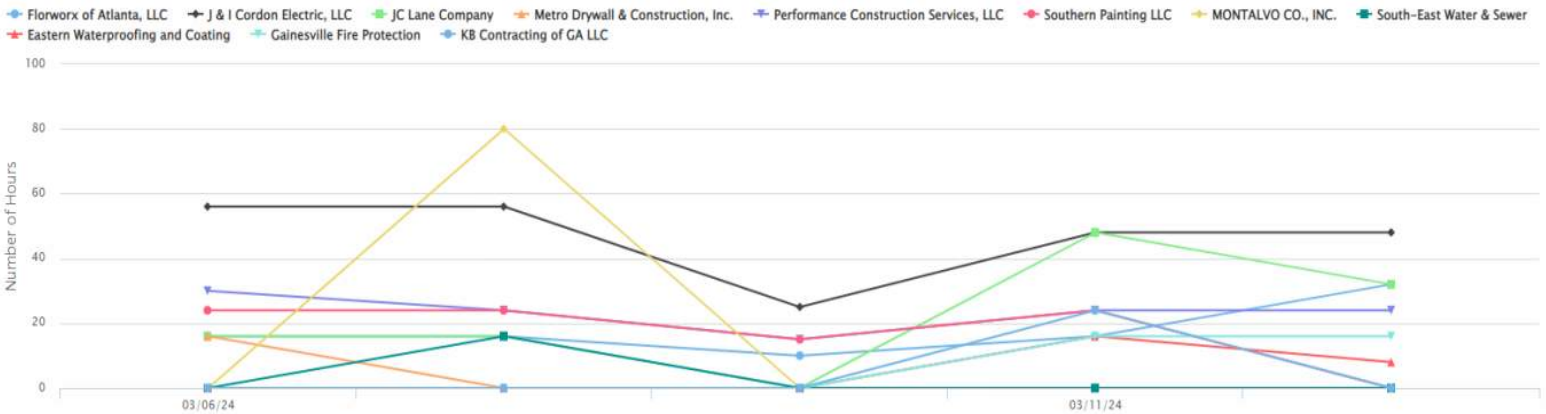

SAFETY REPORT

- Days without an accident: 235
- Days without lost time: 235

MILESTONE TRACKING

- Construction Start: April 10, 2023
- Current Contract Completion Date: June 10, 2024
