

CURRENT CONSTRUCTION ACTIVITIES

LAST WEEK

- Complete Fiber Cement Soffit and Siding Installation
- Continue Light Fixture Installation at The First and Second Levels
- Complete First Coat of Paint at First and Second Levels
- Complete Installation of Wall Tile at the Second Floor Restrooms
- Continue Brick Veneer at Kitchen Chimney
- Complete Cleaning Exterior Brick Veneer and Cast Stone
- Continue Installation of Plumbing Fixtures
- Begin Prepping for Installation of Exterior Paint

THIS WEEK

- Continue Painting at the Apparatus Bay Walls
- Complete Installation of Apparatus Bay Climbing Wall
- Complete Installation of Wall Tile at the Second Floor Restrooms
- Continue Brick Veneer at Kitchen Chimney
- Continue Installation of Plumbing Fixtures
- Complete Installation of Exterior Fiberglass Column Wraps
- Continue Soffit Framing and Sheetrock Installation at Kitchen
- Begin Installation of Millwork at First and Second Floors
- Begin Installation of Exterior Paint
- Prep and Pour Cover Porch Slab-on-Grade

+ JOBSITE PHOTOS



Installation of Millwork at Kitchen




Installation of Apparatus Bay Paint and Climbing Wall



Installation of Fiberglass Column Wraps a Second Floor Main Entrance


WEATHER

Weather delays last week: 0

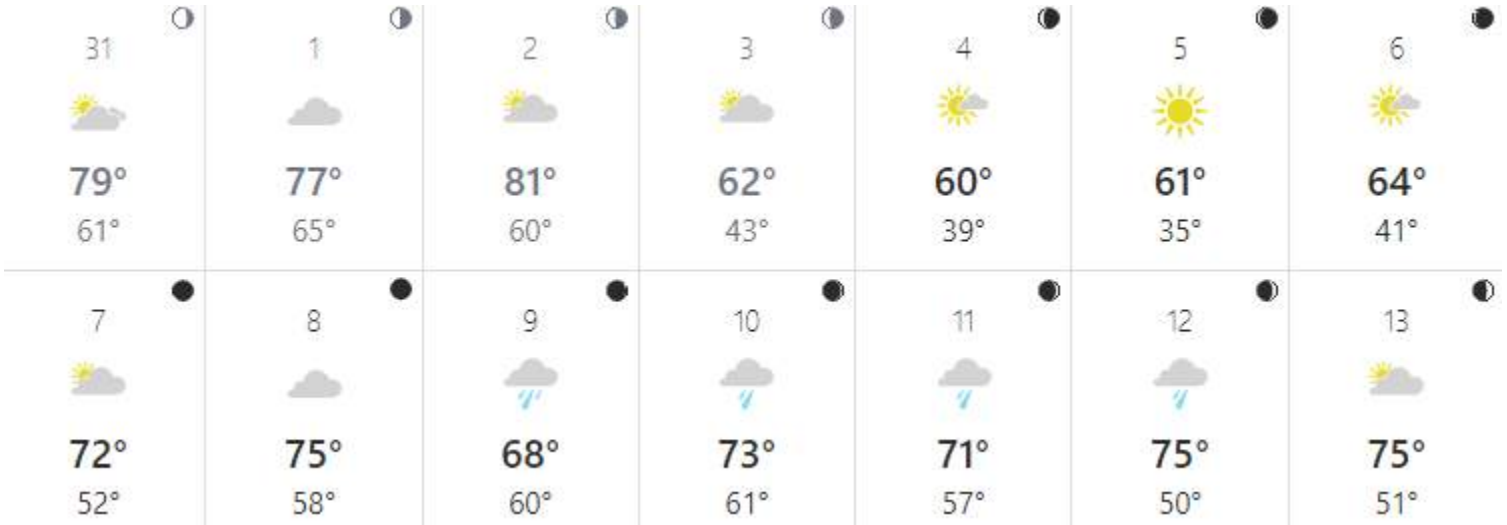

MANPOWER

MANPOWER GRAPH

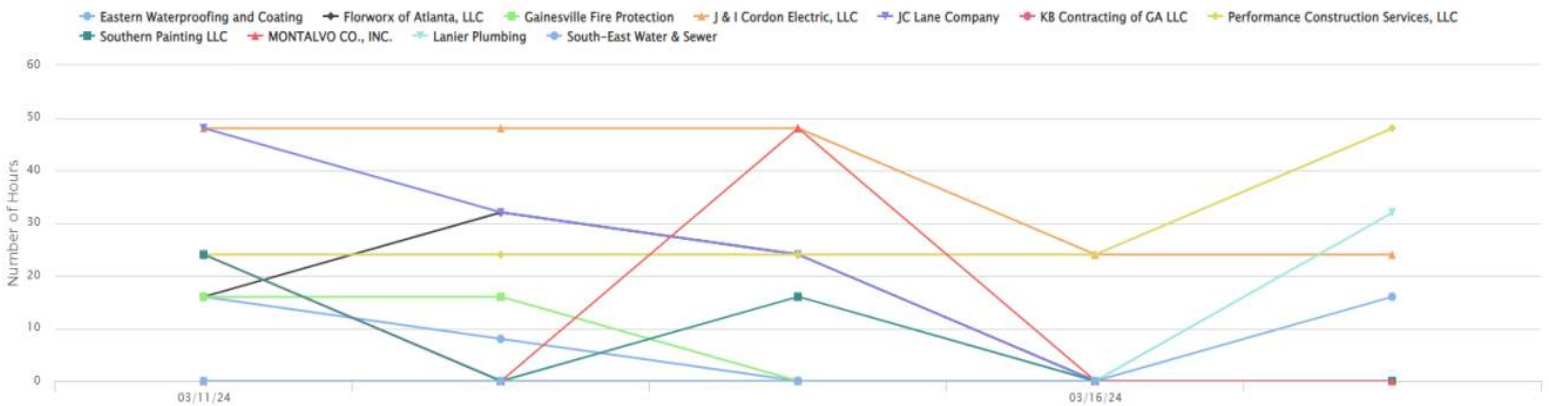

SAFETY REPORT

- Days without an accident: 255
- Days without lost time: 255

MILESTONE TRACKING

- Construction Start: April 10, 2023
- Current Contract Completion Date: June 10, 2024
