

## CURRENT CONSTRUCTION ACTIVITIES

### LAST WEEK

---


- Continued Painting at the Apparatus Bay Walls
- Completed Installation of Apparatus Bay Climbing Wall
- Completed Installation of Wall Tile at the Second Floor Restrooms
- Continued Brick Veneer at Kitchen Chimney
- Continued Installation of Plumbing Fixtures
- Completed Installation of Exterior Fiberglass Column Wraps
- Continued Soffit Framing and Sheetrock Installation at Kitchen
- Began Installation of Millwork at First and Second Floors
- Began Installation of Exterior Paint
- Prep and Pour Cover Porch Slab-on-Grade

### THIS WEEK

---

- Continue Painting at the Apparatus Bay Walls
- Continue Interior Painting at the Second Floor
- Begin Installation of Water Heaters at Generator Room
- Continue Preparation for Paint at Exterior Fiberglass Columns and Covered Porch Soffit
- Begin Installation of Millwork Countertops at First and Second Floors
- Continue Installation of Firepole Safety Kit Framing and Stainless Steel
- Continue Installation of Exterior Paint
- Complete Framing and SheetRock in Preparation for Display Case Installation
- Begin Installation of Data Rack at the Second Floor Data Room

## + JOBSITE PHOTOS

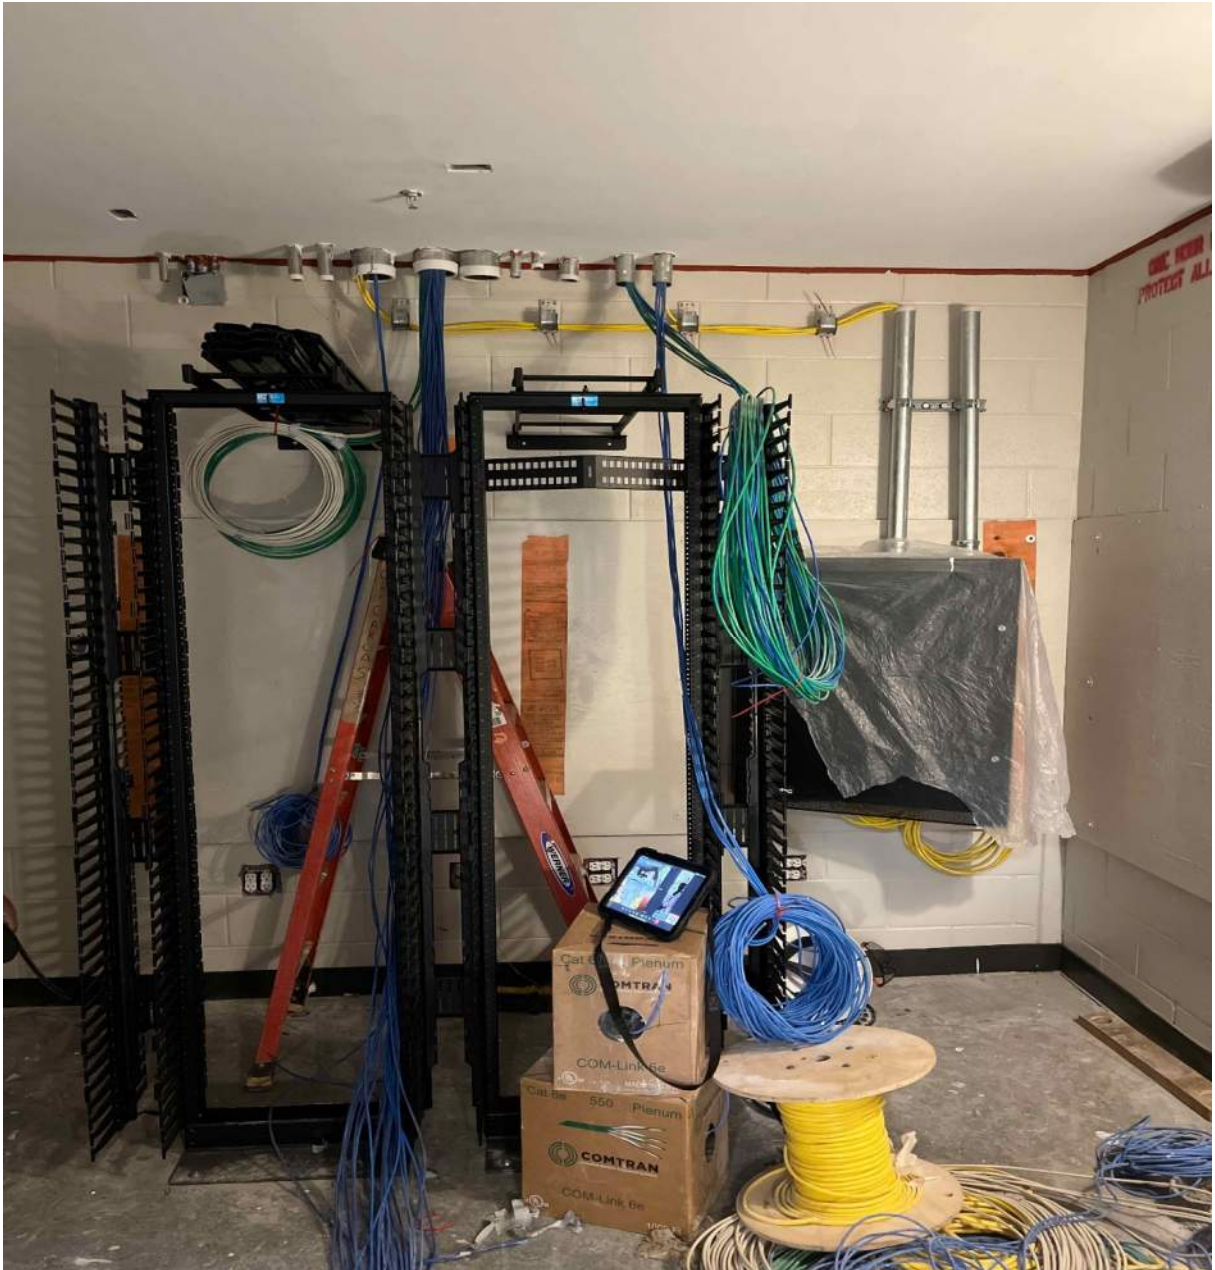

Installation of Data Rack at Second Floor Data Room



Installation of Interior Paint at Stairwell Windows





Installation of Shiplap in Prep for Display Case Installation


## WEATHER

Weather delays last week: 0



## MANPOWER

MANPOWER GRAPH

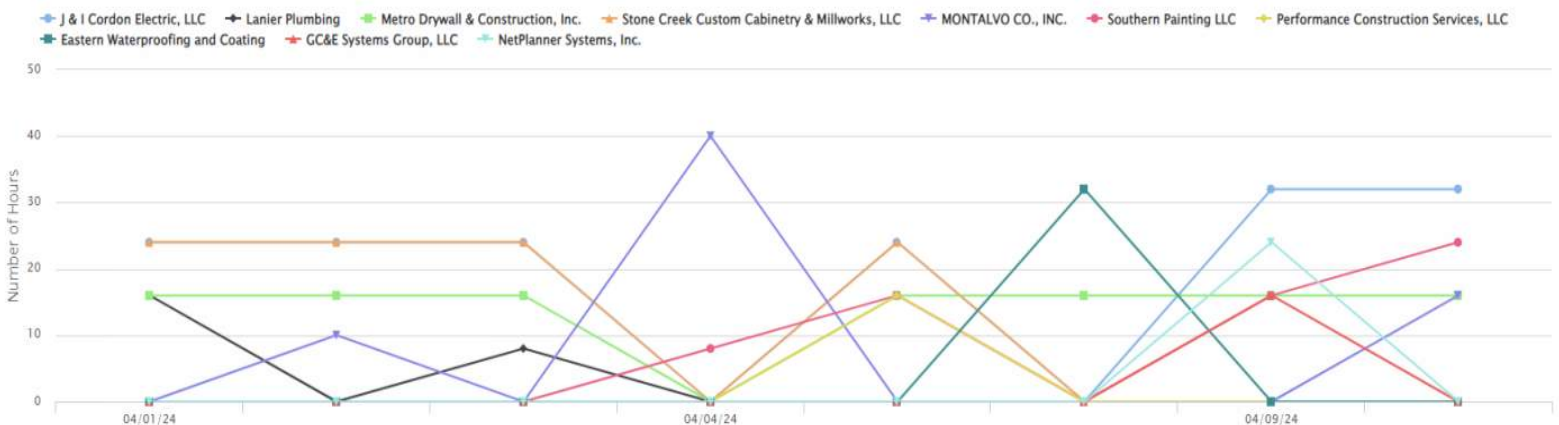

## SAFETY REPORT

- Days without an accident: 260
- Days without lost time: 260

## MILESTONE TRACKING

- Construction Start: April 10, 2023
- Current Contract Completion Date: June 10, 2024
