

CURRENT CONSTRUCTION ACTIVITIES


LAST WEEK

- Continued Painting at the Apparatus Bay Walls
- Began Installation of Water Heaters at Generator Room
- Continued Exterior Paint at Hardie Fascia and Soffits
- Completed Installation of Millwork Countertops at First and Second Floors
- Continued Installation of Firepole Safety Kit Framing and Stainless Steel
- Completed Installation of Display Case at Front Entrance
- Continued Installation of Data Rack at the Second Floor Data Room
- Began Installation of Gutters and Downspouts at Spalding Dr Elevation

THIS WEEK

- Continue Painting at the Apparatus Bay Walls
- Begin Dry fall Overhead Open Ceiling Paint in the Apparatus Bay
- Installation of Interior Wood Doors and Hardware
- Continue Installation of Water Heaters at Generator Room
- Continue Preparation for Paint at Exterior Fiberglass Columns and Covered Porch Soffit
- Continue Installation of Exterior Paint
- Continue Installation of Data Rack at the Second Floor Data Room
- Continue Installation of Gutters and Downspouts at Mount Vernon Elevation
- Complete Paver Subgrade in Preparation for Spalding Permeable Paver Installation
- Installation of Permeable Pavers at Spalding Dr Elevation.

+ JOBSITE PHOTOS

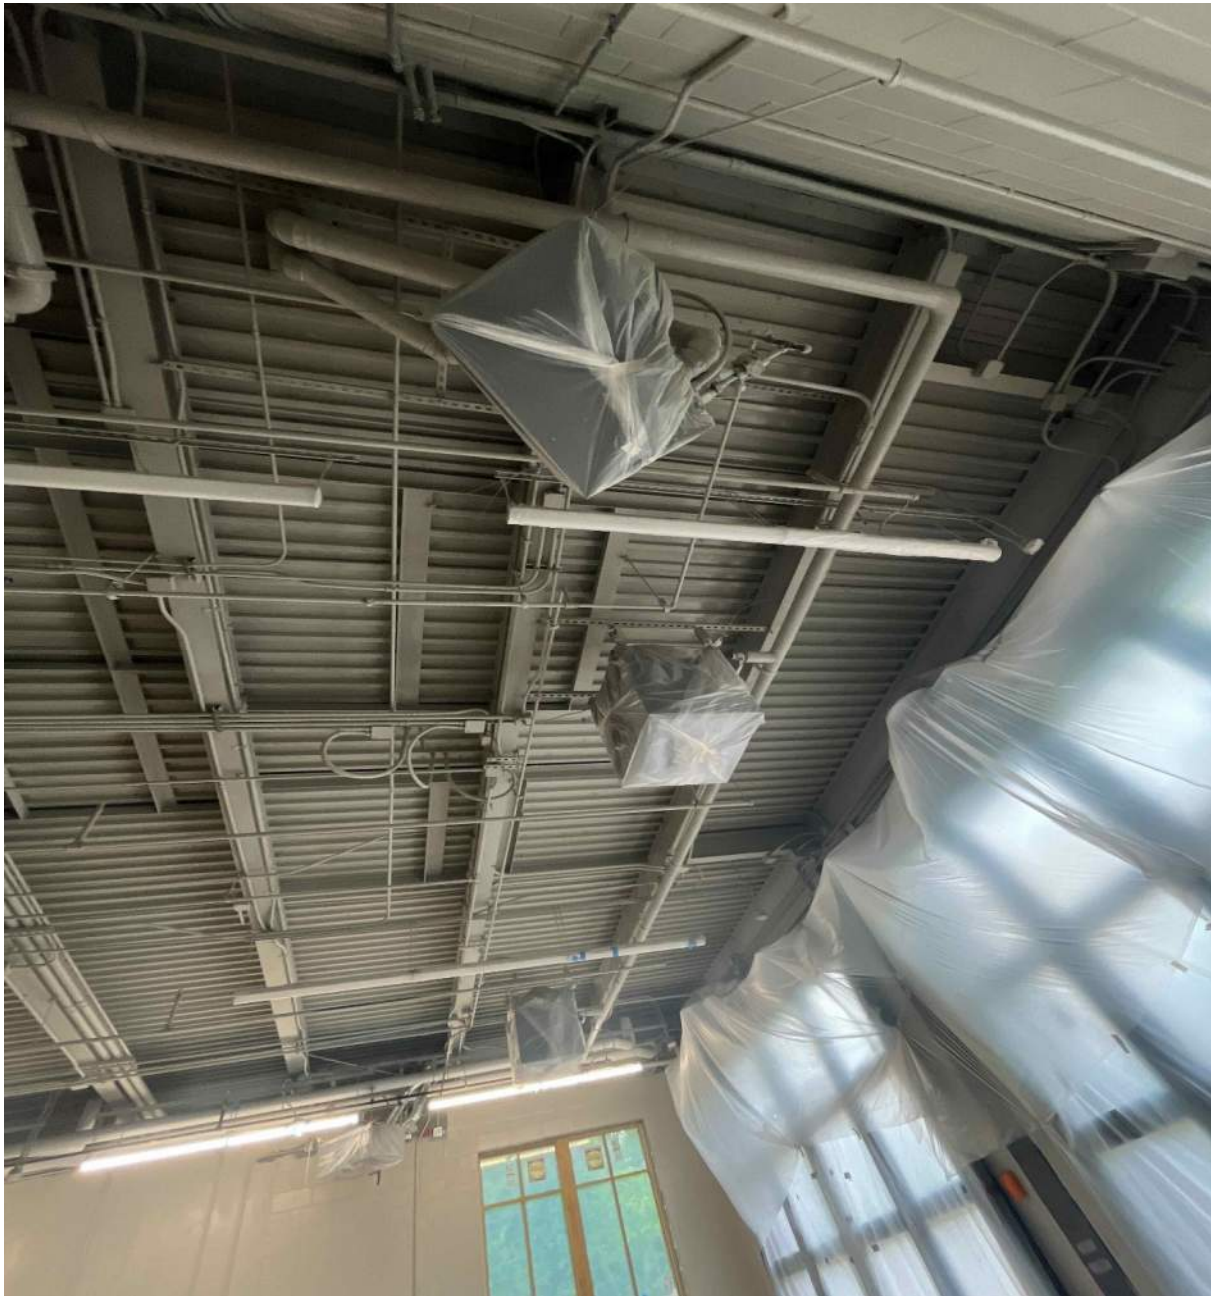

Overhead Open Ceiling Painting in Apparatus Bay




Preparing Subgrade at For Permeable Paver Installation at Spalding Elevation



Installation of Interior Wood Doors and Hardware at the Second Floor


WEATHER

Weather delays last week: 0

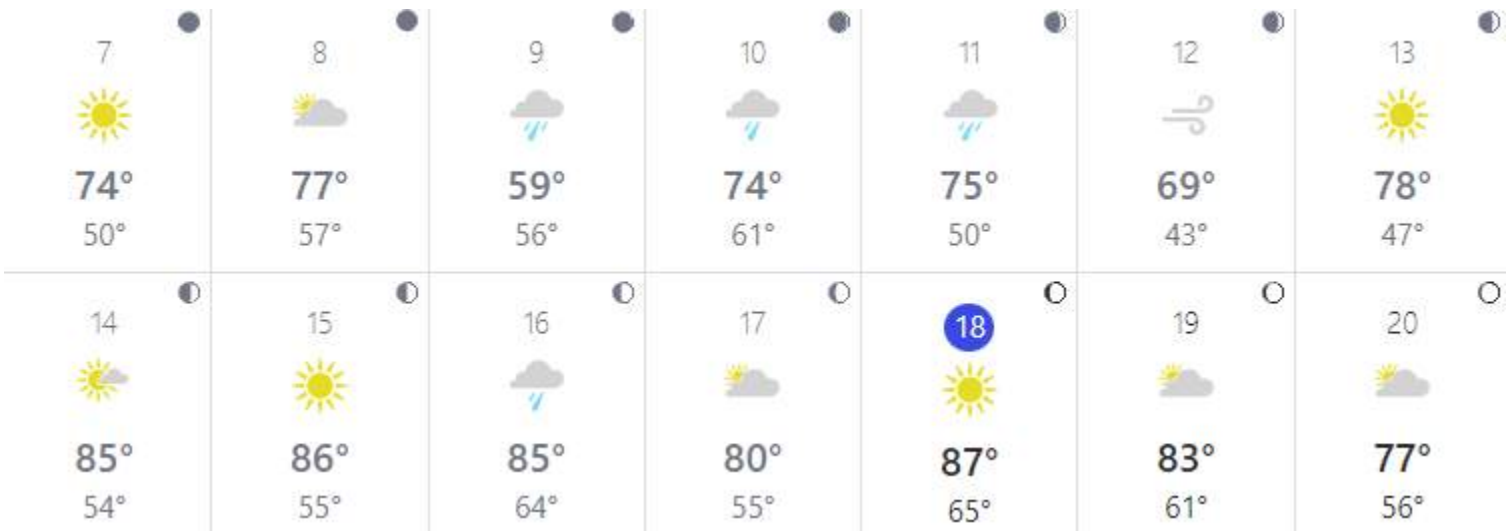

MANPOWER

MANPOWER GRAPH

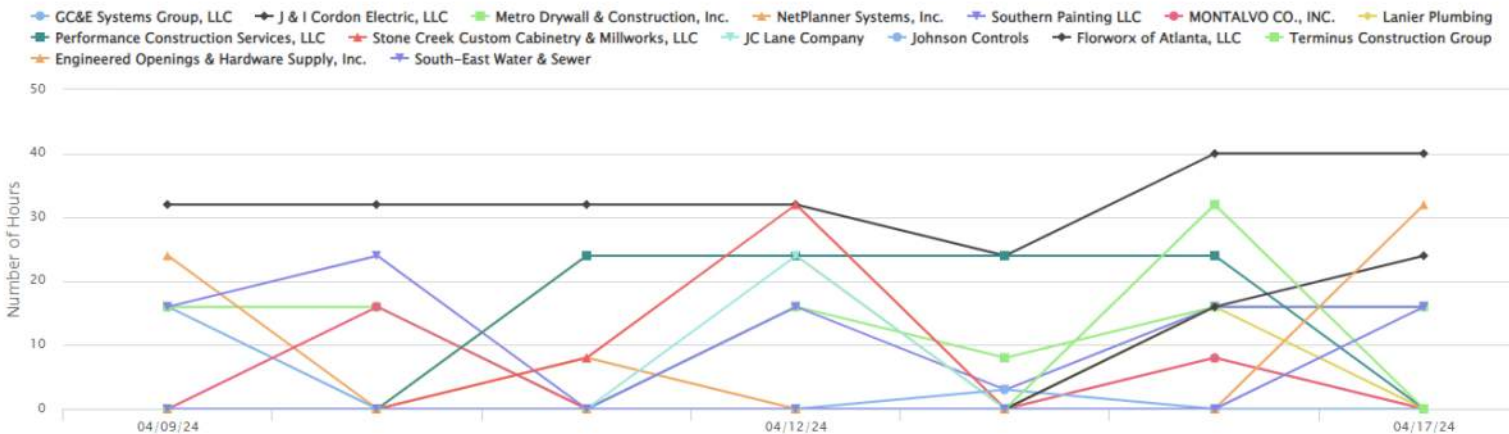

SAFETY REPORT

- Days without an accident: 265
- Days without lost time: 265

MILESTONE TRACKING

- Construction Start: April 10, 2023
- Current Contract Completion Date: June 10, 2024
