

CURRENT CONSTRUCTION ACTIVITIES

LAST WEEK

- Continue Painting at the Apparatus Bay Walls
- Begin Dry fall Overhead Open Ceiling Paint in the Apparatus Bay
- Installation of Interior Wood Doors and Hardware
- Continue Installation of Water Heaters at Generator Room
- Continue Preparation for Paint at Exterior Fiberglass Columns and Covered Porch Soffit
- Continue Installation of Exterior Paint
- Continue Installation of Data Rack at the Second Floor Data Room
- Continue Installation of Gutters and Downspouts at Mount Vernon Elevation
- Complete Paver Subgrade in Preparation for Spalding Permeable Paver Installation
- Installation of Permeable Pavers at Spalding Dr Elevation.


THIS WEEK

- Installation of Interior Wood Doors and Hardware
- Continue Preparation for Paint at Exterior Fiberglass Columns and Covered Porch Soffit
- Continue Installation of Exterior Paint
- Continue Installation of Gutters and Downspouts at Mount Vernon Elevation
- Complete Paver Subgrade in Preparation for Spalding Permeable Paver Installation
- Continue Subgrade in Preparation for Pond Mix Installation.
- Comcast Communication Service Installation
- Begin Dropping Acoustical Ceiling Tile at First and Second Levels

 JOBSITE PHOTOS



Grading in Prep for Landscaping Installation

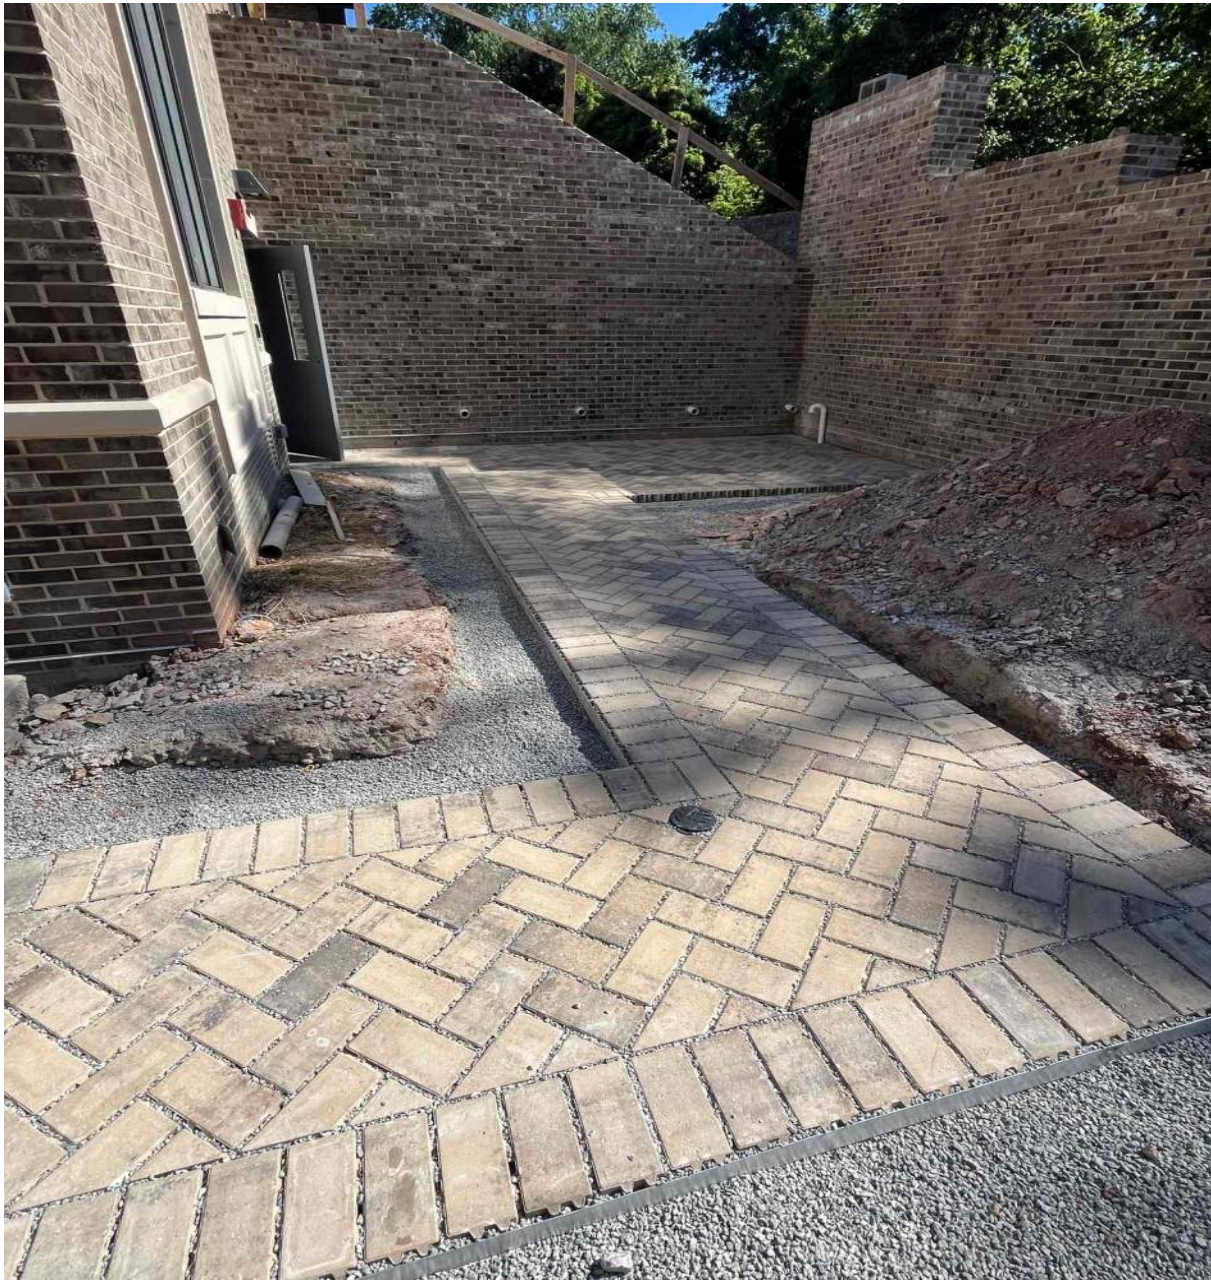

Permeable Paver Installation at Spalding Elevation



Installation of Interior Wood Barn Doors and Hardware at the First Floor Dorms


WEATHER

Weather delays last week: 0



MANPOWER

MANPOWER GRAPH

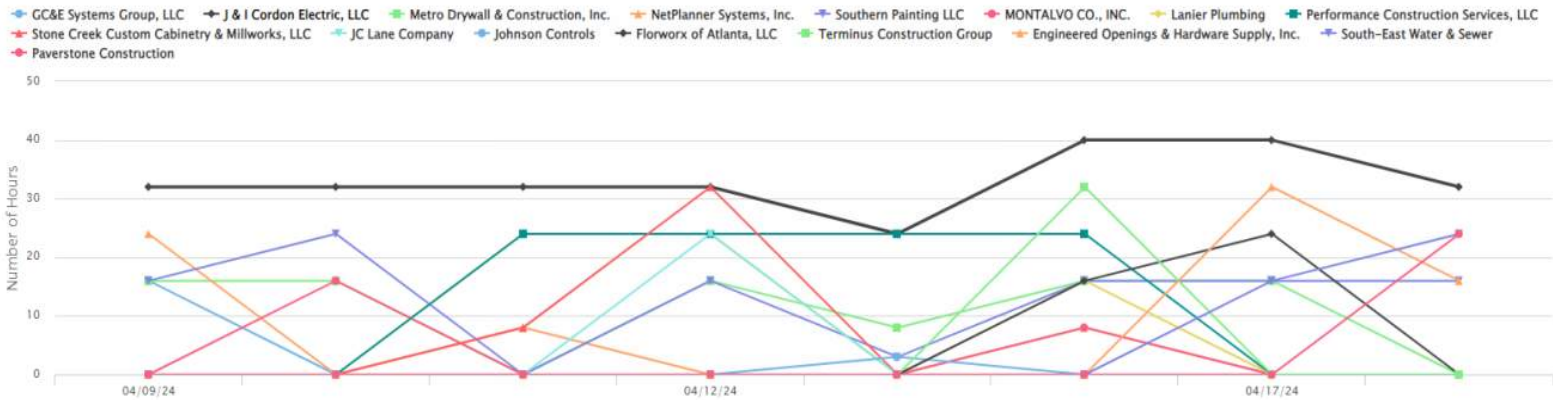

SAFETY REPORT

- Days without an accident: 270
- Days without lost time: 270

MILESTONE TRACKING

- Construction Start: April 10, 2023
- Current Contract Completion Date: June 10, 2024
