

## CURRENT CONSTRUCTION ACTIVITIES

### LAST WEEK - WEEK ENDING 03/09/2024

---

- Brick on the building was complete
- Brick columns were complete
- Floors were sealed in the office and shop area
- Break area cabinets installed
- Canopy's above the entry doors were installed
- Metal panels installed between the brick
- Interior plumbing fixtures were set
- Bathroom accessories installed
- Blinds installed

### THIS WEEK - WEEK ENDING 03/16/2024

---

- Continuing fencing installation
- Continuing with landscaping around the site
- Low voltage trim out
- Final paint interior & exterior
- Biocell pond work to begin
- MEP Testing

 JOBSITE PHOTOS



Brick On The Building Completed



Brick Columns Completed




Floors Sealed In Office And Shop Area



Break Area Cabinets Installed





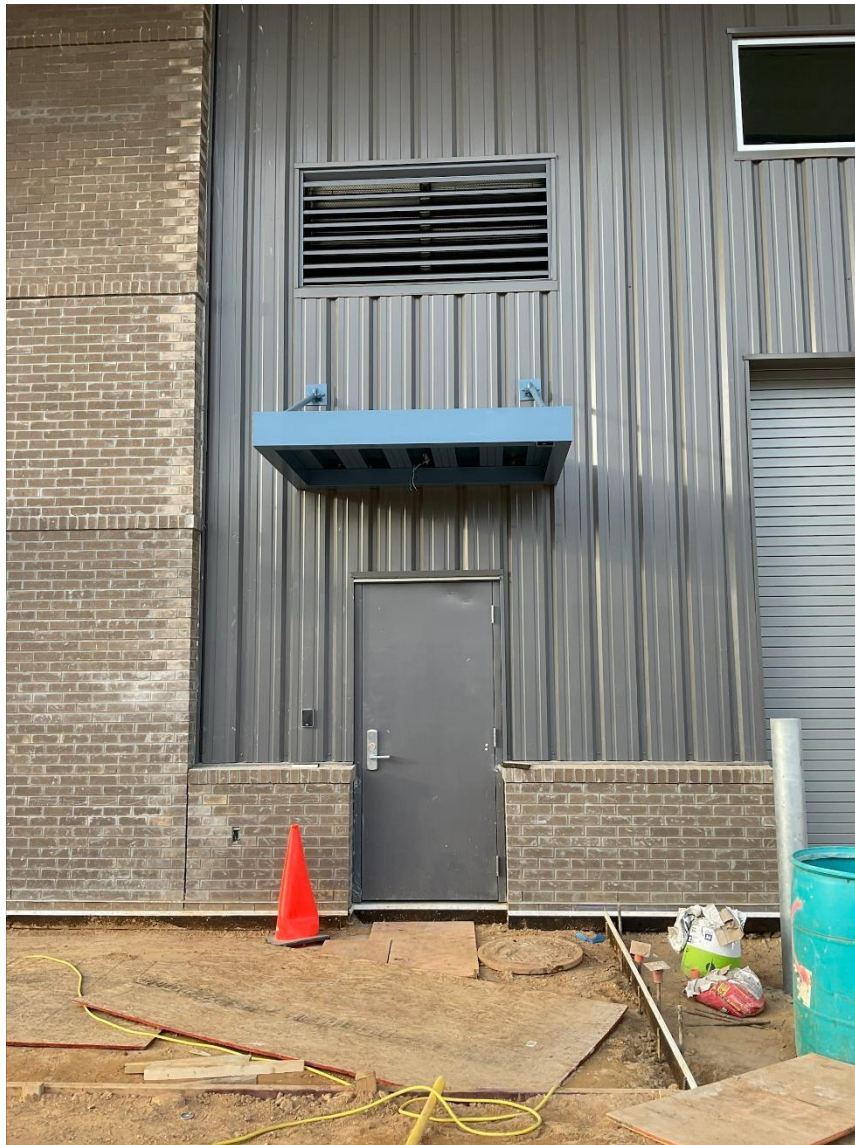











Canopies Above Entrances Installed



Metal Panels Installed Between Brick

## WEATHER

Weather delays last week: 0

3  71° 54°	4  72° 53°	5  64° 53°	6  61° 50°	7  75° 56°	8  65° 52°	9  65° 41°
10  58° 35°	11  67° 39°	12  -- 42°	13  73° 46°	14  80° 56°	15  68° 57°	16  71° 54°

- Total Weather Delays: 3



## SAFETY REPORT

- Days without an accident: 158
- Days without lost time: 158

## MILESTONE TRACKING

- Construction Start: August 21, 2023
- Current Contract Completion Date: March 19, 2024
