

# CURRENT CONSTRUCTION ACTIVITIES

## LAST WEEK - WEEK ENDING 03/16/2024

---

### Roof

- Screen wall steel install
- Roof demo / New roof install
- Penthouse Framing
- Stair 1 extension

### Level 3

- Exterior Sheathing
- Setting of window frames

### Level 2

- Exterior Framing/Sheathing
- Plumbing, Electrical, & Framing inspections 3/12/24

### Level 1

- MEP-R/I-O/H & In-wall
- Exterior Framing/Sheathing
- interior framing (curtain wall/store front)
- Installing Brick Lintel/Kicker assembly (South elevation)

### Basement

- Continue replacement of U/G sanitary sewer piping
- Under slab Plumbing Inspection 3/12/24
- Backfill/Rebar/ slab pour back from U/G plumbing replacement 3/15/24
- CMU Courses/ Masonry door installs at holding cell/elevator additions

### Exterior

- Continue installing cmu courses/masonry frames for exterior/interior walls at Sally Port
- Plumbing & electrical R/I at cmu walls/ mechanical block-outs
- Water Proofing exterior Sheathing
- Heavy Civil working to expose existing roof drains coming out from building and tying into newly installed Storm Line system
- Setting MH C2 & tie in storm line "C" to U/G detention pond

## THIS WEEK - WEEK ENDING 03/23/2024

### Roof

- Screen wall steel install
- Roof demo / New roof install
- MEP R/I as new roof is installed

### Level 3

- Exterior Sheathing
- Setting of window frames
- pipe insulation
- Copper lines for rooftop condenser units

### Level 2

- Exterior Sheathing
- Setting window frames
- Pipe insulation
- Slab demo for elevator CMU extension

### Level 1

- MEP-R/I-O/H & In-wall
- Exterior Framing/Sheathing
- interior framing (curtain wall/store front)
- Slab demo for elevator CMU extension
- CMU courses for holding cell/ elevator area

### Basement

- Backfill/Rebar/ slab pour back from U/G plumbing replacement & stair 3 extension 3/18/24
- CMU Courses/ Masonry door installs at holding cell/elevator additions
- Exterior Framing/Sheathing
- Mechanical R/I

### Exterior

- Plumbing & electrical R/I at cmu walls/ mechanical block-outs
- Water Proofing exterior Sheathing/ exposed BG masonry & CIP walls (per RFI 071)
- Setting MH C10/ running rcp between MHs
- Begin installing storm line B/ setting MH B2
- Excavate/rebar/pour retaining wall b footings
- Excavate/rebar/pour footings for foundation wall & steel columns at courtroom/admin wing
- Setting sequence 6 steel at Sally port addition
- Brick ledge North elevation

### Notes

- ECS Inspector on site for duration of roof demolition to verify structural integrity of existing metal decking

 JOBSITE PHOTOS



Exterior Framing



Electrical In-Wall




Setting MH C2



## Mechanical RI



CMU Walls

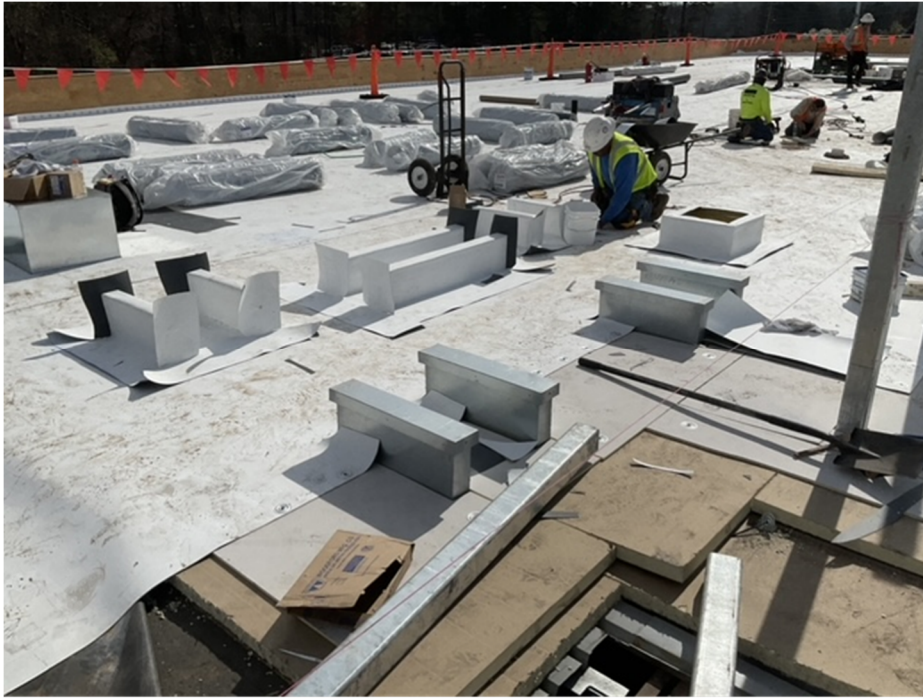

New Roof Install





Exterior Soffit Framing



Retaining Wall B



Roof Penthouse Framing/Sheathing

















Brick Ledge Install



## TPO Roofing

 WEATHER

Weather delays this week: 0

10  58° 35°	11  67° 39°	12  71° 42°	13  75° 47°	14  82° 60°	15  70° 54°	16  71° 50°
17  69° 45°	18  57° 30°	19  59° 38°	20  70° 44°	21  74° 52°	22  56° 51°	23  65° 44°

- Total Weather Delays: 15

## SAFETY REPORT

- Days without an accident: 175
- Days without lost time: 175

## MILESTONE TRACKING

- Construction Start: August 21, 2023
- Current Contract Completion Date: Mar 14, 2025
