

# CURRENT CONSTRUCTION ACTIVITIES

## LAST WEEK - WEEK ENDING 04/13/2024

---

### Level 3:

- Low voltage R/I
- Sheetrock/insulation installation
- Low voltage for fire alarms
- Begin setting glass

### Level 2:

- Setting window frames
- CMU courses for holding cell/ elevator area
- Low Voltage R/I
- Electrical R/I adjustments based on Bulletin #6
- Copper lines for rooftop condenser units

### Level 1:

- MEP-R/I-O/H & In-wall
- Low voltage R/I
- Copper lines for rooftop condenser units

### Basement:

- MEP O/H R/I
- Demo existing 4" sprinkler pipe

### Exterior/Sallyport:

- Water Proofing exterior Sheathing
- Wreck formwork at retaining wall B
- Setting sequence 6 steel at Sally port addition
- Concrete pour remainder of slab at sallyport 4/8/24
- Installing storm pipe from Sally Port to MH B2
- Excavating for FTGs at Court/Admin Wing addition

### Site Engineering(Fulton County)

- Crew set new polymer transition MH at top of slope
- Crew back filled around MH and other excavated areas

## THIS WEEK - WEEK ENDING 04/20/2024

### Level 3:

- Sheetrock/insulation installation
- Setting glass
- Pulling Low Voltage wire for Fire Alarms
- Framing Soffit/Hard ceilings

### Level 2:

- Setting glass
- Low Voltage R/I
- Begin Sheetrock/insulation installation

### Level 1:

- MEP-R/I-O/H & In-wall
- Low voltage R/I
- Copper lines for rooftop condenser units
- Electrical & Plumbing R/I Inspections (4/17)
- Setting glass

### Basement:

- MEP O/H R/I
- Wall layout
- Mechanical O/H R/I inspection
- Demo existing 4" sprinkler pipe


### Exterior/Sallyport:

- Water Proofing exterior Sheathing
- Setting sequence 6 steel at Sally port addition
- Excavating for FTGs at Court/Admin Wing addition
- Pouring Footings/piers at Court/Admin Wing
- Site Grading
- Laying CMU at interior walls
- Mech/Electrical R/I as Interior CMU walls are set

### Site Engineering(Fulton County)

- Crew saw cut across Morgan Falls Rd.
- Excavate across roadway with intention to extend bypass across road allowing existing MH on SSPQH property to be replaced

 JOBSITE PHOTOS

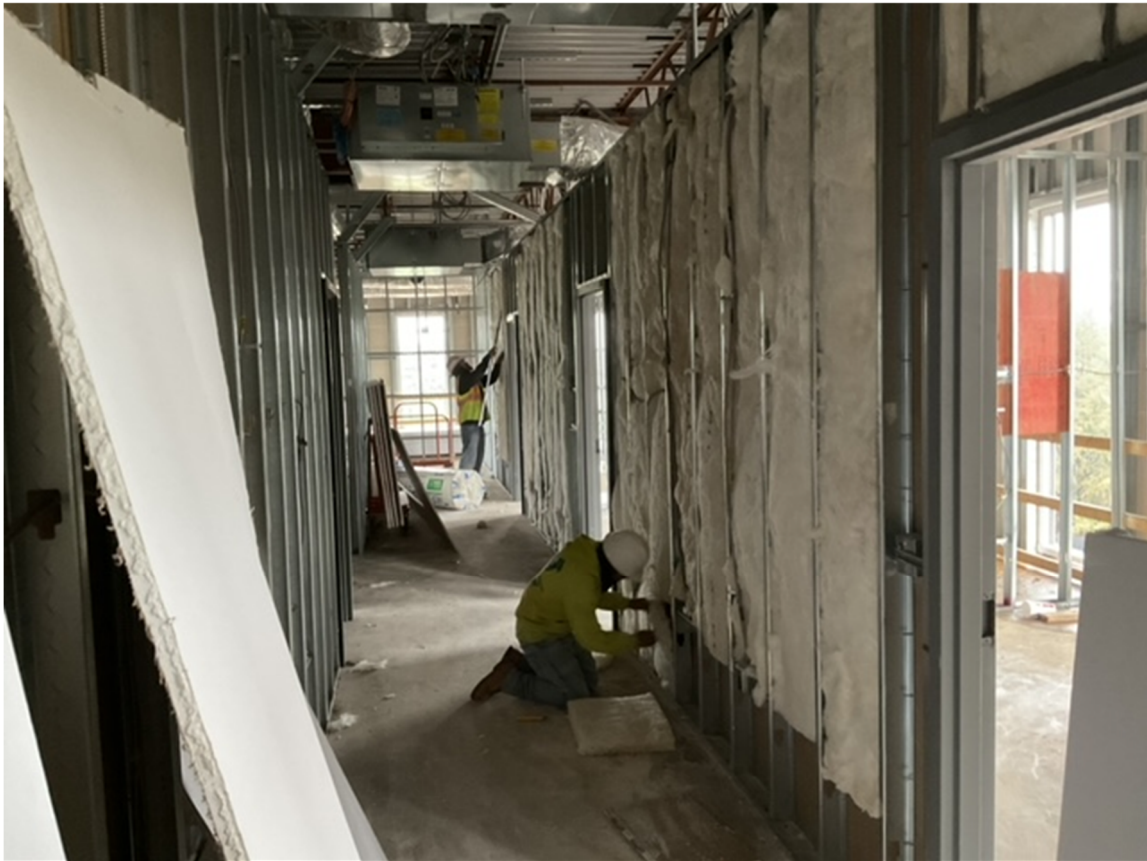

Sheetrock/Insulation Installation





Storm Pipe





## Waterproofing Exterior Sheathing



## Sheetrock Install



## MEP O-H





## Setting Sequence 6 Steel At Sally Port



CMU Walls At Sally Port



















Footings/Piers At Courtroom Addition



 WEATHER

Weather delays this week: 0

7  74° 50°	8  78° 56°	9  60° 56°	10  73° 59°	11  75° 50°	12  68° 46°	13  77° 48°
14  86° 57°	15  86° 58°	16  84° 62°	17  79° 60°	18  87° 63°	19  82° 60°	20  78° 55°

- Total Weather Delays: 19
- SSPHQ jobsite received 0.6” of rain Tuesday 4/9 causing 2 days of exterior work delay.
- Site Also received an additional .5” of rain on Thursday 4/11

## SAFETY REPORT

- Days without an accident: 195
- Days without lost time: 195

## MILESTONE TRACKING

- Construction Start: August 21, 2023
- Current Contract Completion Date: Mar 14, 2025
