

CURRENT CONSTRUCTION ACTIVITIES

LAST WEEK - WEEK ENDING 04/20/2024

Level 3:

- Sheetrock/insulation installation
- Setting glass
- Pulling Low Voltage wire for Fire Alarms
- Framing Soffit/Hard ceilings
- Insulation Inspection by CoSS

Level 2:

- Setting glass
- Begin Sheetrock/insulation installation
- Pulling Low Voltage wire for Fire Alarms

Level 1:

- MEP-R/I-O/H & In-wall
- Low voltage R/I
- Copper lines for rooftop condenser units
- Electrical & Plumbing R/I Inspections (4/17) CoSS
- Setting glass

Basement:

- MEP O/H R/I
- Wall layout
- Mechanical O/H R/I inspection CoSS
- Demo existing 4" sprinkler pipe
- Setting glass

Exterior/Sallyport:

- Water Proofing exterior Sheathing
- Setting sequence 6 steel at Sally port addition
- Excavating for FTGs at Court/Admin Wing addition
- Pouring Footings/piers at Court/Admin Wing
- Site Grading
- Laying CMU at interior walls
- Mech/Electrical R/I as Interior CMU walls are set
- Brick ledge repair/pour per RFI 107

Site Engineering(Fulton County)

- Crew saw cut across Morgan Falls Rd.
- Excavate across roadway with intention to extend bypass across road allowing existing MH on SSPQH property to be replaced

THIS WEEK - WEEK ENDING 04/27/2024

Level 3:

- Sheetrock/insulation installation
- Framing Soffit/Hard ceilings
- Screw Pattern Inspection per CoSS 4/24/24

Level 2:

- Sheetrock/insulation installation
- Pulling Low Voltage wire for Fire Alarms

Level 1:

- Low voltage R/I
- Installing glass curtain wall system

Basement:

- MEP O/H R/I
- Wall layout
- Demo existing 4" sprinkler pipe / installing new 6" main lines
- Installing glass curtain wall system
- Interior Framing

Exterior/Sallyport:

- Water Proofing exterior Sheathing
- Waterproofing @ RWB & Foundation wall & Sally Port
- Setting sequence 6 steel at Sally port addition/Installing 1st floor decking
- Installing screen wall steel @ Sally Port roof
- Site Grading / Back fill
- Begin brick Install @ North elevation
- Prepping to start laying brick @ Sally port
- U/G Sanitary @ Court Addition

Site Engineering(Fulton County)

- Relocate Bypass to allow MH rework

+ JOBSITE PHOTOS



Brick Install At North Elevation



Mechanical O/H & In-Wall




Installing Glass Curtain Wall System



Setting Glass



Framing Soffit/Hard Ceilings

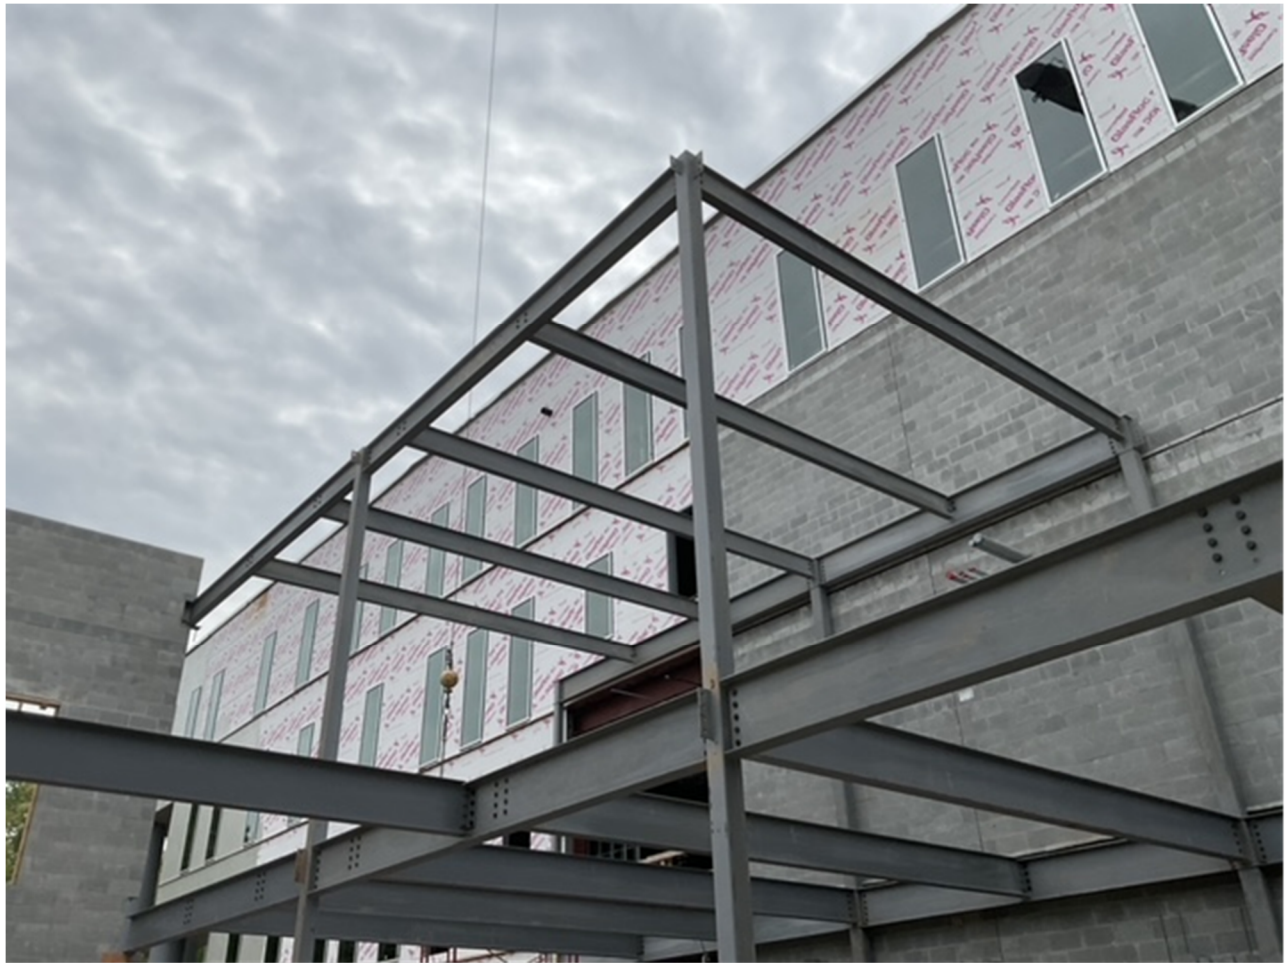

Setting Sequence 6 Steel At Sally Port

















CMU Walls At Sally Port



Footings/Piers At Courtroom Addition

 WEATHER

Weather delays this week: 0

14  86° 57°	15  86° 58°	16  86° 64°	17  81° 56°	18  89° 67°	19  84° 63°	20  81° 52°
21  58° 42°	22  68° 39°	23  73° 50°	24  72° 50°	25  76° 56°	26  74° 60°	27  77° 60°

- Total Weather Delays: 19
- SSPHQ jobsite received 0.6” of rain Sunday 4/21/24 causing site conditions to be soft & muddy on Monday 4/22/24.

SAFETY REPORT

- Days without an accident: 200
- Days without lost time: 200

MILESTONE TRACKING

- Construction Start: August 21, 2023
- Current Contract Completion Date: Mar 14, 2025
