

CURRENT CONSTRUCTION ACTIVITIES

LAST WEEK

- Continued Installation of Interior Wood Doors and Hardware
- Began Installation of Landscaping
- Completed Installation of Cast Stone Chimney Top
- Completed Remaining Pilaster Veneer and Cast Stone
- Completed Installation of TV's at First and Second Floor
- Completed Installation of Fireplaces at Dayroom and Lounge
- Completed Installation of Rubber Wall Base and Corner Guards
- Completed Second Coat at the First and Second Floors
- Began Installation of Site Fencing
- Began Installation of Apparatus Bay Flooring
- Completed Bi-fold Door Sensor Installation and Commissioning

THIS WEEK

- Continue Installation of Landscaping
- Continue Installation of Site Fencing
- Complete Installation of Gym Athletic Flooring and Rubber Stair Treads
- Continuing MEP Trim out at the First and Second Floors
- Complete Installation of Interior Door Hardware
- Begin Rough Clean at First and Second Floors
- Begin Installation of Decon Equipment

JOBSITE PHOTOS



Installation of Landscaping and Site Fencing at Corner of Site




Installation of Apparatus Bay Epoxy Flooring



Installation of Fireplace and TV at Dayroom on the Second Floor


WEATHER

Weather delays last week: 0

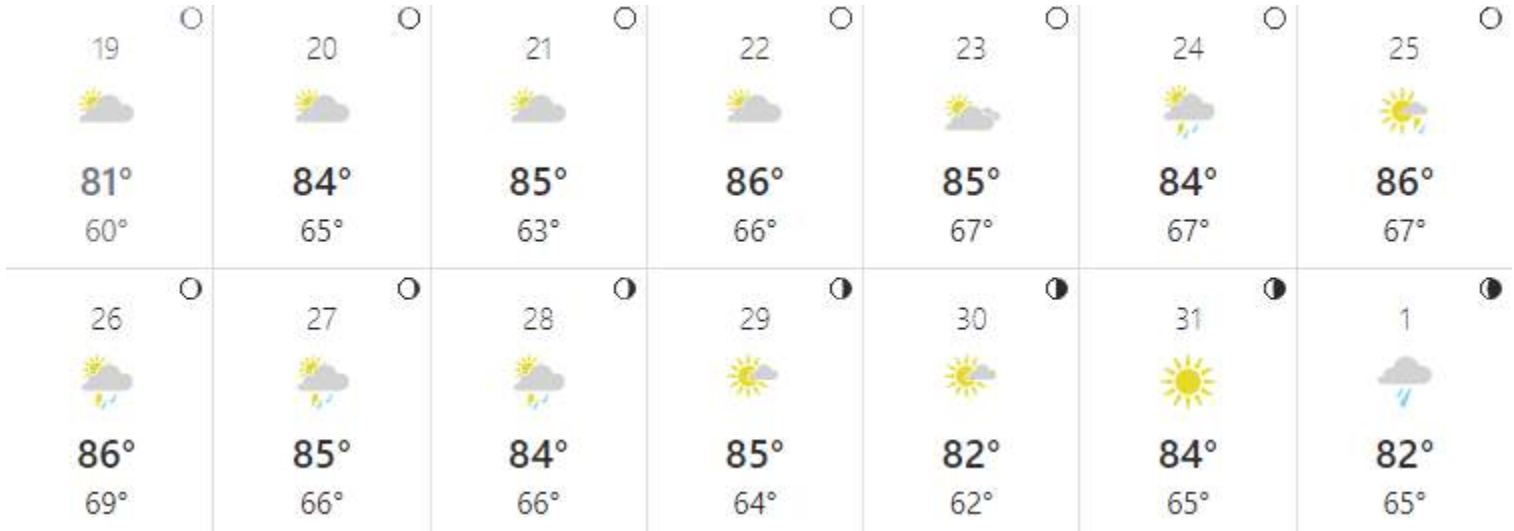

MANPOWER

MANPOWER GRAPH

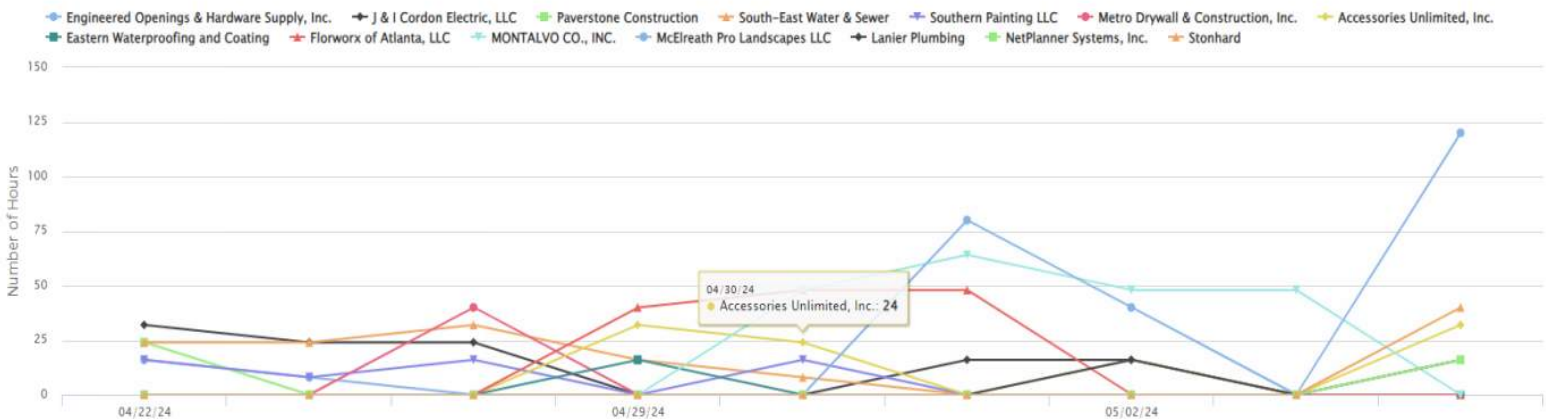

SAFETY REPORT

- Days without an accident: 285
- Days without lost time: 285

MILESTONE TRACKING

- Construction Start: April 10, 2023
- Current Contract Completion Date: June 10, 2024
