

# + CURRENT CONSTRUCTION ACTIVITIES

## LAST WEEK - WEEK ENDING 04/27/2024

---

### Level 3:

- Sheetrock/insulation installation
- Framing Soffit/Hard ceilings
- Screw Pattern Inspection per CoSS 4/24/24

### Level 2:

- Sheetrock/insulation installation
- Pulling Low Voltage wire for Fire Alarms

### Level 1:

- Low voltage R/I
- Installing glass curtain wall framing

### Basement:

- MEP O/H R/I
- Wall layout
- Demo existing 4" sprinkler pipe / installing new 6" main lines
- Installing glass curtain wall framing
- Interior Framing

### Exterior/Sallyport:

- Water Proofing exterior Sheathing
- Waterproofing @ RWB & Foundation wall & Sally Port
- Setting sequence 6 steel at Sally port addition/Installing 1<sup>st</sup> floor decking
- Installing screen wall steel & additional support steel @ Sally Port roof
- Site Grading / Back fill
- Begin brick Install @ North elevation
- Begin brick install @ Sally port
- Brick ledge repair/pour per RFI 107
- Coring Foundation wall for generator conduits
- Set MH B3 & Foundation drain

## THIS WEEK - WEEK ENDING 05/04/2024

### Roof:

- Set Roof Top Units via Crane 4/30/24

### Level 3:

- Sheetrock/insulation installation
- Framing Soffit/Hard ceilings

### Level 2:

- Sheetrock/insulation installation
- Framing Soffit/Hard ceilings

### Level 1:

- Low voltage R/I
- Pulling Low Voltage wire for Fire Alarms

### Basement:

- MEP O/H R/I
- Wall layout
- installing new 6" main sprinkler lines
- Interior Framing

### Exterior/Sallyport:

- Waterproofing @ Foundation wall & Sally Port
- Nelson stud install at elevated slab/ wire mesh install
- Elevated slab pour Thursday 5/2/24
- Site Grading / Back fill at RWB
- continue brick Install @ North elevation
- continue brick install @ Sally port
- U/G Sanitary @ Court Addition


### Site Engineering(Fulton County)

- Fusing bypass piping
- Relocate Bypass to allow MH rework

### Note/Delays:

- Elevated Slab Inspection by CoSS 4/29/24
- Moment Weld Inspection by XNDT 4/29/24

 JOBSITE PHOTOS

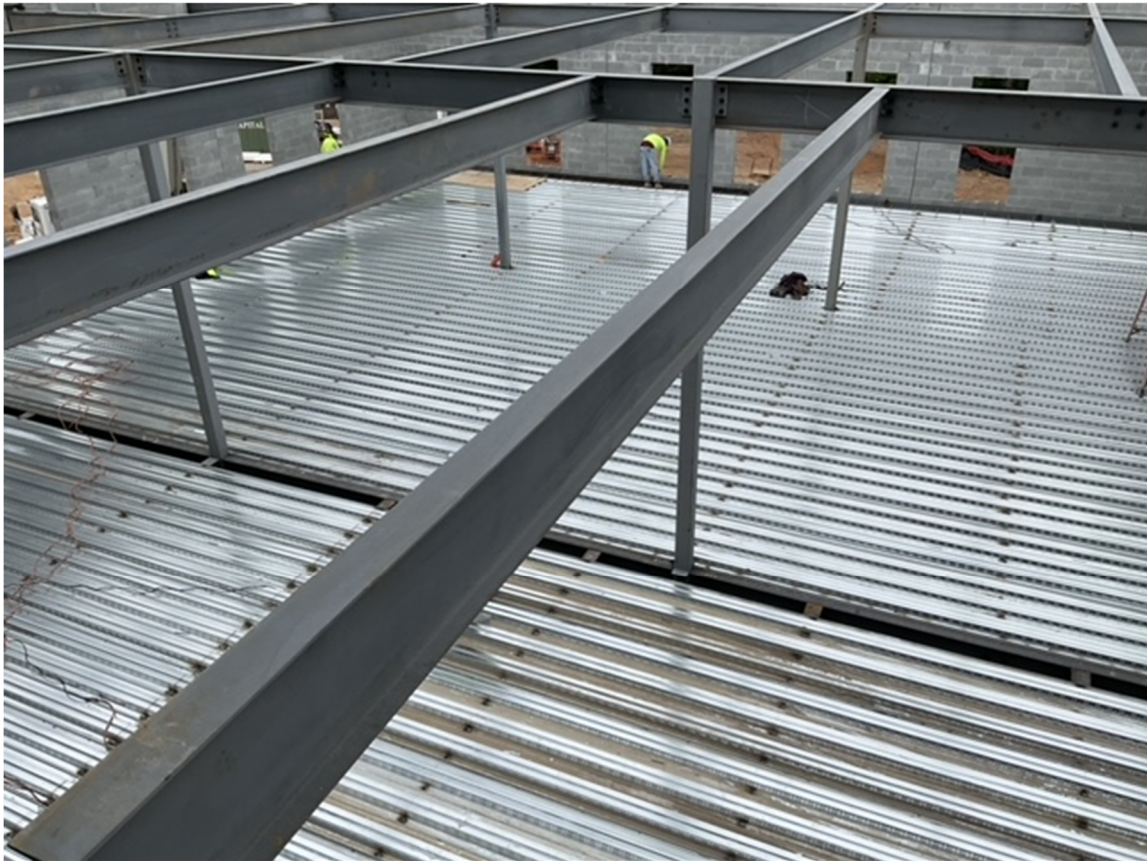

Setting Sequence 6 Steel At Sally Port Addition/Installing 1<sup>st</sup> Floor Decking



Interior Framing



Brick Install At Sally Port And Waterproofing



Brick Install At North Elevation



## Setting Rooftop Units



## Setting Rooftop Units



















Nelson Studs And Wire Mesh At Elevated Slab

 WEATHER

Weather delays this week: 0

21  58° 42°	22  68° 39°	23  74° 49°	24  75° 50°	25  80° 58°	26  79° 56°	27  75° 57°
28  79° 55°	29  78° 62°	30  76° 57°	1  85° 58°	2  86° 62°	3  82° 63°	4  77° 62°

- Total Weather Delays: 19

## SAFETY REPORT

- Days without an accident: 205
- Days without lost time: 205

## MILESTONE TRACKING

- Construction Start: August 21, 2023
- Current Contract Completion Date: Mar 14, 2025
