

CURRENT CONSTRUCTION ACTIVITIES

LAST WEEK

- Continued Installation of Landscaping
- Continued Installation of Site Fencing
- Completed Apparatus Bay Epoxy Flooring
- Completed Commissioning of Apparatus Bay Bi-fold Doors
- Completed Installation of Gym Athletic Flooring and Rubber Stair Treads
- Continued MEP Trim out at the First and Second Floors
- Completed Installation of Interior Door Hardware
- Began Rough Clean at First and Second Floors
- Completed Installation of Decon Equipment

THIS WEEK

- Continue Installation of Landscaping
- Complete Plumbing Final Inspection
- Continue West Net Alert System Device Installation
- Continue Electrical Trim out Throughout Building
- Continue GC Punch List Work at the First and Second Floors
- Complete Kitchen Cabinet Support
- Complete Installation of Additional Shiplap at Kitchen Island Trash Compartments

JOBSITE PHOTOS



Installation of Landscaping at Site Screen Wall



Installation of Decon Equipment



Installation of Kitchen Equipment


WEATHER

Weather delays last week: 0



MANPOWER

MANPOWER GRAPH

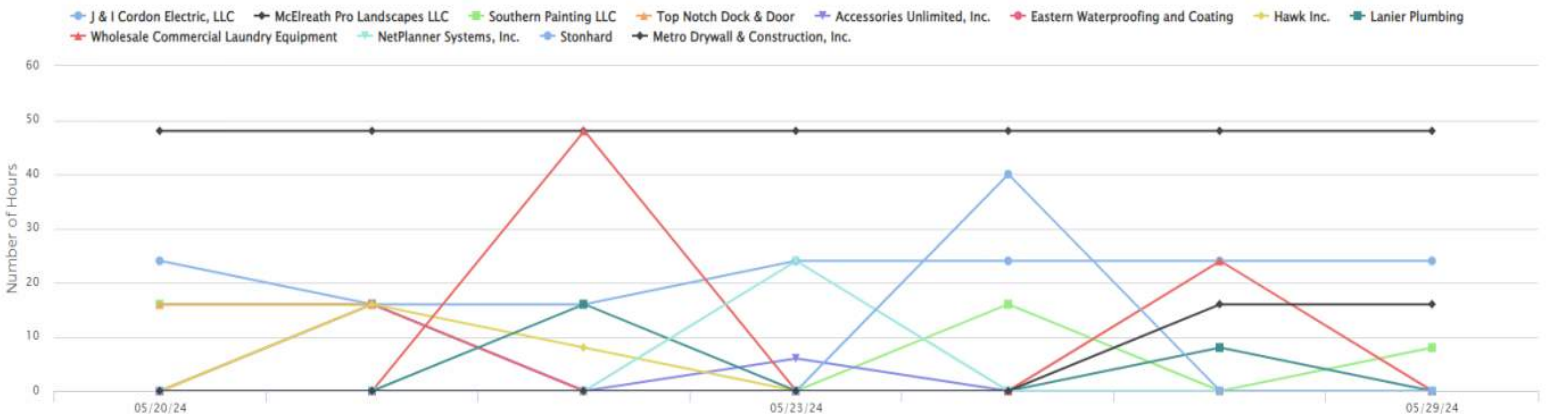

SAFETY REPORT

- Days without an accident: 290
- Days without lost time: 290

MILESTONE TRACKING

- Construction Start: April 10, 2023
- Current Contract Completion Date: June 10, 2024
