

# + CURRENT CONSTRUCTION ACTIVITIES

## LAST WEEK - WEEK ENDING 06/08//2024

### Roof:

- Condenser unit tie in

### Level 3:

- Paint (1<sup>st</sup> coat) primer continues/ begin 1<sup>st</sup> finish coat and exposed corridor ceilings

### Level 2:

- Framing Soffit/Hard ceilings
- Tape/Bed/Finishing drywall

### Level 1:

- Continue drywall/insulation installation
- Finish curtain wall glazing
- Fireproofing install
- U/G rough-in plumbing & electrical at court addition prior to slab pour

### Basement:

- MEP O/H & In wall R/I
- installing new Branch line/heads
- Finish curtain wall glazing

### Sallyport:

- MEP O/H & in wall R/I
- Interior Framing level 1
- Hair interceptor install @ kennel area
- Fireproofing install @ basement level

### Exterior:

- Rock Crusher Operations continue/ finish 6/7/24
- Slab prep/formwork, rebar, GAB, termite protection, moisture barrier
- Brick install @ North radius
- Fiber Cement siding continues
- Excavating E- line removing crushable material
- C14-C13 MH and pipe install prior to slab pour

## THIS WEEK - WEEK ENDING 06/15/2024

### Level 3:

- Continue 1<sup>st</sup> finish coat and exposed corridor ceilings
- Acoustic grid install begins following paint
- Hoist beam/ HD decking install at elevator cap

### Level 2:

- Framing Soffit/Hard ceilings
- Tape/Bed/Finishing drywall
- Begin primer 1<sup>st</sup> coat

### Level 1:

- Continue drywall/insulation installation
- U/G rough-in plumbing & electrical at court addition prior to slab pour
- Begin setting sequence 7 structural steel at court/admin addition

### Basement:

- MEP O/H & In wall R/I
- installing new sprinkler Branch line/heads
- Slab extension prep @ swat/ammo depot

### Sallyport:

- MEP O/H & in wall R/I
- Interior framing level 1
- Kennel area slab prep

### Exterior:

- Slab prep/ formwork, rebar, GAB, moisture barrier
- Slab pour for courtroom/ admin addition
- Fiber Cement siding continues/ mock up inspection
- Elevated sidewalk steel at public retrieval
- Bio Cell install
- Storm line install
- Oil/water separator install

### Note/Delays:

- R/I inspections at basement level scheduled for 6/14

## JOBSITE PHOTOS



Underground plumbing rough in




Primer/dry fall





Slab prep

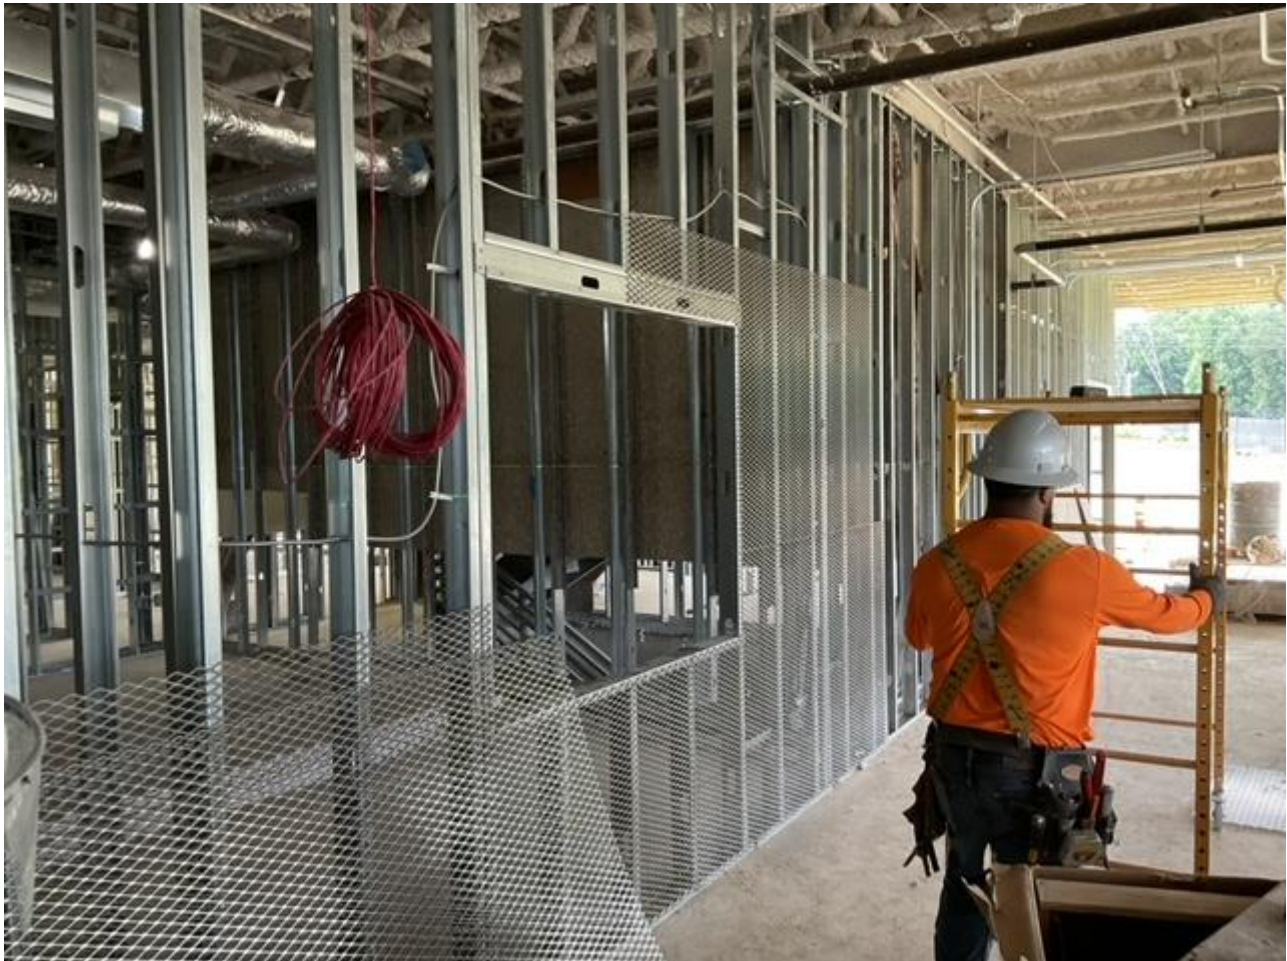

Interior framing/ security mesh





Slab pour

















Excavate/install Bio cell



 WEATHER

Weather delays this week: 0

2  85° 68°	3  87° 69°	4  84° 70°	5  85° 69°	6  85° 69°	7  89° 62°	8  89° 69°
9  93° 69°	10  85° 63°	11  87° 65°	12  90° 68°	13  91° 69°	14  95° 73°	15  97° 75°

- Total Weather Delays: 24

## SAFETY REPORT

- Days without an accident: 230
- Days without lost time: 230

## MILESTONE TRACKING

- Construction Start: August 21, 2023
- Current Contract Completion Date: Mar 14, 2025
