

# CURRENT CONSTRUCTION ACTIVITIES

## LAST WEEK - WEEK ENDING 06/22/2024

### Roof:

- Condenser unit tie in

### Level 3:

- Continue 1<sup>st</sup> finish coat and exposed corridor ceilings
- Acoustic grid install begins following paint
- Fire protection

### Level 2:

- Framing Soffit/Hard ceilings
- Tape/Bed/Finishing drywall

### Level 1:

- Continue drywall/insulation installation
- Drywall Tape/Bed/ Skim in progress

### Basement:

- MEP O/H & In wall R/I
- installing new sprinkler Branch line/heads
- Slab extension pour @ swat/ammo depot
- Fire protection

### Sallyport:

- MEP O/H & in wall R/I
- Interior framing level 1
- Kennel area slab pour

### Exterior:

- Fiber Cement siding continues
- Slab prep/ formwork, rebar, GAB, moisture barrier
- Elevated sidewalk steel at public retrieval
- Storm Line Install (E Line)
- Oil/Water separator install and connection

## THIS WEEK - WEEK ENDING 06/29/2024

### Level 3:

- Paint touch up walls & O/H
- ACT grid install continues
- Hoist beam/ HD decking install at elevator cap
- HVAC Grille/ Diffuser installation
- Permanent lighting & O/H signage install
- Fire protection
- Cable tray install

### Level 2:

- Framing Soffit/Hard ceilings
- Tape/Bed/Finishing drywall
- Start ACT grid 6/28
- Prime paint complete touch up in progress 1<sup>st</sup> coat starts 6/27

### Level 1:

- Continue drywall/insulation installation
- Security Mesh and High impact wall installation
- Tape/Bed/ Skim
- Detention area fire protection
- Erecting sequence 7 structural steel at court/admin addition

### Basement:

- MEP O/H & In wall R/I
- installing new sprinkler Branch line/heads
- Poured shower area concrete, Electrical trenches, elevated sidewalk and canopy footings on 6/26
- PRV station complete
- Fire Protection

### Sallyport:

- MEP O/H & in wall R/I
- Grates for trench drains completed

### Exterior:

- Fiber Cement siding continues/ Mockup inspection
- Grading-F/R/P retaining wall B footings pending Jericho response
- Pressure washing/acid cleaning brick facade complete
- CGI installing last remaining glass on 3<sup>rd</sup> floor on 6/26
- Continue Caulking on all exterior windows
- Fire line


### Note/Delays:

- Fulton County is back onsite lining the sewer across the golf course. They will be back on our site next week replacing manhole 1.1
- Tracking Topping out event on 7/8 at 11am

 JOBSITE PHOTOS



Diffuser and light install

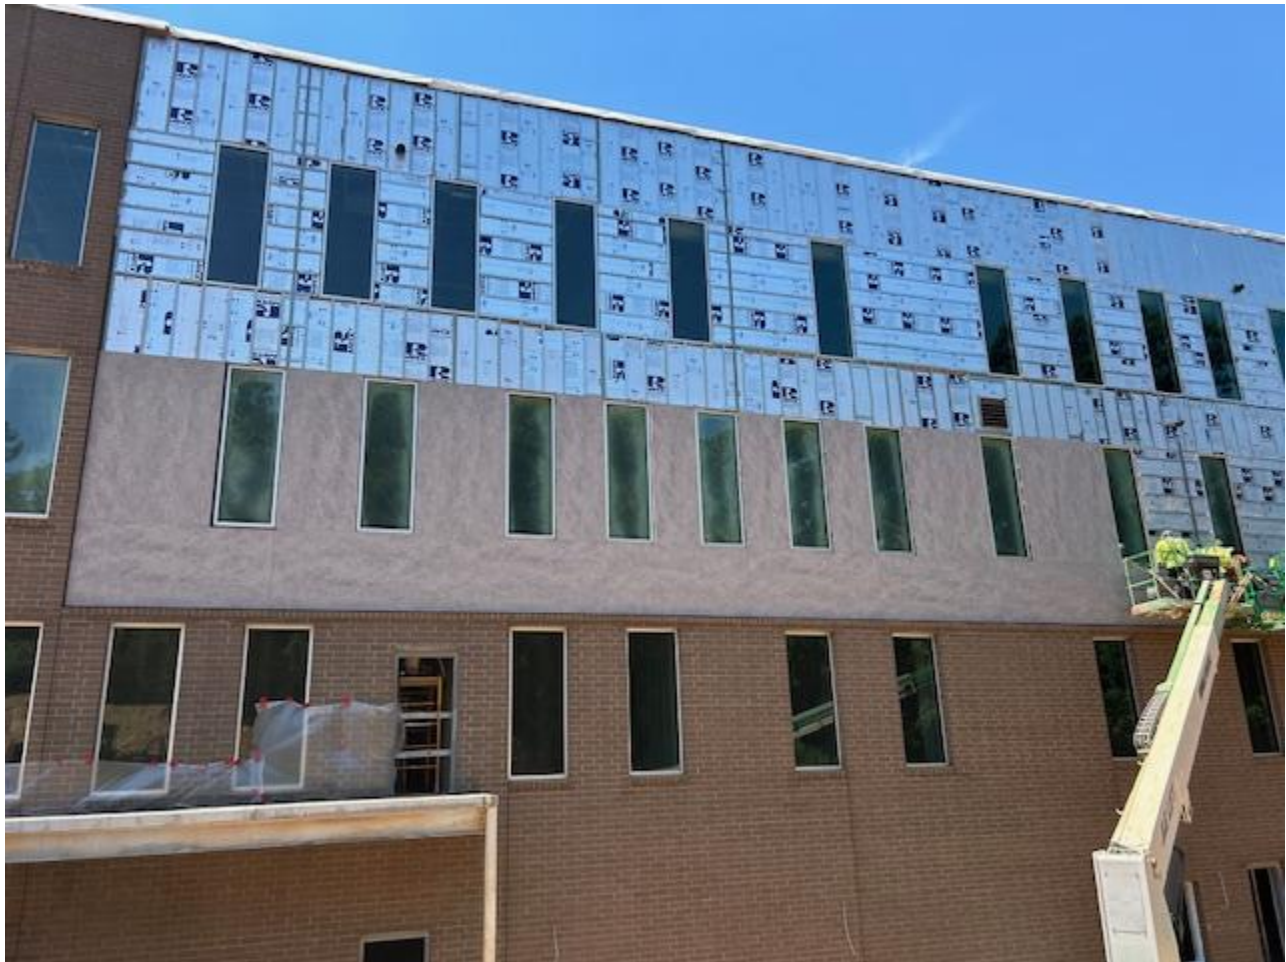

Fiber Cement Siding Continues



Pouring of canopy footings



Pouring of Elevated sidewalk



Steel Install

















1<sup>st</sup> Finish Coat



 WEATHER

Weather delays this week: 0

16  96° 73°	17  93° 72°	18  90° 70°	19  88° 72°	20  91° 69°	21  94° 72°	22  96° 77°
23  97° 70°	24  97° 67°	25  98° 73°	26  99° 73°	27  86° 72°	28  90° 74°	29  89° 75°

- Total Weather Delays: 24

## SAFETY REPORT

- Days without an accident: 240
- Days without lost time: 240

## MILESTONE TRACKING

- Construction Start: August 21, 2023
- Current Contract Completion Date: Mar 14, 2025
