

CURRENT CONSTRUCTION ACTIVITIES

LAST WEEK - WEEK ENDING 07/06/2024

Level 3:

- Cable Tray Install
- F/A device install
- Fire protection lines & Heads
- Perm lighting install
- ACT grid install
-
- Grills & Diffusers install

Level 2:

- Paint at door frames and exposed corridors
- Fire protection lines & Heads

Level 1:

- Fire protection lines & heads
- Drywall/Insulation/ security mesh install
- Drywall finishing
- Mini split units installed

Basement:

- Drywall/Insulation/ security mesh install
- Fire protection lines & heads

Exterior:

- Storm/drainage piping & structures installed in courtyard
- Fireline install completed
- Fiber cement siding install continues at North Elevation
- Backer rod and caulk install at exterior of window frames
- Sequence 7 steel/roof decking install continues at courtroom addition

THIS WEEK - WEEK ENDING 07/13/2024

Roof:

- Mini split unit disconnects install
- Gas line tie in to RTU's
- Condensate drains install

Level 3:

- F/A device install
- Fire protection lines & heads
- Perm lighting install
- Caulking at ACT grid
- Grills & Diffusers/slot diffusers install

Level 2:

- ACT grid install
- Paint touch up
- Cable tray install
- F/A device install
- Fire protection lines & heads

Level 1:

- Fire protection lines & heads
- Drywall/Insulation/security mesh install
- Drywall Finishing
- O/H 6" roof drainpipe install at Sally Port
- Paint/Primer begins

Basement:

- Shower valve R/I
- Begin Hydrostatic testing plumbing lines
- Fire protection lines & heads
- Drywall/Insulation/ Security mesh install
- Waterproofing at penetration for exterior conduits/ water line

Sallyport:

- MEP O/H & in wall R/I
- Grates for trench drains completed

Exterior:

- Sequence 7 steel/roof decking install continues at courtroom addition
- Grading for curb & gutter
- Storm/drainage piping & structures installed in courtyard
- Fiber cement siding install continues at North Elevation
- Curb & Cutter F/R/P begins 7/11


Note/Delays:

- Universal equipment services on site 7/3 to remove remainder diesel from old generator
- Generator to be removed 7/17
- SSPHQ jobsite received approximately 2.5" of rain over the weekend causing site conditions to be very wet and muddy. This required remedial site work to be completed resulting in lost time for the site Civil Subcontractor.
- Tracking Topping Out party for 7/15

 JOBSITE PHOTOS



Sequence 7 steel

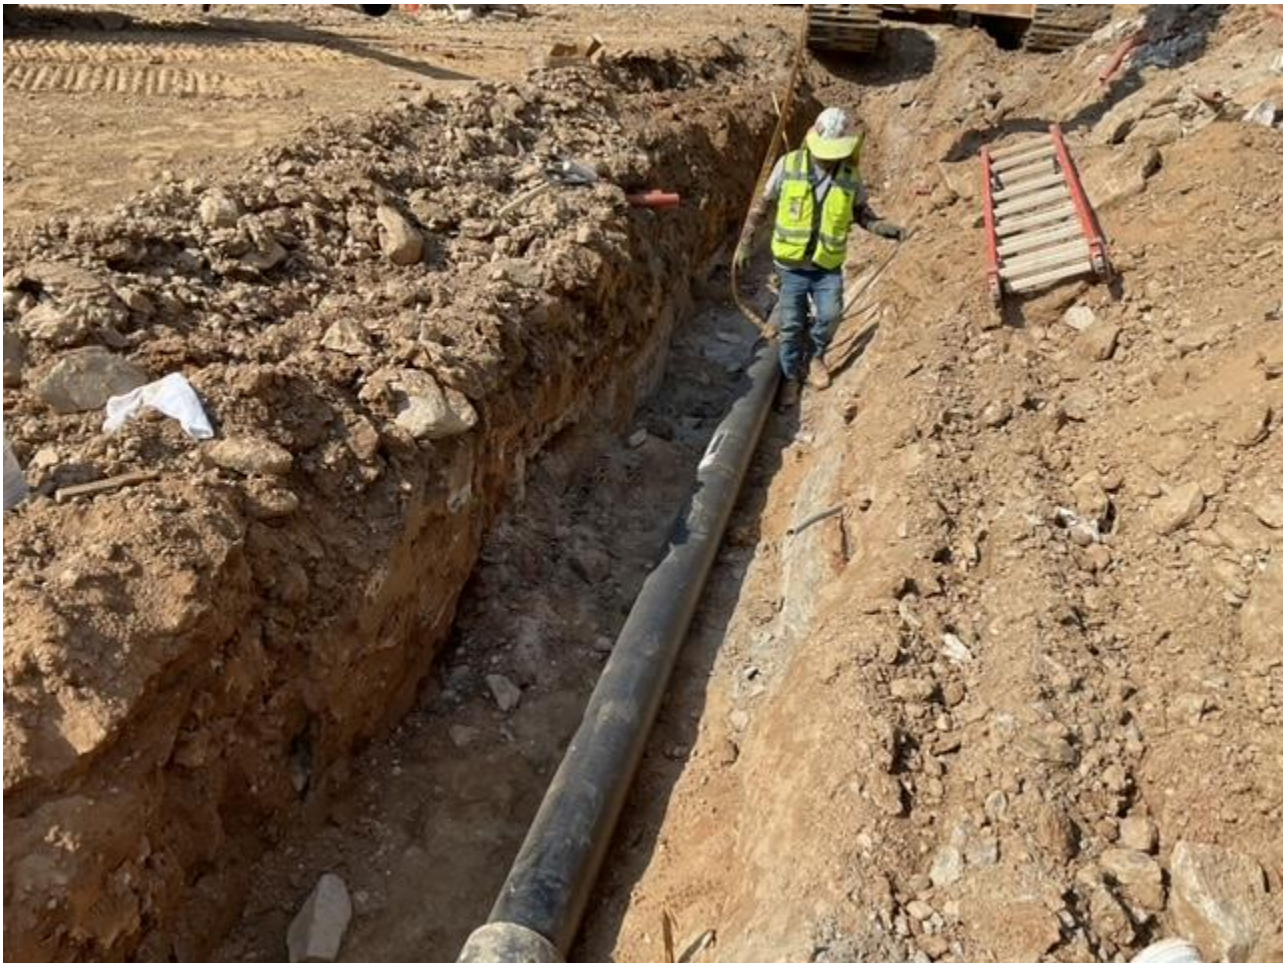


Fire line install



Fiber cement siding install



Cable Tray install

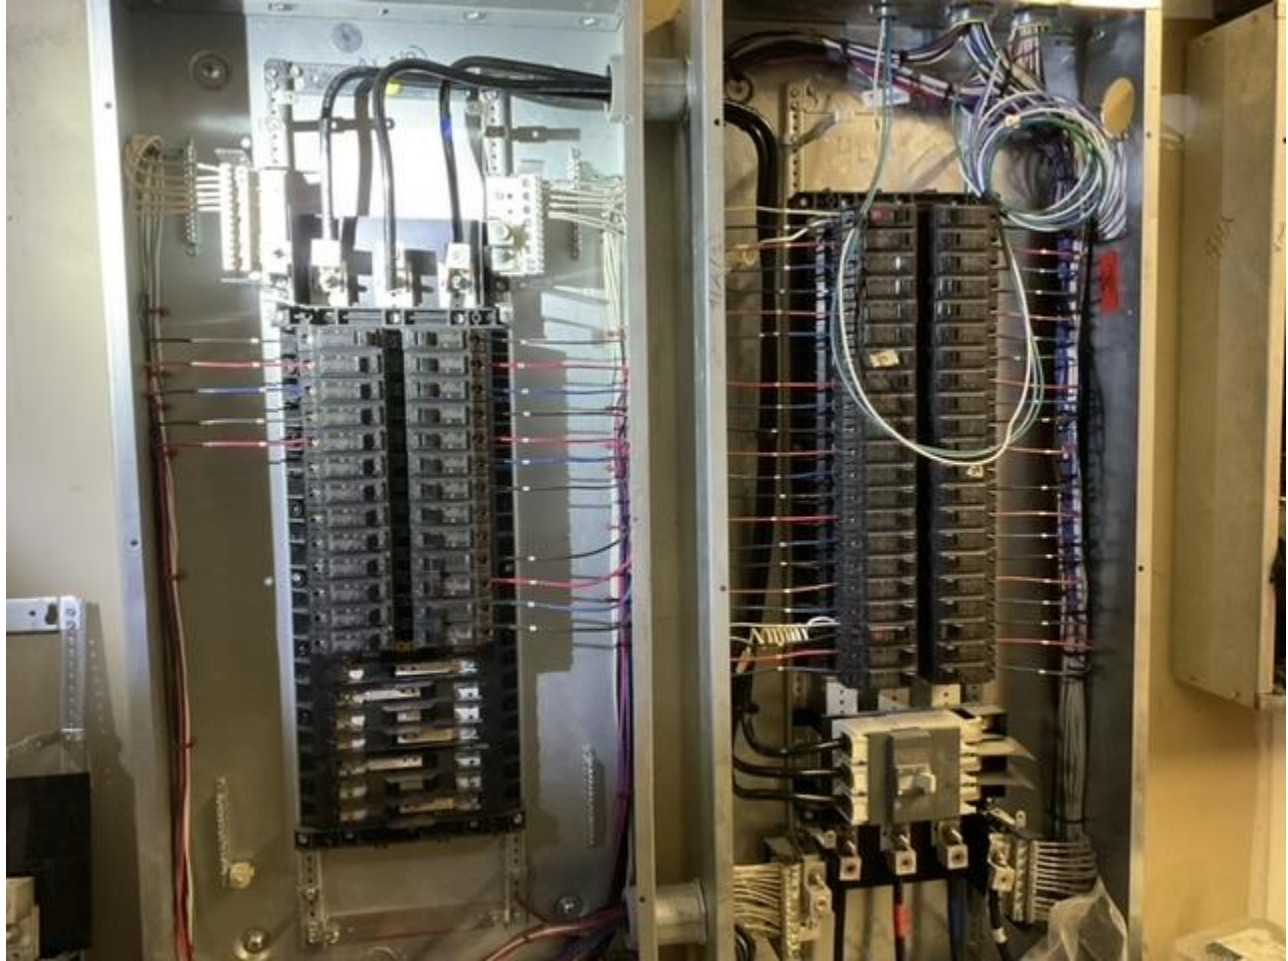















Electrical Panel



Mini Split Unit Install

 WEATHER

Weather delays this week: 1

SUN	MON	TUE	WED	THU	FRI	SAT
30  97° 77°	1  97° 76°	2  92° 75°	3  93° 75°	4  96° 75°	5  91° 75°	6  93° 73°
7  92° 70°	8  92° 74°	9  91° 75°	10  88° 69°	11  91° 72°	12  93° 73°	13  94° 74°

- Total Weather Delays: 25

SAFETY REPORT

- Days without an accident: 245
- Days without lost time: 245

MILESTONE TRACKING

- Construction Start: August 21, 2023
- Current Contract Completion Date: Mar 14, 2025
